


THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.


REBAR TAKEOFF (BOTTOM LAYER)

BAR	SIZE	LENGTH	QTY	SHAPE
B1	#5	20 in (1'-8")	4 pcs	STR
B2	#5	21 in (1'-9")	8 pcs	STR
B3	#5	25 in (2'-1")	8 pcs	STR
B4	#5	58 in (4'-10")	4 pcs	STR
B5	#5	48 in (4'-0")	4 pcs	STR
B6	#5	32 in (2'-8")	4 pcs	STR
B7	#5	62 in (5'-2")	4 pcs	STR
B8	#5	24 in (2'-0")	4 pcs	DIAG
B9	#5	Ø68 in (5'-8")	1 pcs	CIRC

Total Pieces: 41 Pcs
Total Footage: 130.35 LF
Total Weight: 135.96 lbs (0.068 Tons)
12" REBAR OVERLAP FOR CIRCULAR REINFORCEMENT

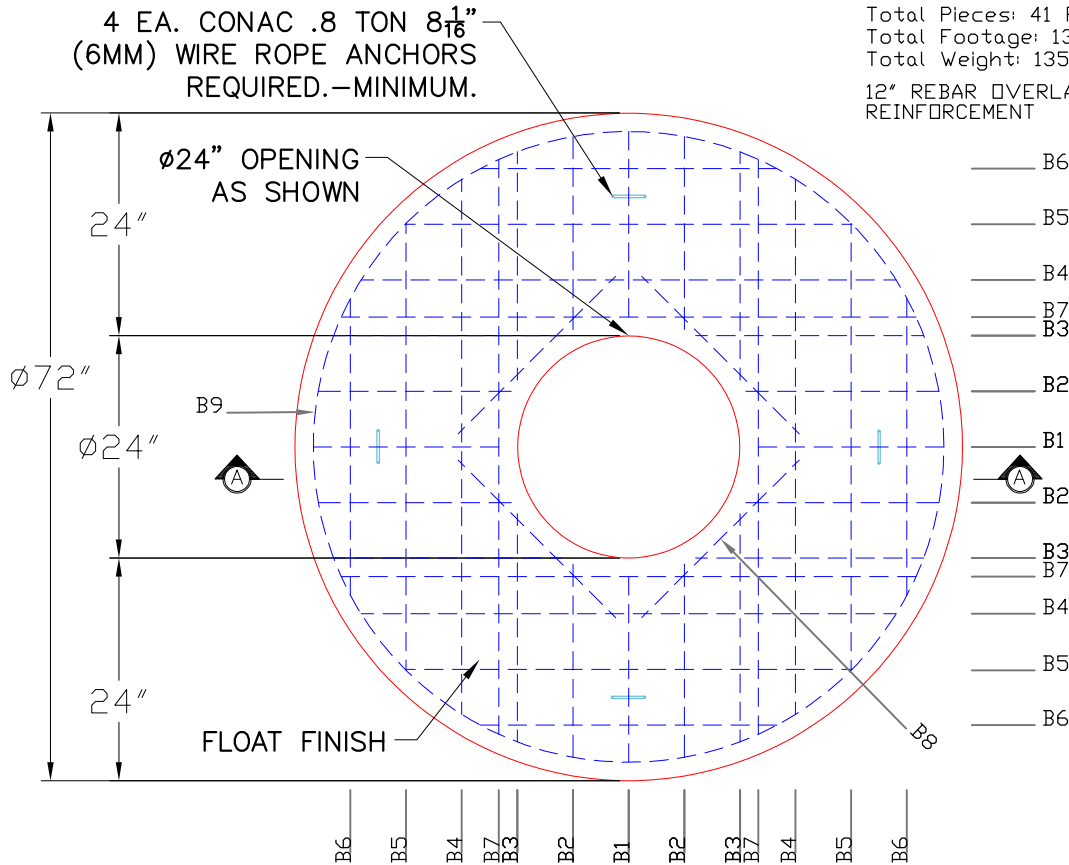

TOP VIEW

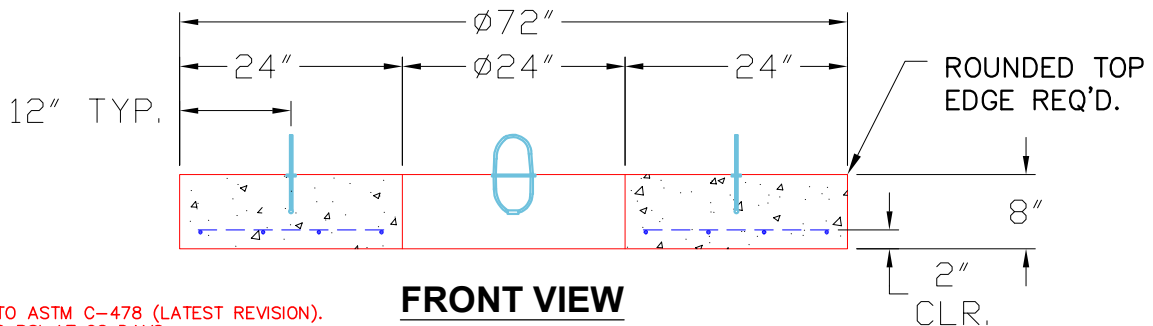

FRONT VIEW

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 5,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C.E.W. (GRADE 60).

PRODUCTION WORK ORDER

PRODUCT I.D.:
MH060LD08CC

DESCRIPTION: 60"Ø X 8" MH TOP SLAB
W/ Ø24" CONCENTRIC OPENING



QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ HOLE LOCATION CORRECT.
- ☐ REINFORCING CORRECT.
- ☐ FINISH ON SLAB SURFACE UNIFORM.
- ☐ OUTSIDE TOP EDGE TROWELLED.
- ☐ FLAT BOTTOM.

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 2,429 LBS.

TOP SECTION JOINT: FLAT

BASE SECTION JOINT: FLAT

QC CHECK INITIALS:

CUSTOMER: ADS ADVANCED DRAINAGE SYSTEMS, INC.

PROJECT: ADS DAVIS JEWELERS

STRUCTURE: 2

QUOTE/SALES ORDER NO: 26-3772

PC: M. SULLIVAN

DRAWING: S. FELLETTTER

DATE: 10/09/26

SCALE: NTS

PG. 1 of 1
