

Contractor: Contech Engineering Solutions

TECH: S. Felleter

Plant: Beaver Dam



Size: 48"

Rim to Invert: 3.87'

Floor Height: 6"

Slack: 0.44"

CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 48" - Conseal CS-102 1.00"
2) Hole - 20
1) Hole - 12

0 lb
1413 lb
4083 lb
2588 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 8084 lb


Invert: 1
Degree: 270°

Invert: 3
Degree: 18°

48" - MH BASE T/n - 18" - (P1)

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	639.63'							
Reducer								
Invert 1	635.76'	270°	15" HDPE	17.6"	20"	Hole 20	26.25"	P2
Invert 2	635.86'	123°	15" HDPE	17.6"	20"	Hole 20	27.45"	P2
Invert 3	635.86'	18°	6" HDPE	6.9"	12"	Hole 12	26.95"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

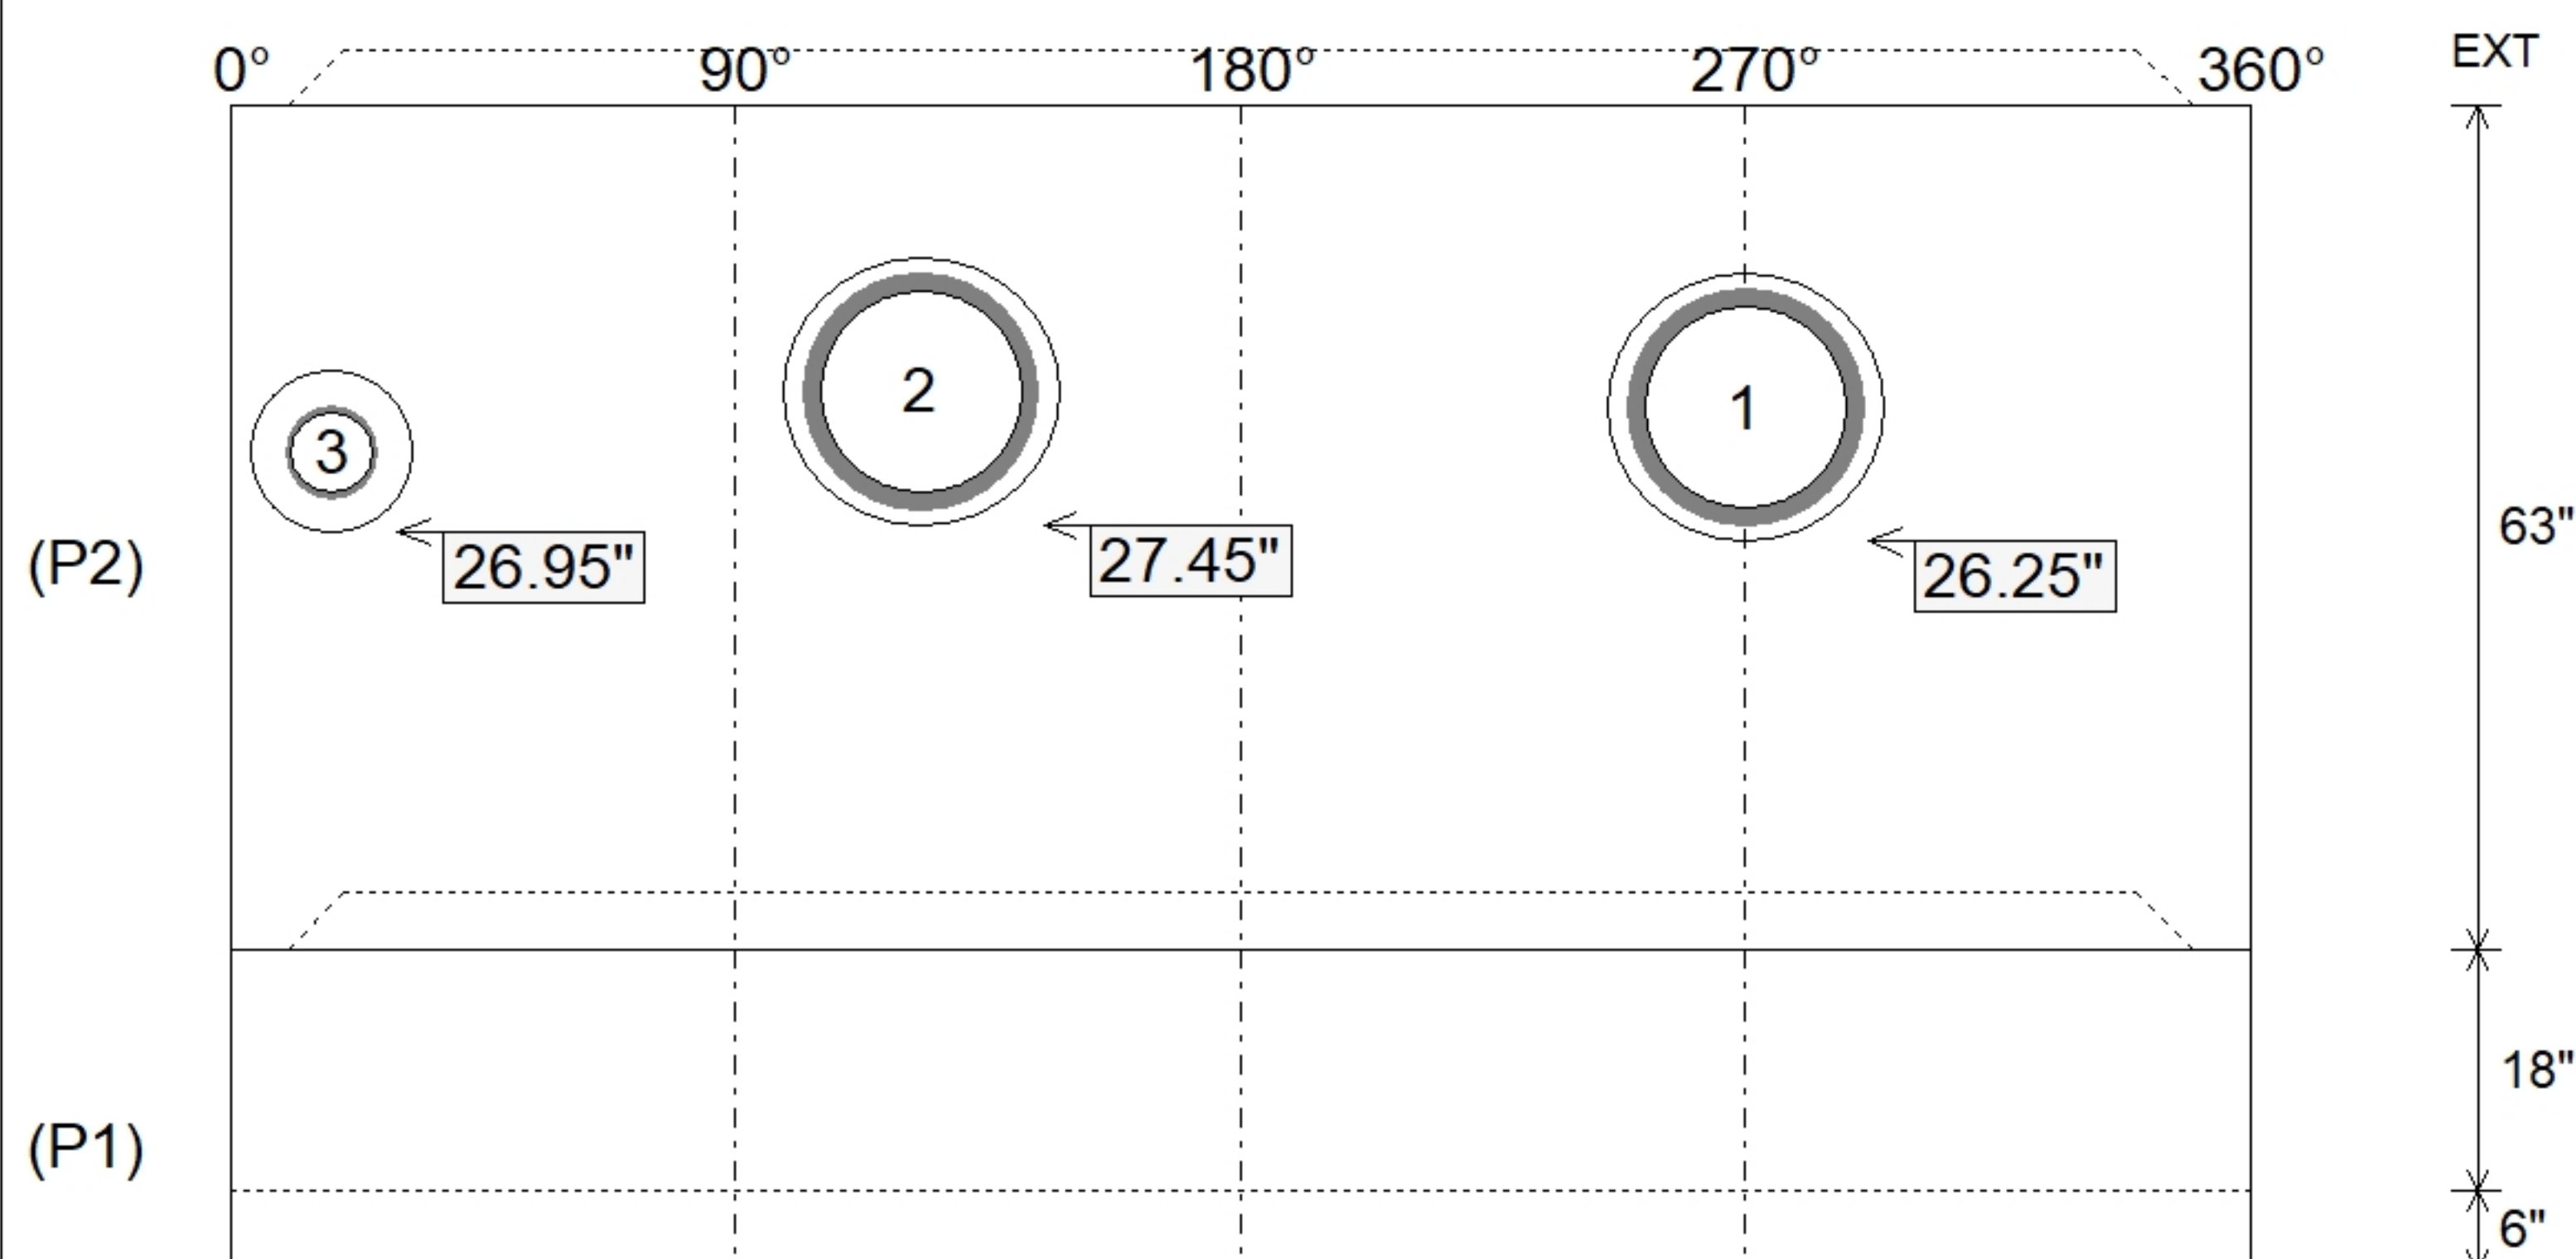

Submittal Drawing
9/29/2026 1:17:05 PM

SUBMITTAL
APPROVED BY:
