

Job Name: 26-3807 ADS North Oldham HS

Job Location: Goshen, KY

Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam

10/9/2026 12:58:47 PM

Tech: S. Felletter

PC: M. Sullivan



Structure ID: DS-1

P3 MH036RSVF

MH RISER Custom Ht T/G

P5) 24" - CASTING HEIGHT - 7"

P4) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/G - 10"

P3) 36" - MH RISER Custom Ht T/G - 20"

P2) 36" - MH RISER T/G - 72"

P1) 36" - MH BASE T/n - 18"

1) ASSEMBLY REQUIRED

1) CASTING - HOE MC-375 F/C Storm

3) 36" - Conseal CS-102 1.00"

1) 24" - Conseal CS-102 1.00"

1) Hole - 20

1) Hole - 16

0 lb

896 lb

844 lb

2857 lb

1525 lb

0 lb

271 lb

0 lb

0 lb

0 lb

0 lb

6392 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY ICAST (HOE MC-375 F/C "STORM").

4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE.

.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 652.5'

Rim to Invert: 6.05'

Slack: 0.56"

Sump: 54.96"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

(P5)


(P4)

(P3) <<


(P2)

(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

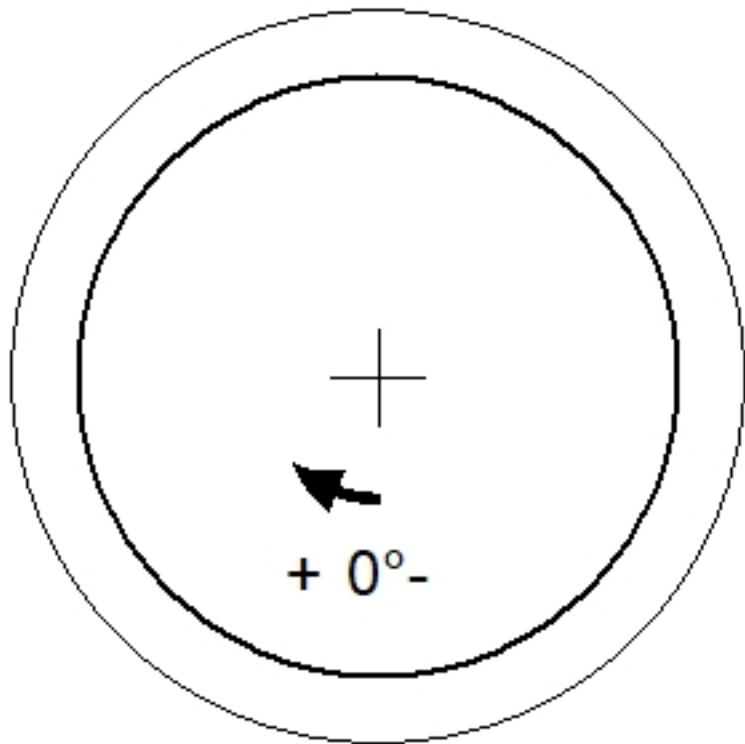

INSIDE WALL DIMENSIONS

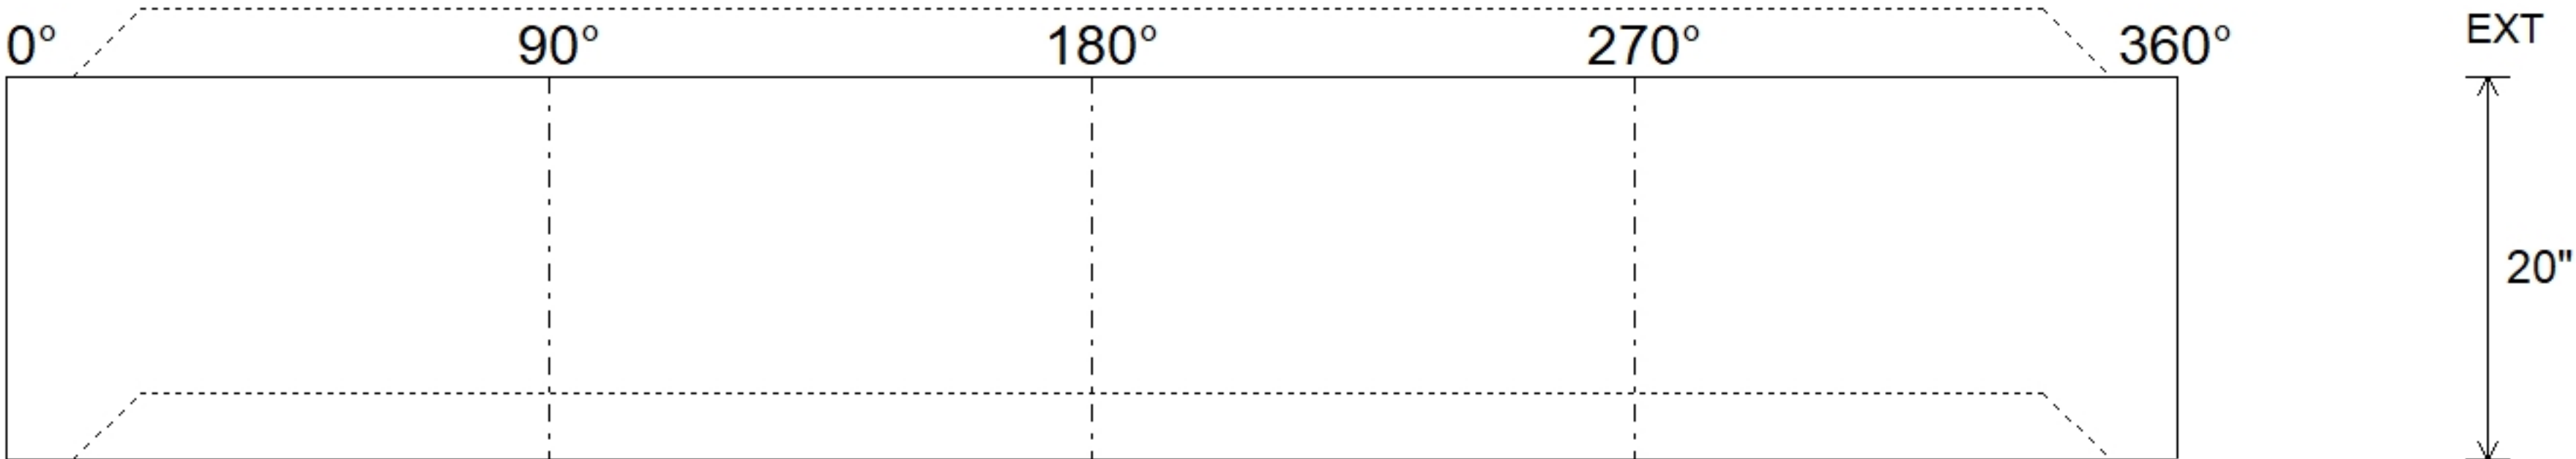

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 4"

Floor Height: 0"

Height (Int): 20"

Height (Ext): 20"

Weight (Net): 844 lb

Volume (Net): 0.22cu.yd
