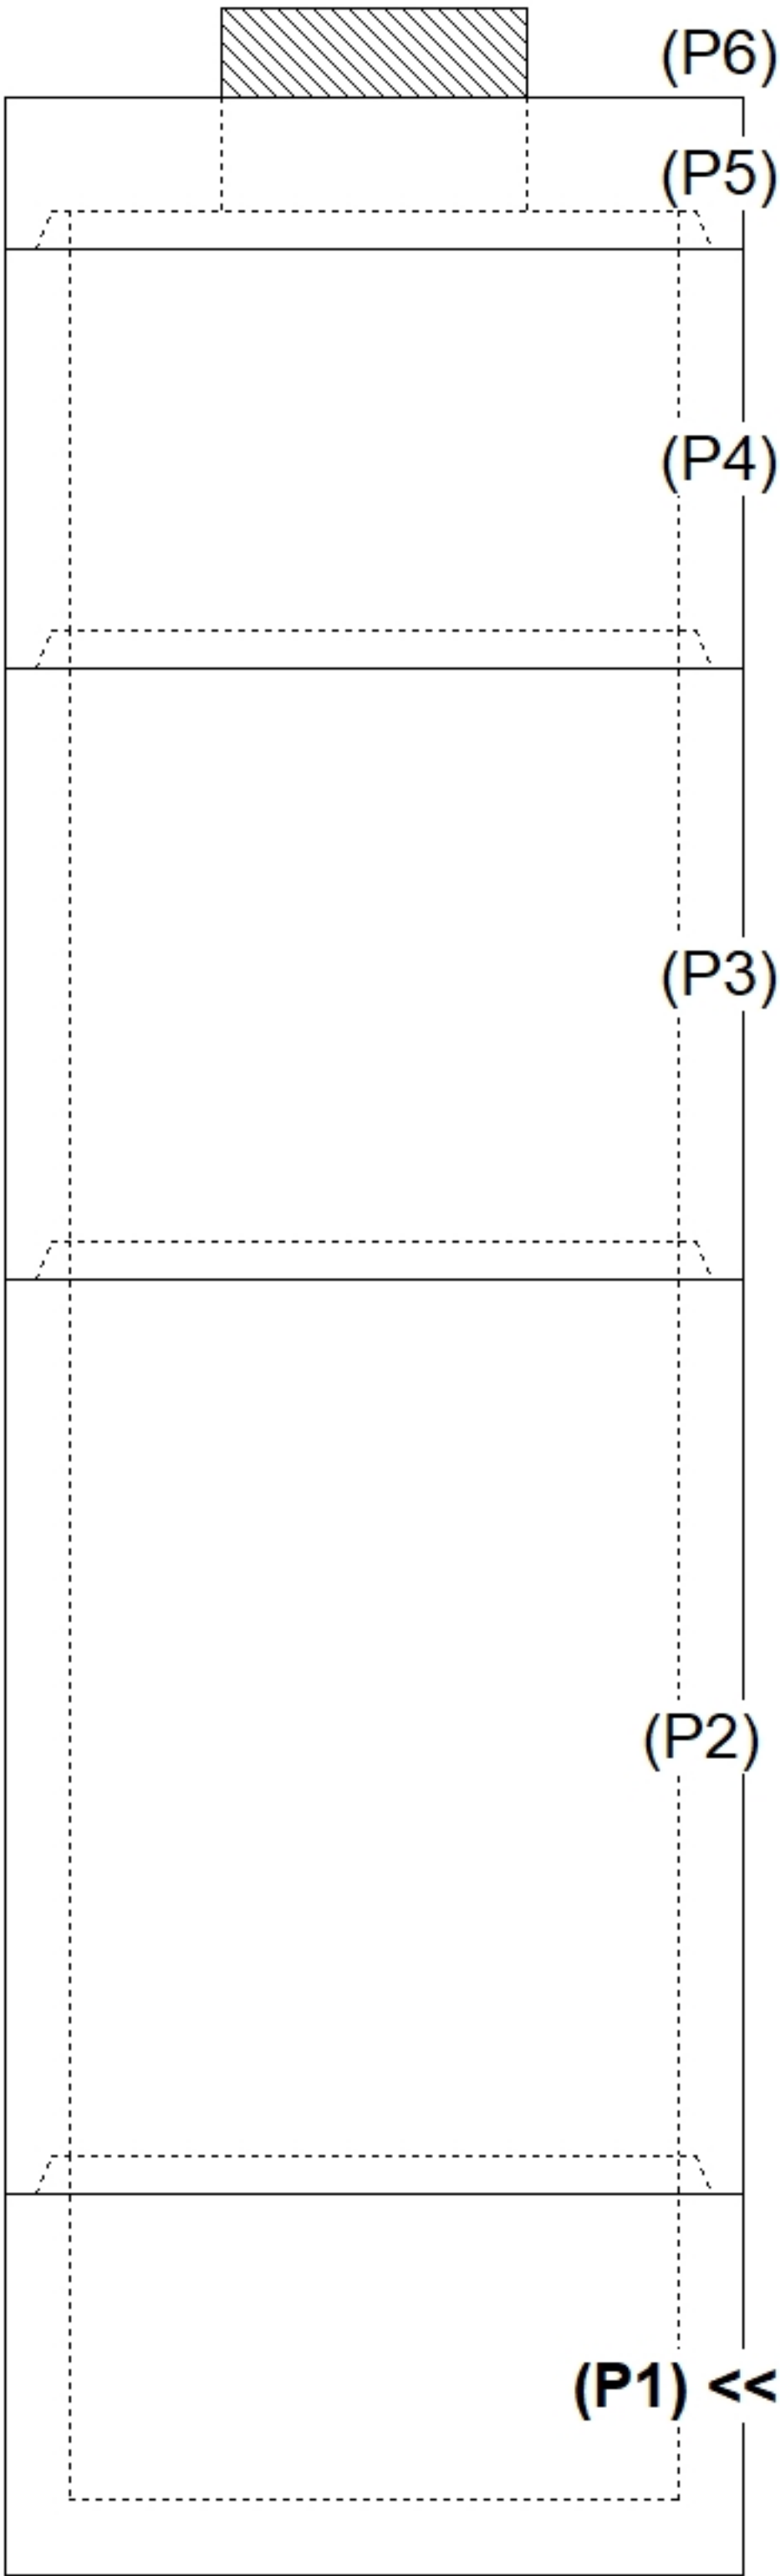
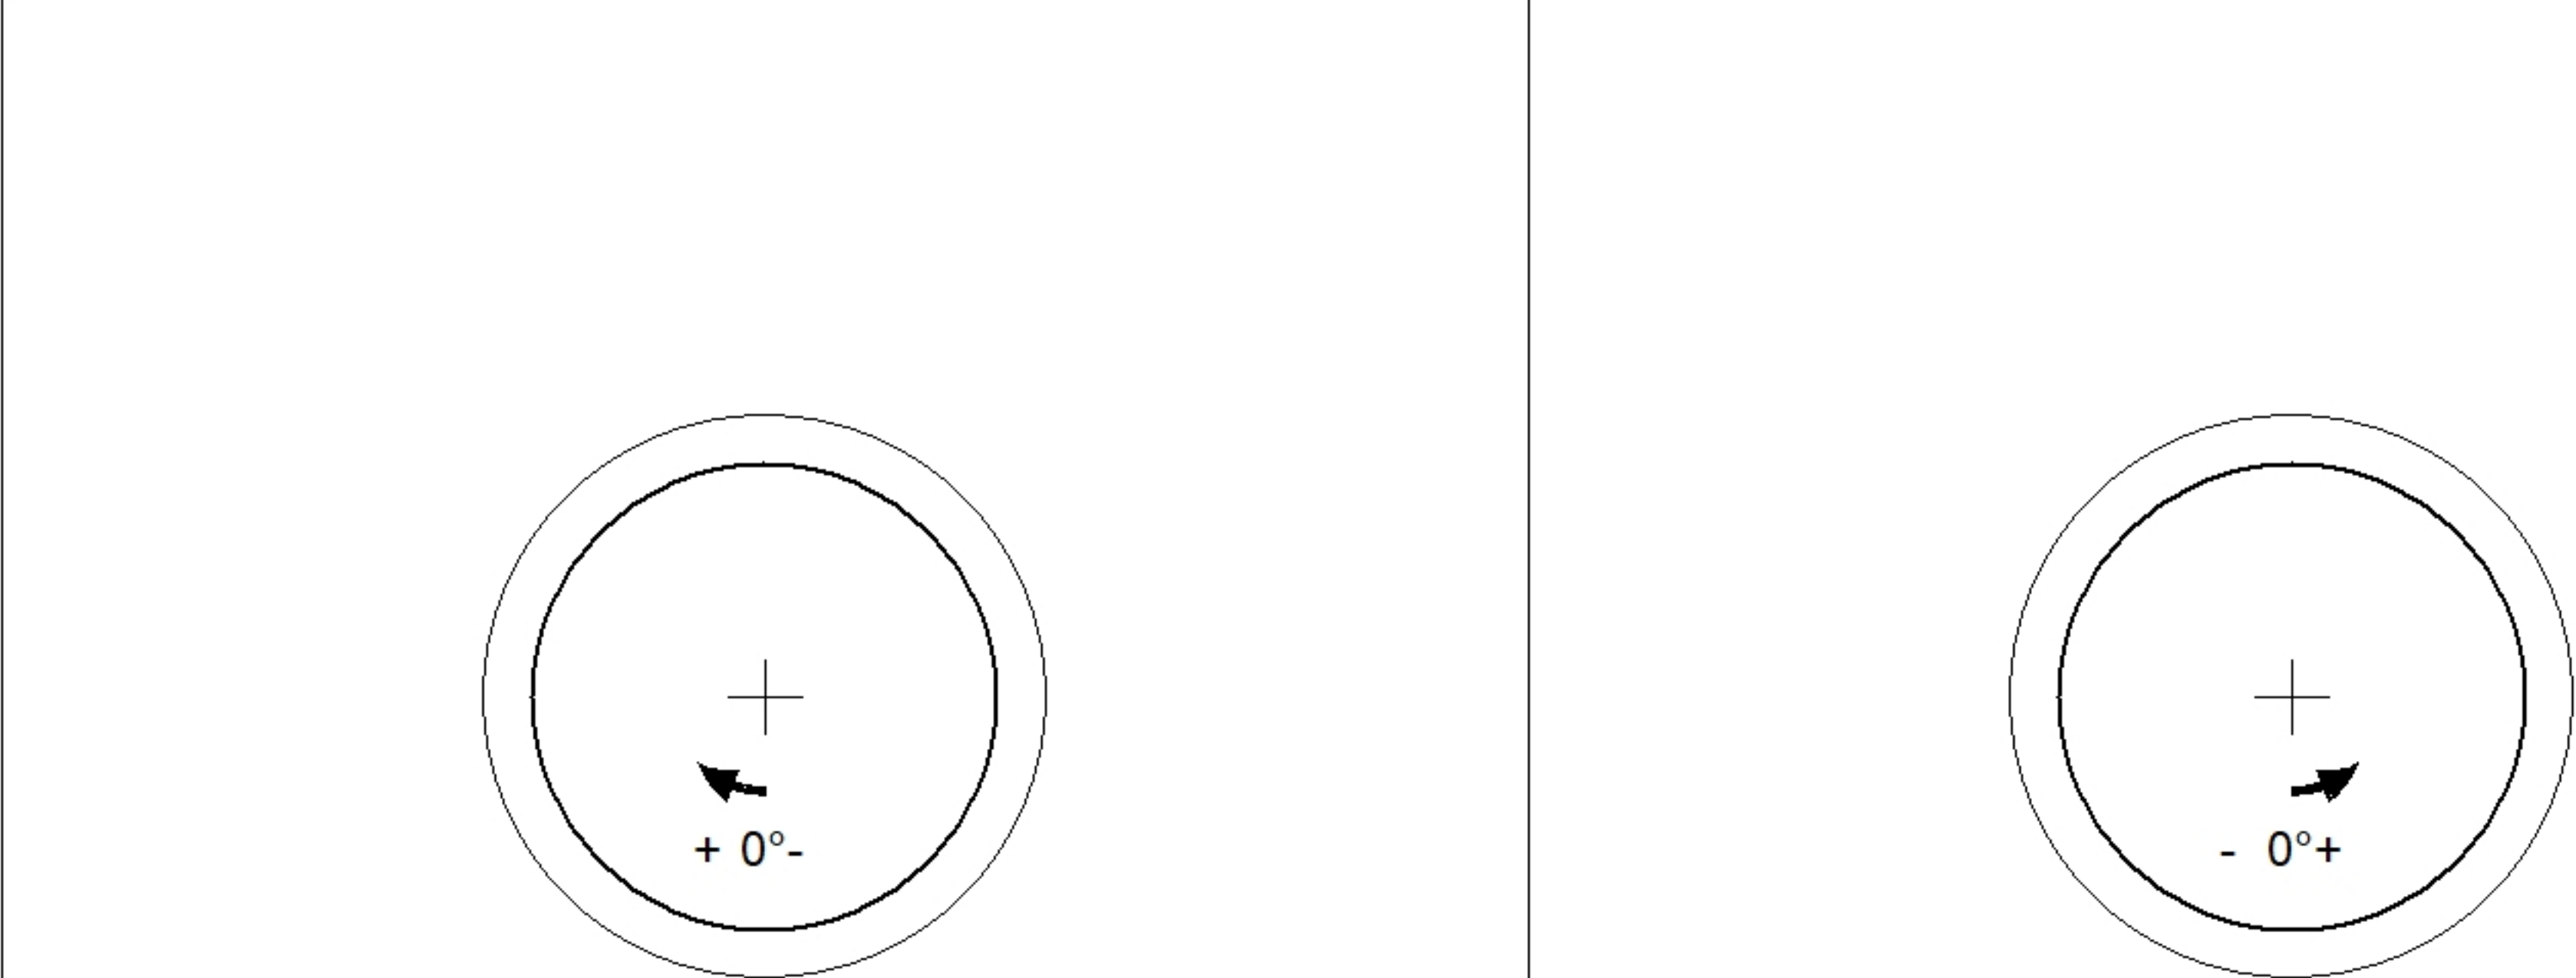
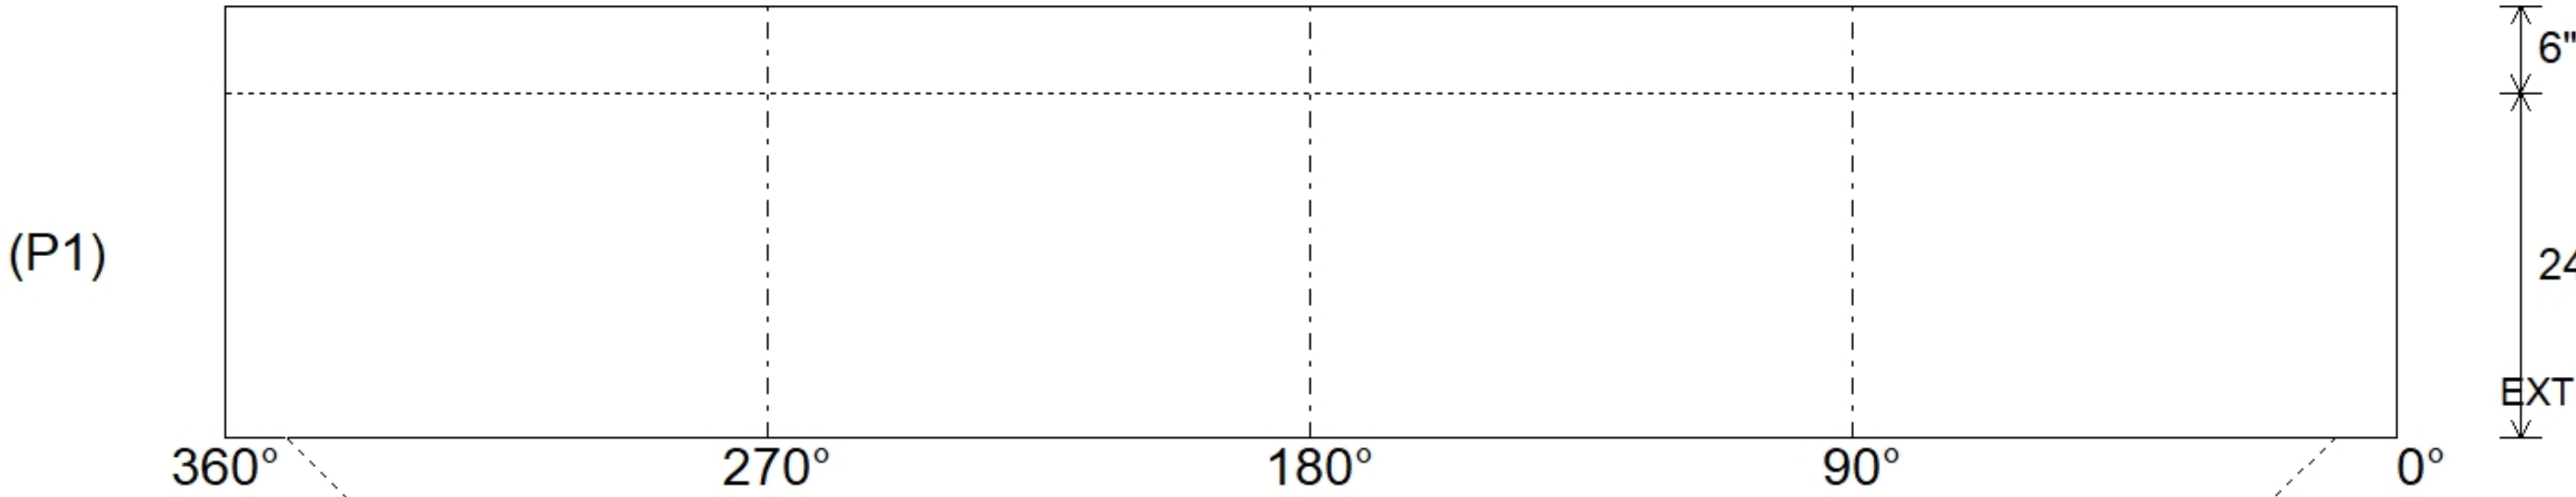


Job Name: 26-3823 ADS Pulte Hayes Avenue Job Location: Louisville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 10/7/2026 3:44:22 PM		Tech: S. Felletter PC: M. Sullivan						
Structure ID: WQU-2													
P1		MH048BA24			MH BASE T/n								
P6) 24" - CASTING HEIGHT - 7" P5) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P4) 48" - MH RISER Custom Ht T/G - 33" P3) 48" - MH RISER SPECIAL T/G - 48" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ASSEMBLY REQUIRED 1) CASTING - HOE MC-375 F/C Storm 4) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 16					0 lb 1580 lb 2305 lb 3353 lb 4858 lb 3007 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					Structure Total: 15375 lb	
Rim: 695.92'		Rim to Invert: 9.64'		Slack: 0.68"		Sump: 81"		Step Position: 0°					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌵)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 24" Height (Ext): 30"		Weight (Net): 3007 lb Volume (Net): 0.77cu.yd				
