




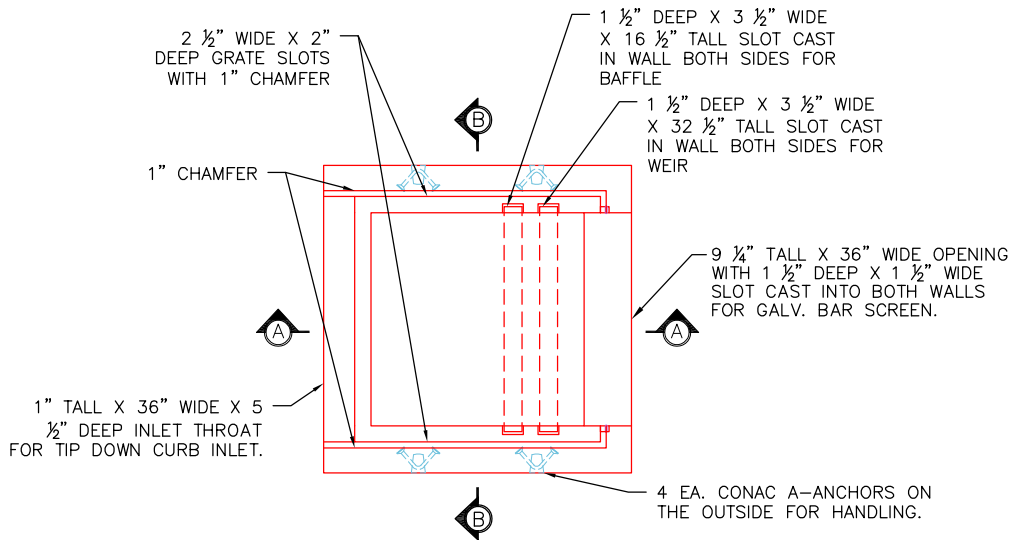

PLAN VIEW

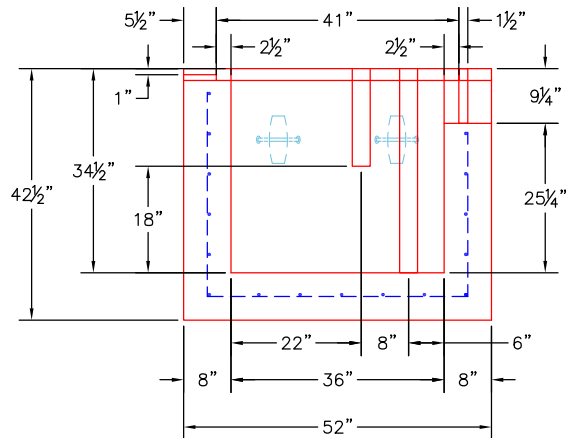

SECTION A-A

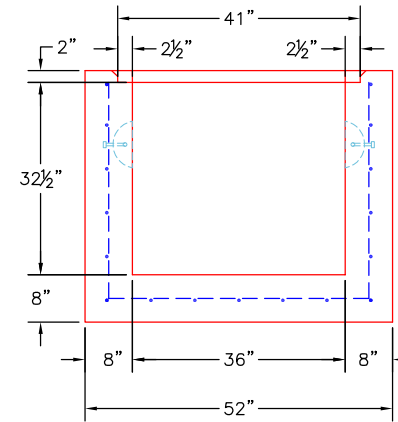

SECTION B-B

GENERAL NOTES:

1. MANUFACTURED PER ASTM C-913 (LATEST REVISION).
2. CONCRETE : 5,000 PSI AT 28 DAYS.
3. REINFORCING: PER ASTM 615 (GRADE 60).
 - TOP SLAB (As. 62) #5 BAR @ 6" C.C.E.W.
 - WALLS/FLOOR (As. 12) #5 BAR @ 12" C.C.E.W.
4. WEIGHTS: TOTAL = 4,305 LBS
 - BASE = 3,924 LBS.
 - WEIR = 241 LBS
 - BAFFLE = 140 LBS
5. 41" X 41" X 1.25" GALV. BAR GRATE BY ICAST.
6. 1.25" X 7" X 39" GALV. BAR SCREEN BY ICAST.
7. VERIFY ALL ASPECTS OF DESIGN.

REVISIONS



SUBMITTAL DRAWING: 36" X 36" PRETX LT		
CUSTOMER: CONVERGENT WATER TECHNOLOGIES		
PROJECT: GALLATIN PRETX		
STRUCTURE ID.:		
QUOTE/SALES ORDER NO: 26-3904		
PC C. GOFF	DRAWN BY: J. HORSLEY	
DATE: 10/7/26	SCALE: NTS	PG. 1 of 1
