

Job Name: 26-3958 908730 Summit View Farms 6th Plat
Job Location: Lees Summit, MO
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

10/14/2026 12:22:37 PM

Tech: S. Felletter

PC: C. Goff



Structure ID: 10-CS-6

P3 MH072RSVF

MH RISER Custom Ht T/G

P5) 30" - CASTING HEIGHT - 4"
P4) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15"
P3) 72" - MH RISER Custom Ht T/G - 68"
P2) 72" - MH RISER SPECIAL T/G - 24"
P1) 72" - MH BASE T/n - 24"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
3) 72" - Conseal CS-102 1.00"
2) Hole - 32

0 lb
4661 lb
8939 lb
3499 lb
7398 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 24497 lb



Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

**P2 & P3 RISERS TO BE MECHANICALLY ATTACHED
PRIOR TO INTERNAL INSTALLATION/DELIVERY**


Rim: 987.3' Rim to Invert: 6.12' Slack: 8.4" Sump: 69.96" Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	981.18'	270°	202.633"	24" HDPE	27.8"	Hole 32	32"	33.16"	12.96"	0"
Invert 2	981.18'	7°	5.253"	24" HDPE	27.8"	Hole 32	32"	33.16"	12.96"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

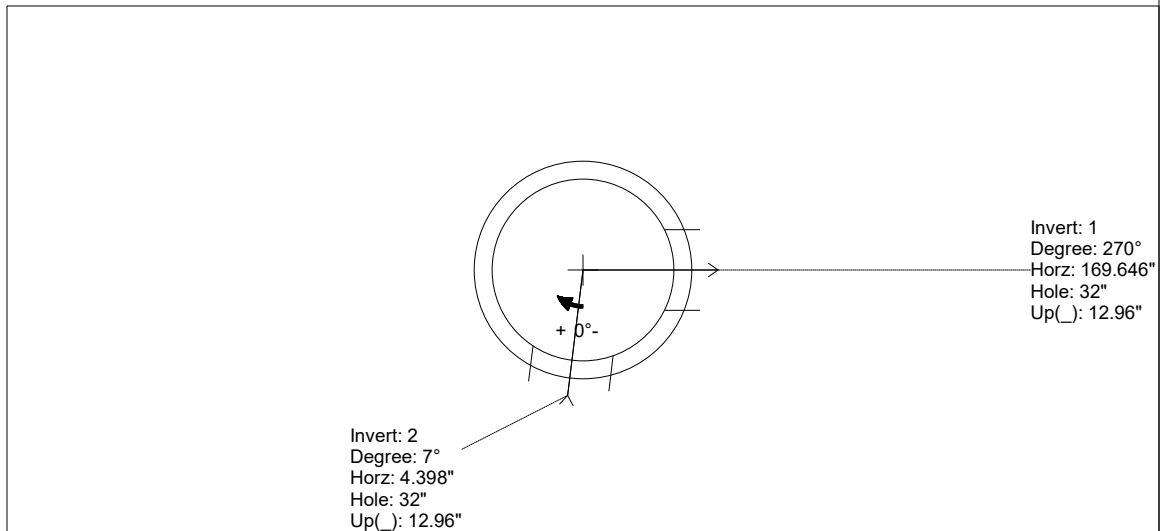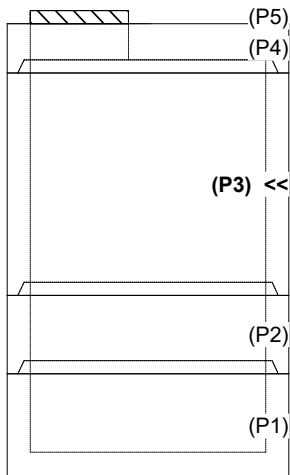

INSIDE WALL DIMENSIONS

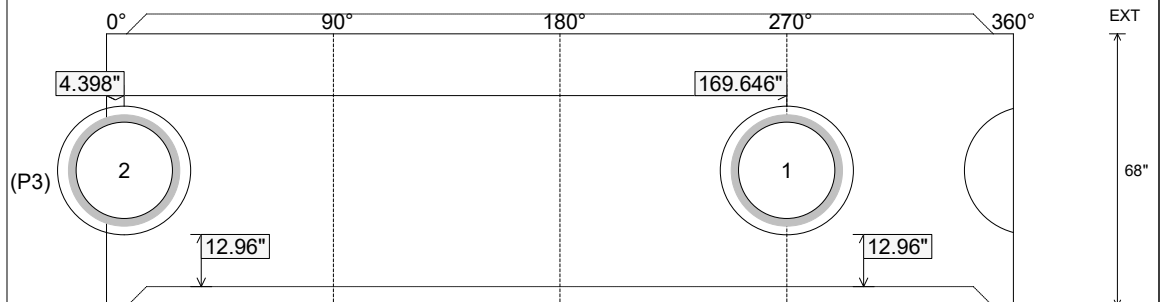

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 7"
Floor Height: 0"

Height (Int): 68"
Height (Ext): 68"

Weight (Net): 8939 lb
Volume (Net): 2.28cu.yd
