

Contractor: Bear Construction LLC

Plant: Beaver Dam




Slack: 0.06"

- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

2) Hole - 26


0 | b

Structure Total: 8376 lb

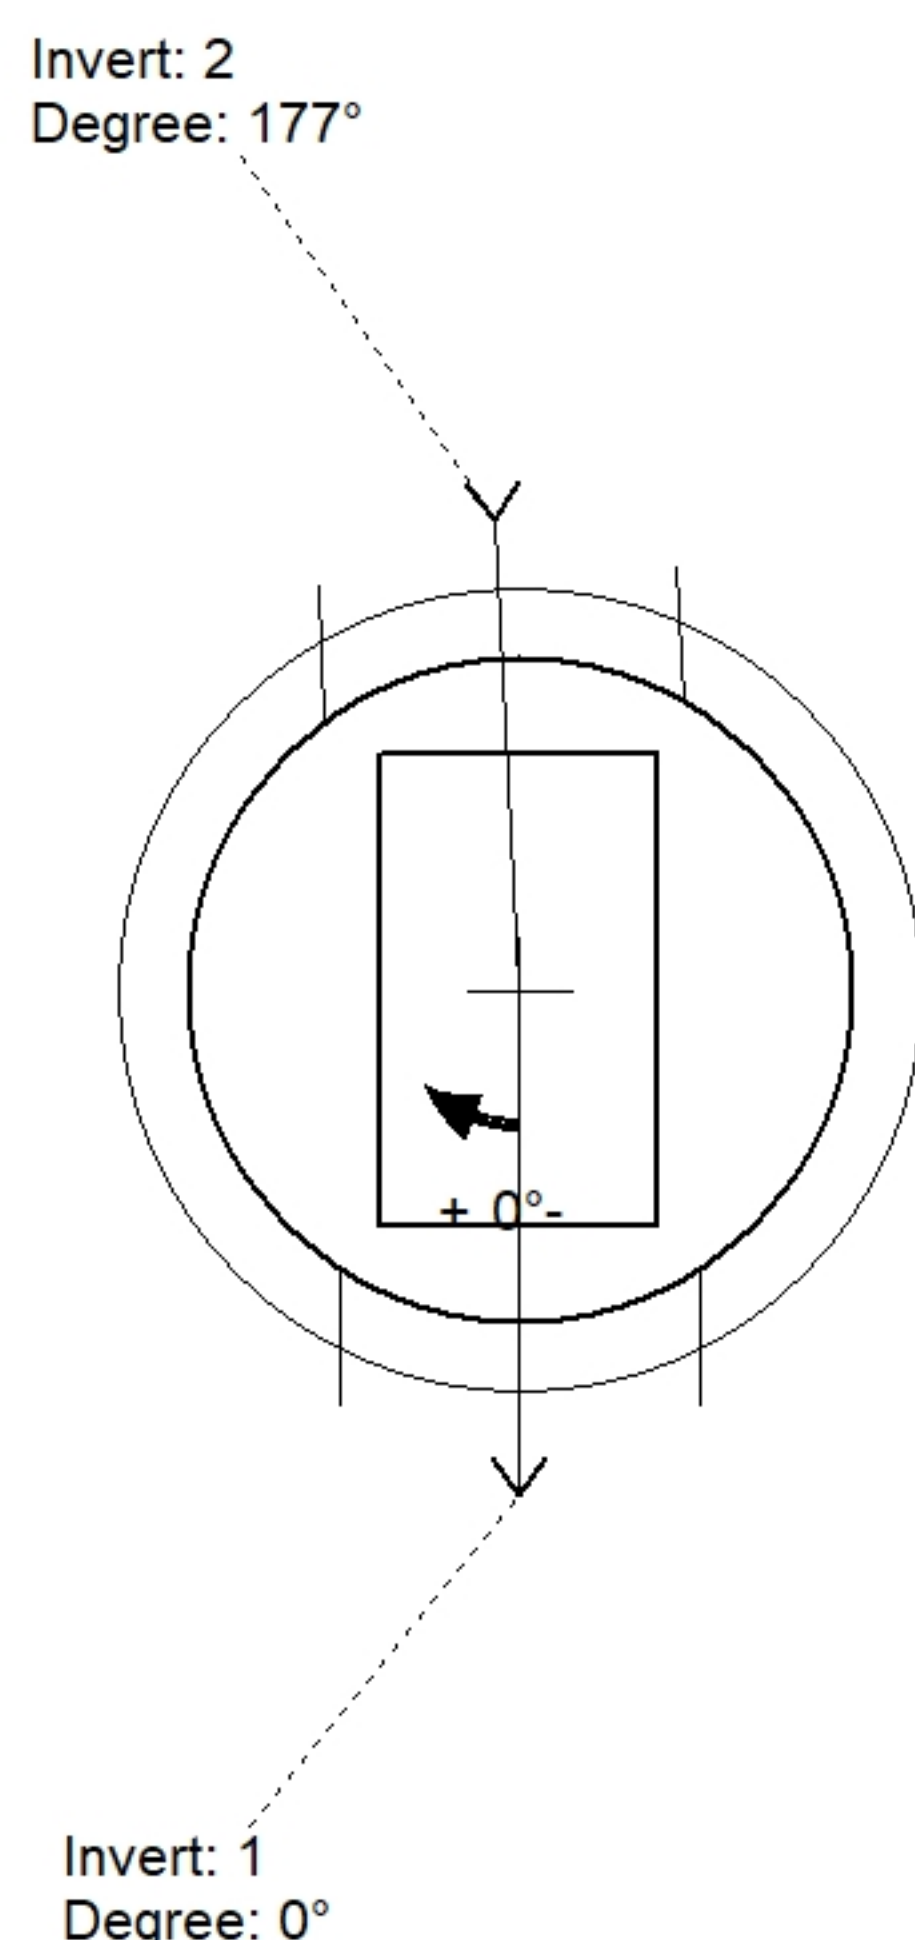

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	570.3'							
Reducer								
Invert 1	563.67'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	563.67'	177°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

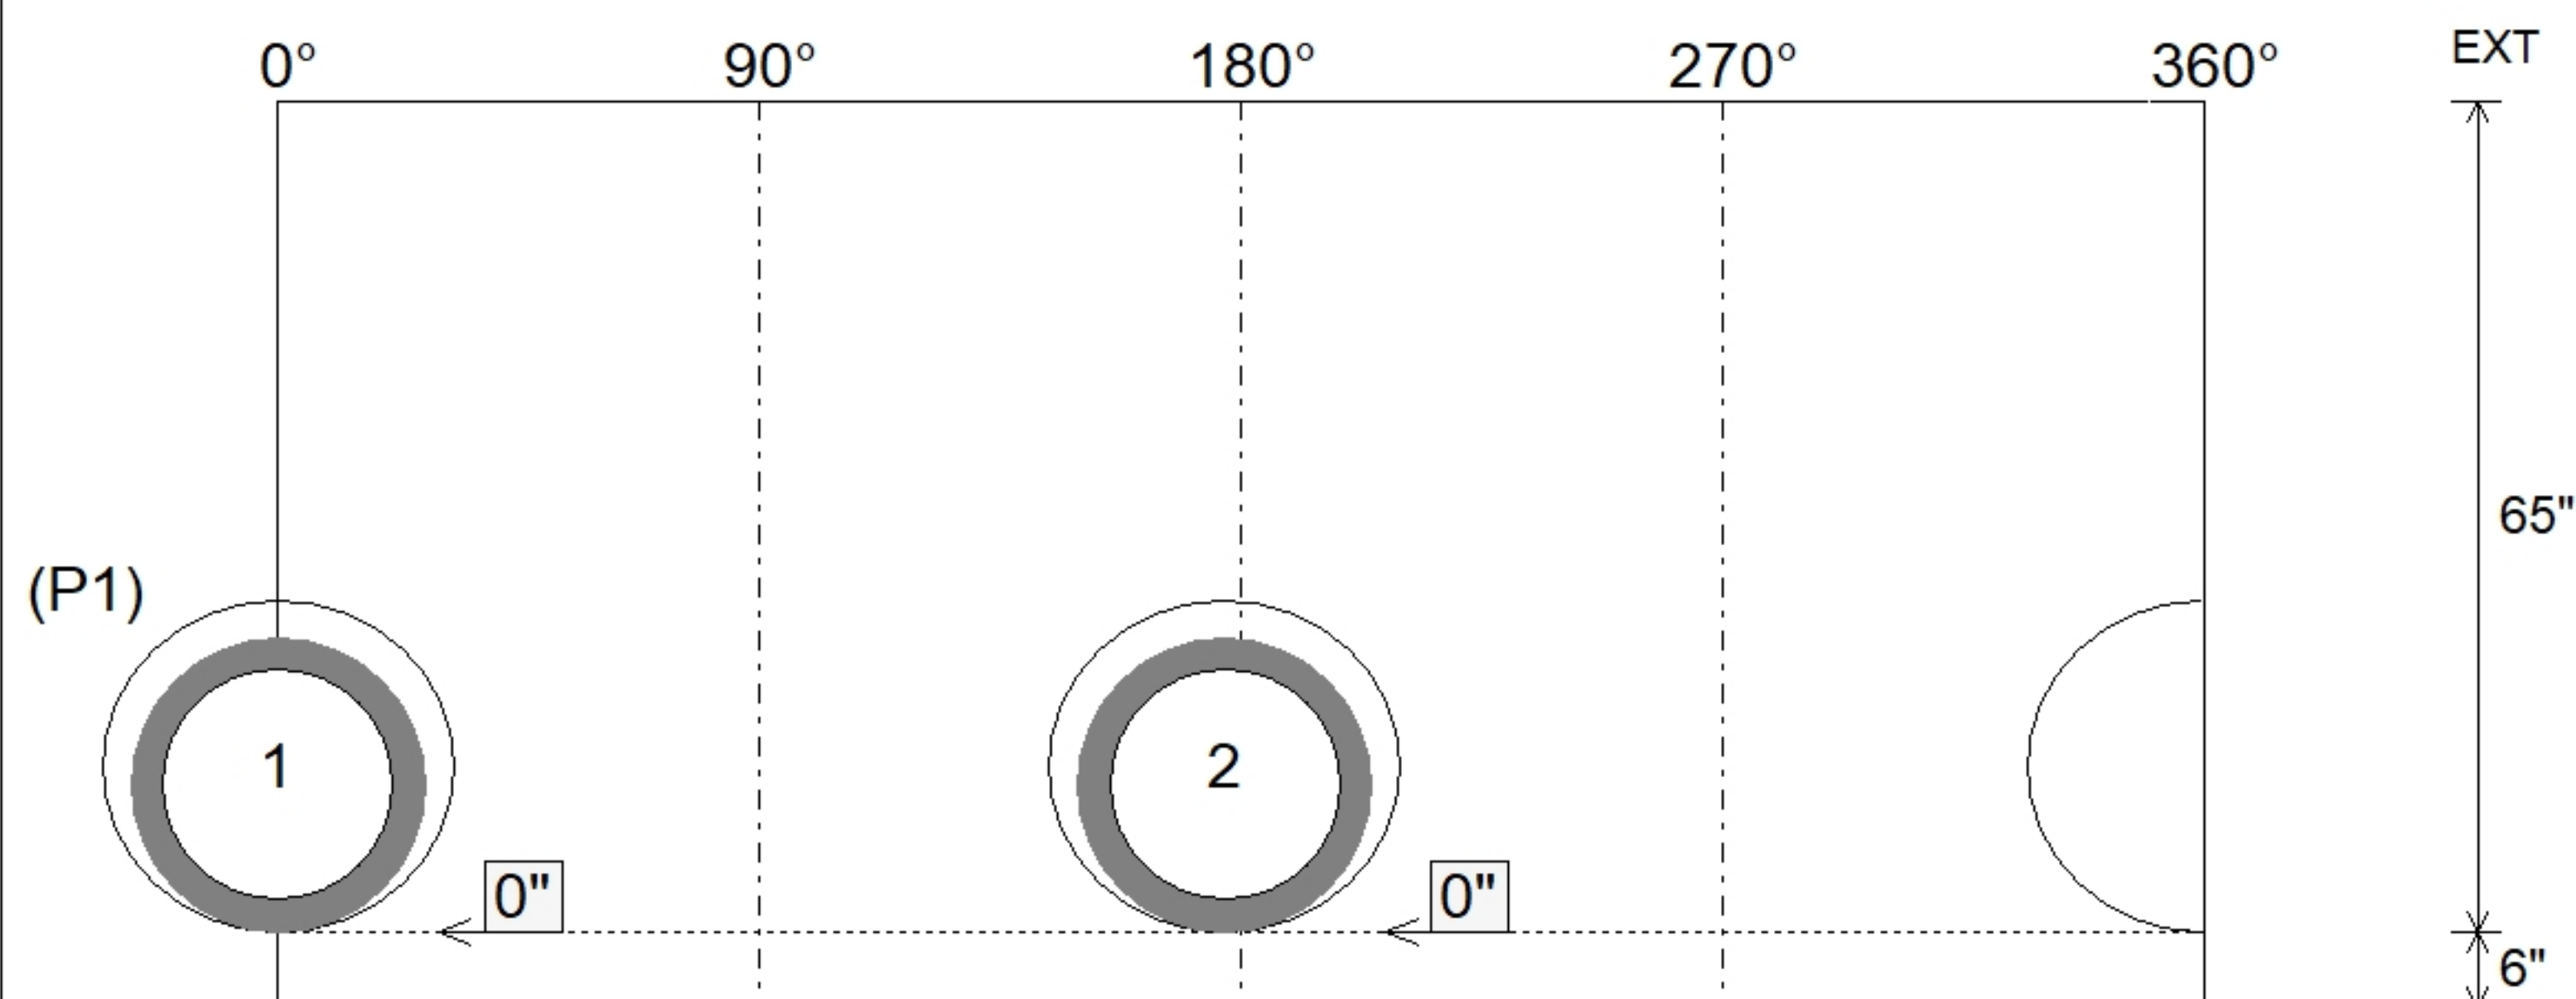

SUBMITTAL
APPROVED BY:
