

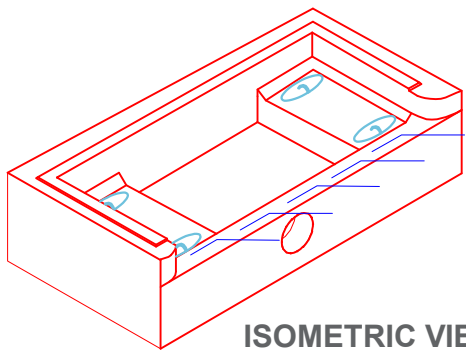
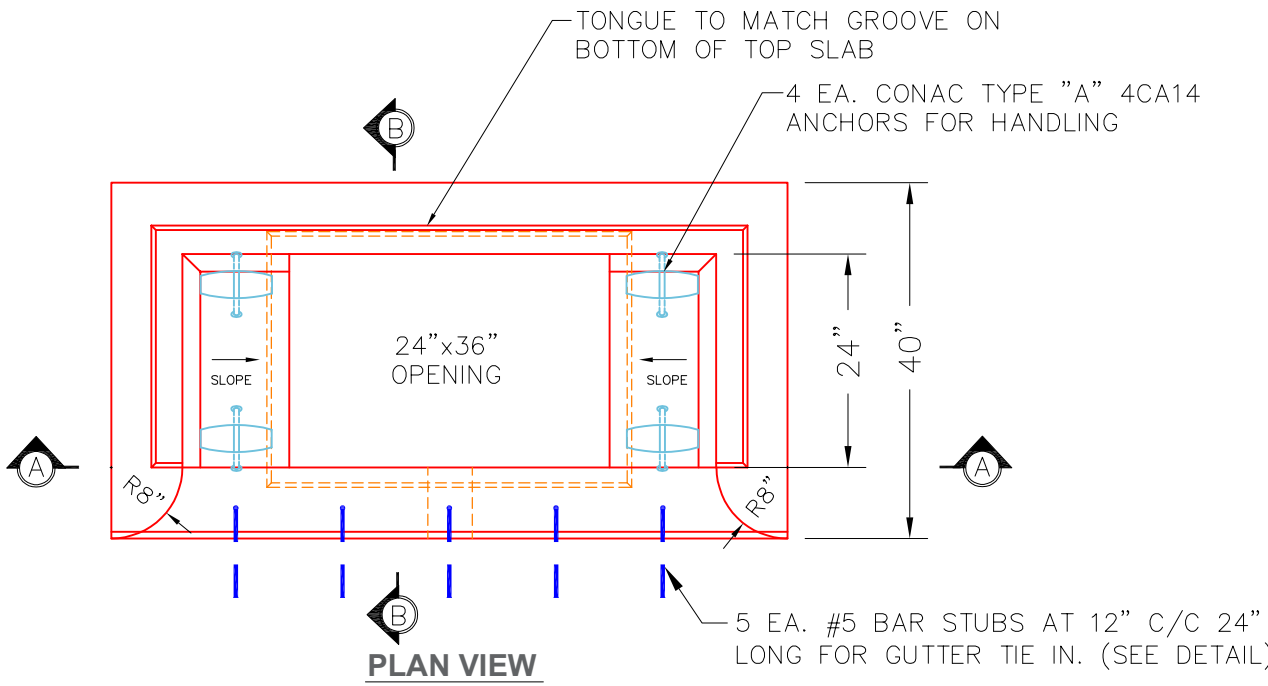


- NOTES:**
- 1. MANUFACTURE PER KYTC SPECIFICATIONS.
  - 2. CONCRETE  $f'_c = 4,500$  PSI AT 28 DAYS.
  - 3. REINFORCING: #5 BAR @ 12" C/C E.W. (GRADE 60).

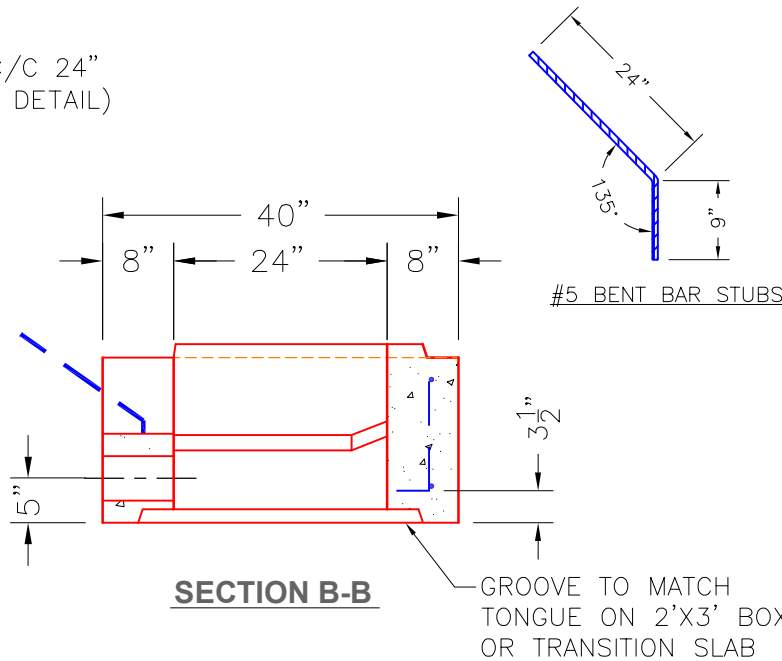

**ISOMETRIC VIEW**  
(SAG ORIENTATION)

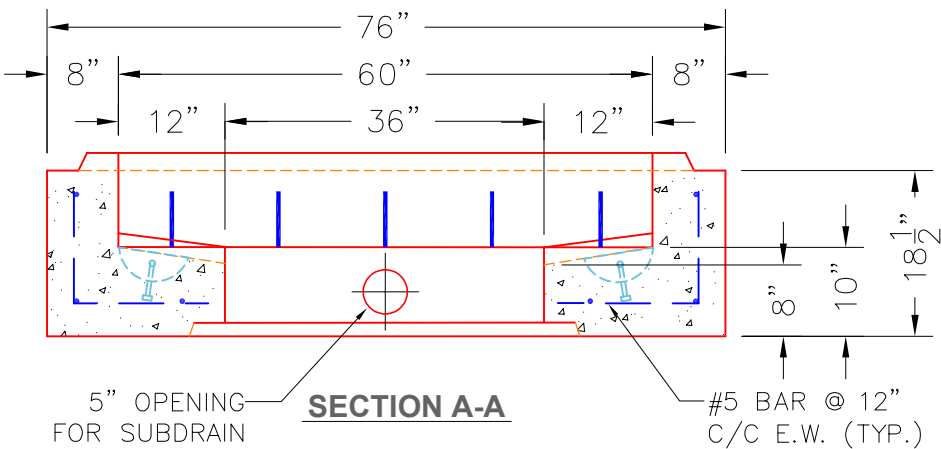

| PRODUCTION WORK ORDER                                                              |                                                       | PRODUCT I.D.: CBITA-5BS    | DESCRIPTION: KYTC 5' CBI-TYPE A TOP PHASE BOTTOM (SAG) |                |  |
|------------------------------------------------------------------------------------|-------------------------------------------------------|----------------------------|--------------------------------------------------------|----------------|--|
|  | QUALITY CONTROL CHECKLIST                             |                            | PRODUCT VIEW: RIGHT SIDE UP                            |                |  |
|                                                                                    | <input type="checkbox"/> ALL DIMENSIONS CORRECT.      |                            | CUSTOMER: STOCK                                        |                |  |
|                                                                                    | <input type="checkbox"/> LIFTERS INSTALLED.           |                            | PROJECT: STOCK                                         |                |  |
|                                                                                    | <input type="checkbox"/> CASTING AT CORRECT LOCATION. |                            | STRUCTURE ID.: STOCK                                   |                |  |
|                                                                                    | <input type="checkbox"/> REINFORCING CORRECT.         |                            | SALES ORDER NO.: N/A                                   |                |  |
|                                                                                    | <input type="checkbox"/> EXTENDED REBAR INSTALLED.    |                            | CHK.: J.H. ROSS, PE                                    |                |  |
|                                                                                    | <input type="checkbox"/> KYTC THROAT CORRECT.         |                            | DRAWING: N. RICHARDS                                   |                |  |
| <input type="checkbox"/> ALL PATCHWORK ACCEPTABLE.                                 |                                                       | TOP JOINT: SHIP-LAP TONGUE |                                                        | DATE: 04/18/24 |  |
|                                                                                    |                                                       | BOTTOM JOINT: N/A          |                                                        | SCALE: NTS     |  |
|                                                                                    |                                                       | QC CHECK INITIALS:         |                                                        | PG. 1 of 1     |  |
