


Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC				Plant: 100 6/22/2026 6:25:18 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: AR SS-ARV										
P2		MH048DHVF		MH DH RISER Custom Ht T/F						
P4) 24" - CASTING HEIGHT - 7" P3) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P2) 48" - MH DH RISER Custom Ht T/F - 45" P1) 48" - P.I.P. BY OTHERS - BTM SLAB F/n - 0" 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) DOGHOUSE - 8"x10" 4) MH Step ML-10-TDS-NCR - 10"				0 lb 1561 lb 3077 lb 0 lb 271 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4909 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 90 DEGREES 5. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Rim: 538'		Rim to Invert: 5'		Slack: 0"		Sump: 4"		Step Position: 90°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	533'	0°	0"	4" PVC SDR21	4.375"	DOGHOUSE 8"x10"	8" x 10"	8.038"	1"	0"
Invert 2	533'	180°	91.125"	4" PVC SDR21	4.375"	DOGHOUSE 8"x10"	8" x 10"	8.038"	1"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

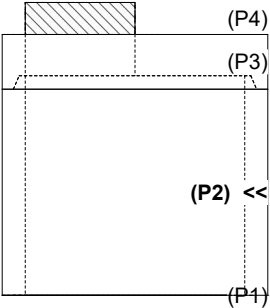

(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 5" Floor Height: 0"	Height (Int): 45" Height (Ext): 45"	Weight (Net): 3077 lb Volume (Net): 0.79cu.yd
----------------------------------	----------------------------------	--	--	--
