
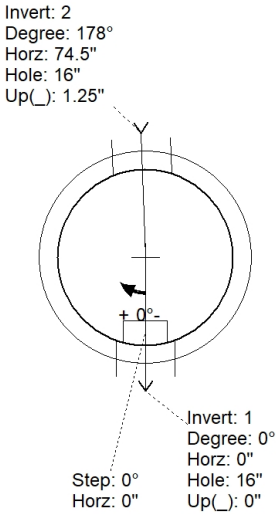
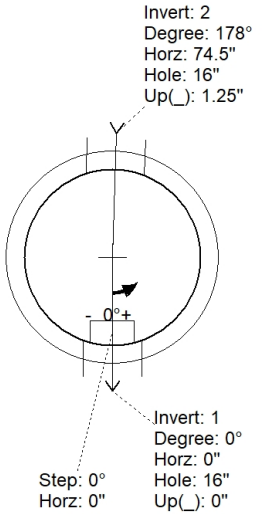


Job Name: 26-2260 - Bowling Green JR High School Job Location: Bowling Green, KY Contractor: Scott & Ritter, Inc.					Plant: 100 7/15/2026 1:37:25 PM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 4 SS-MH											
P1		MH048BA36		MH BASE T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 36" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y DD (DBL Bands) 2) MH Step ML-10-TDS-NCR - 10" Structure Total: 6690 lb					0 lb 1561 lb 3674 lb 1440 lb 0 lb 0 lb 0 lb 15 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-375 F/C). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 519' Rim to Invert: 4.54' Slack: 2.48' Sump: 3" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	514.46'	0°	0"	10" PVC SDR35	10.5"	PSX 16Y DD (DBL Bands)	16"	16.312"	0"	0"	
Invert 2	514.56'	178°	90.125"	10" PVC SDR35	10.5"	PSX 16Y DD (DBL Bands)	16"	16.312"	1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 36" Height (Ext): 42"		Weight (Net): 3674 lb Volume (Net): 0.94cu.yd	

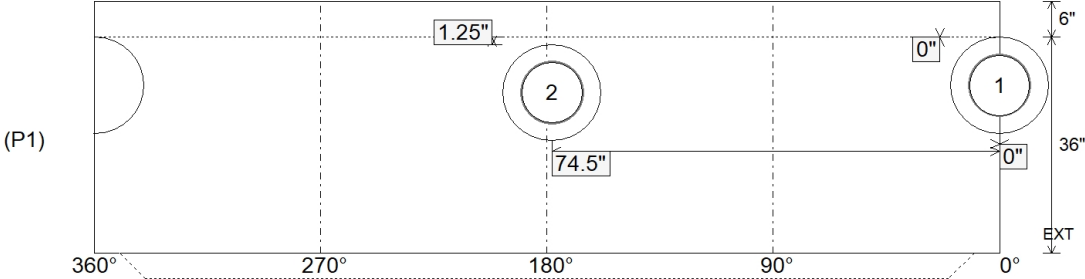

Weight (Net): 3674 lb
Volume (Net): 0.94cu.yd
