


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:26 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 5081+13 RT CBBI-MOD B1											
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 38" 1) 36" x 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 48"x44" 1) DOGHOUSE INVRTD - 40"x40" Structure Total: 10454 lb					4000 lb 977 lb 5476 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: . -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.				
Rim: 580.31' Rim to Invert: 5.25' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	575.06'	90°	32"	36" RCP B WALL	44"	DOGHOUSE INVRTD 48"x44"	48" x 44"	48"	-4"	0"	
Invert 2	575.06'	270°	32"	36" CMP	37"	DOGHOUSE INVRTD 40"x40"	40" x 40"	40"	-2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

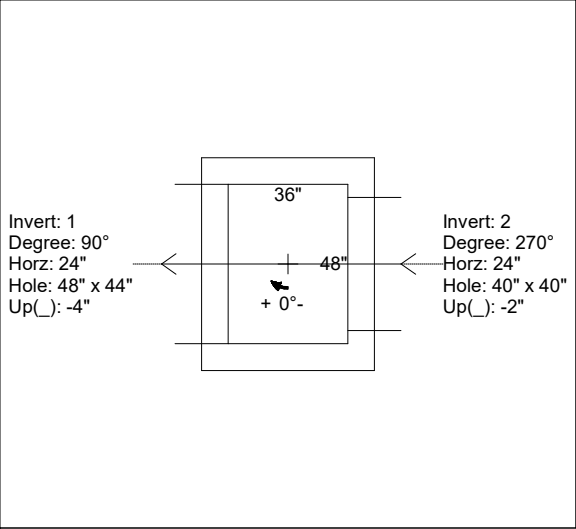

Invert: 1
Degree: 90°
Horz: 24"
Hole: 48" x 44"
Up(): -4"

Invert: 2
Degree: 270°
Horz: 24"
Hole: 40" x 40"
Up(): -2"


UPSIDE-DOWN VIEW (int. dimensions)

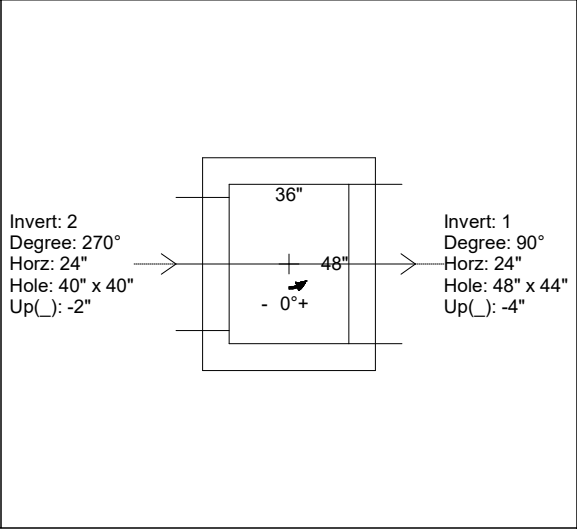

Invert: 2
Degree: 270°
Horz: 24"
Hole: 40" x 40"
Up(): -2"

Invert: 1
Degree: 90°
Horz: 24"
Hole: 48" x 44"
Up(): -4"

INSIDE WALL DIMENSIONS

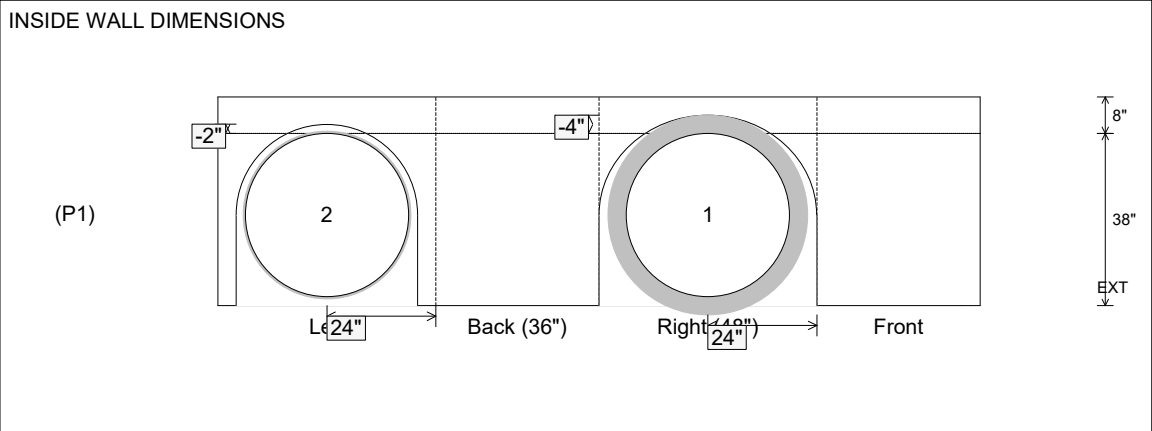

(P1)

2

1

Back (36")

Right (24")

Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 38" Height (Ext): 46"	Weight (Net): 5476 lb Volume (Net): 1.4cu.yd
----------------------------------	-------------------------------	--	--	---
