



Job Name: 26-2270 - Walmart #299 Fuel Station Job Location: Bowling Green, KY Contractor: Stewart Richey					Plant: 100 8/10/2026 11:47:12 AM		Tech: Jared - F PC: T. Lewis				
Structure ID: 1.1.2 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" x 34" - CASTING HEIGHT - 6.5" P2) 48" - MH FLAT TOP w/24"x34" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 64" 1) CASTING - JBS 3080 SET (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) Hole - 26 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1839 lb 5568 lb 500 lb 0 lb 0 lb 0 lb ----- 7907 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 3080 SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 546.01' Rim to Invert: 6.95' Slack: 0.9" Sump: 0" Step Position: 180°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	539.06'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

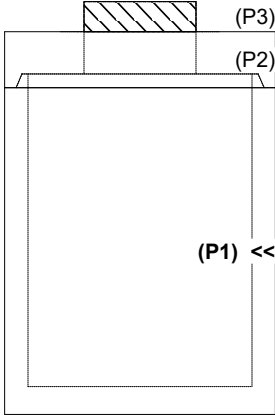

(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

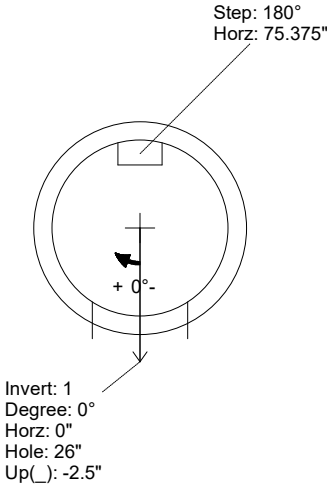

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(): -2.5"


UPSIDE-DOWN VIEW (int. dimensions)

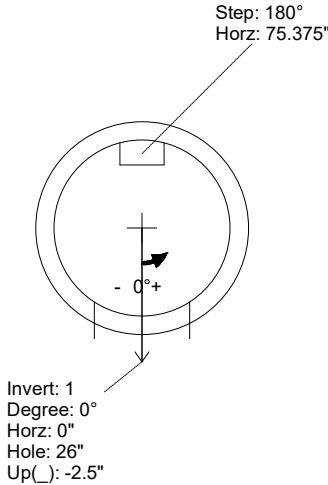

Step: 180°
Horz: 75.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(): -2.5"

INSIDE WALL DIMENSIONS

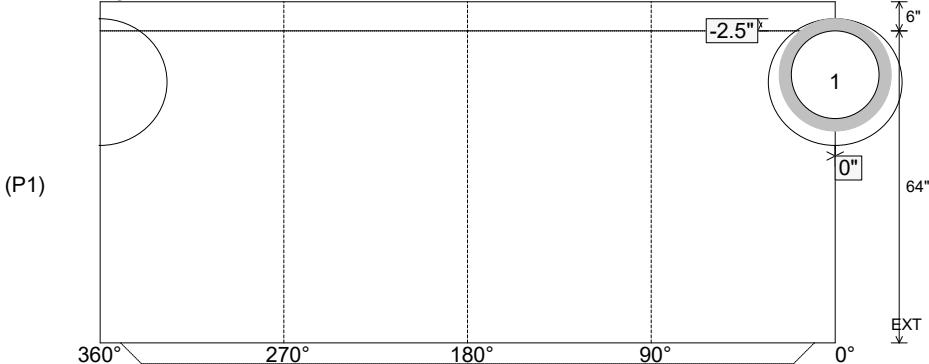

(P1)

360° 270° 180° 90° 0°

6"

2.5"

64"

0"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 64" Height (Ext): 70"	Weight (Net): 5568 lb Volume (Net): 1.42cu.yd
----------------------------------	---------------------------------	--	--	--
