

Job Name: 26-2644 881922 Hawkins School Tennis
Job Location: Cleveland, OH
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

6/15/2026 10:28:10 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 15-CS-8

P1 MH096BAVF

MH MONOBASE 13F, Custom Ht T/n

- P4) 24" - CASTING HEIGHT - 4"
P3) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17"
P2) 96" - MH RISER T/G - 96"
P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24"
1) CVSTENCILING
1) ASSEMBLY REQUIRED
2) 96" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 32

0 lb
10015 lb
22680 lb
17113 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

49809 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE




Structure Total:

Rim: 1028.15' Rim to Invert: 5.9' Slack: 11.844" Sump: 82.044" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

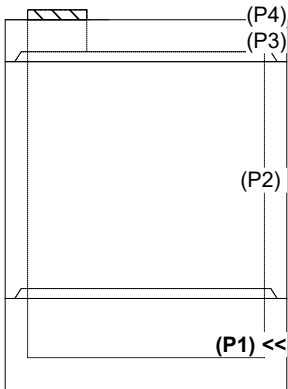

INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 9"
Floor Height: 13"

Height (Int): 24"
Height (Ext): 37"

Weight (Net): 17113 lb
Volume (Net): 4.37cu.yd
