



Job Name: 25-2023 - Guthrie KY. Convenience Store Job Location: Guthrie, KY Contractor: Core & Main LP					Plant: 100 6/1/2026 5:37:22 PM		Tech: Jared - F PC: T. Lewis				
Structure ID: OCS											
P1		BX3636-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P3) 24" - CASTING HEIGHT - 0" P2) 36" x 36" - CB FLAT TOP 8"W w/24"Hole F/F - 6" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 32" 1) CASTING - JBS 2072 F/G 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 7 1) Weir n/n - 24"x8"					0 lb 1134 lb 5138 lb 250 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 6521 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 2072 F/G CAST-IN, FLANGE UP). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 549.67' Rim to Invert: 3.17' Slack: 0.04" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	546.5'	0°	26"	18" HDPE	21.2"	Hole 24	24"	24"	-1.625"	0"	
Invert 2	546.5'	180°	26"	7" Orifice	7"	Hole 7	7"	7"	0"	0"	
Invert 3	548.5'	180°	26"	24" x 8" Weir	24" x 8"	Weir 24"x8"	24" x 8"	24"	24"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

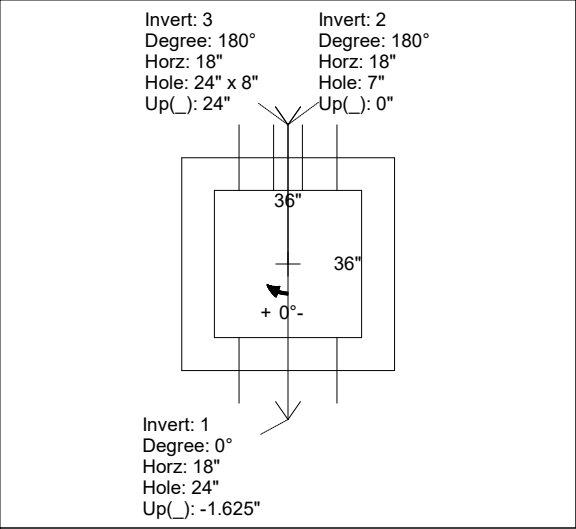

UPSIDE-DOWN VIEW (int. dimensions)

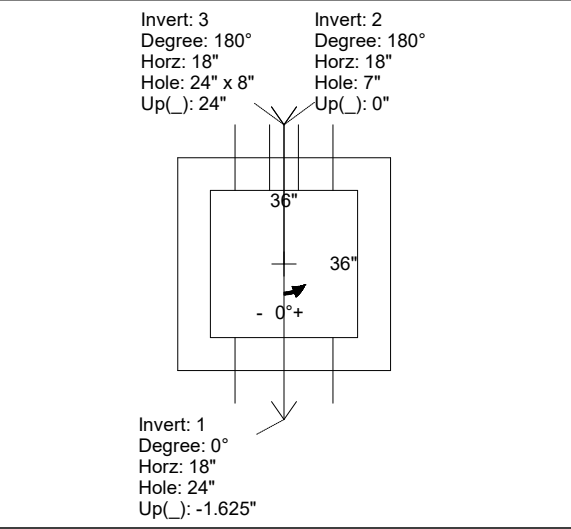

INSIDE WALL DIMENSIONS

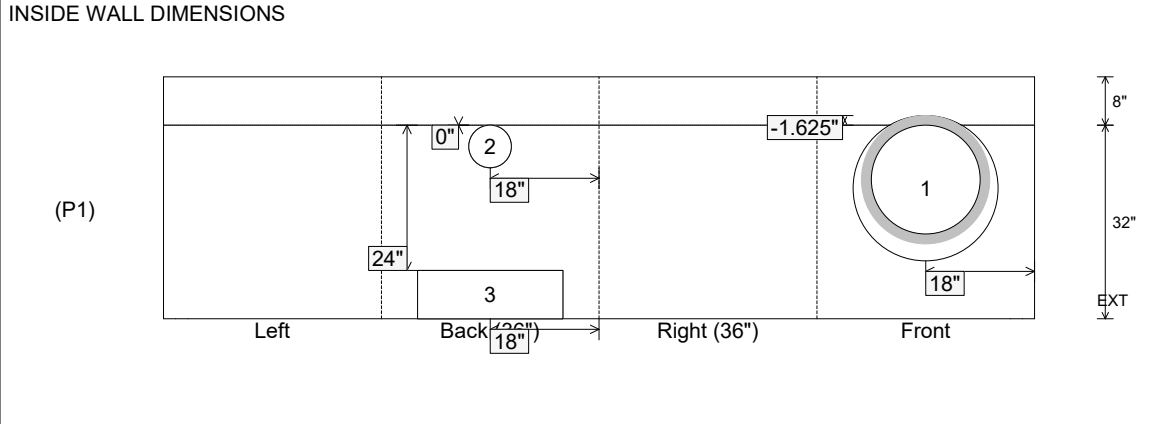

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 32" Height (Ext): 40"	Weight (Net): 5138 lb Volume (Net): 1.31cu.yd
----------------------------------	-------------------------------	--	--	--
