



Job Name: 26-2435 838635 Bridge Park Block J Job Location: Dublin, OH Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/4/2026 8:07:04 AM		Tech: S. Felletter PC: C. Goff						
Structure ID: 20-CS-8													
P2		MH096RS96		MH RISER T/G									
P5) 24" - CASTING HEIGHT - 4" P4) 96" - MH FLAT TOP SPEC. (2 - 24"Ø HOLES) F/G - 17" P3) 96" - MH RISER T/G - 36" P2) 96" - MH RISER T/G - 96" P1) 96" - MH MONOBASE 13F, Custom Ht T/n - 24" 1) CVSTENCILING 1) ASSEMBLY REQUIRED 3) 96" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 3) Hole - 36						0 lb 10015 lb 8819 lb 21710 lb 17113 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 57657 lb Structure Total:		Structure Notes: 4" CASTING BY OTHERS LIFT ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 841.96' Rim to Invert: 8' Slack: 1.044" Sump: 82.044" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	833.96'	270°	268.606"	24" RCP B WALL	30"	Hole 36	36"	36.902"	47.044"	0"			
Invert 2	834.46'	172°	171.112"	24" RCP B WALL	30"	Hole 36	36"	36.902"	53.044"	0"			
Invert 3	835.36'	355°	353.167"	24" RCP B WALL	30"	Hole 36	36"	36.902"	63.844"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

RIGHT-SIDE UP VIEW (int. dimensions)

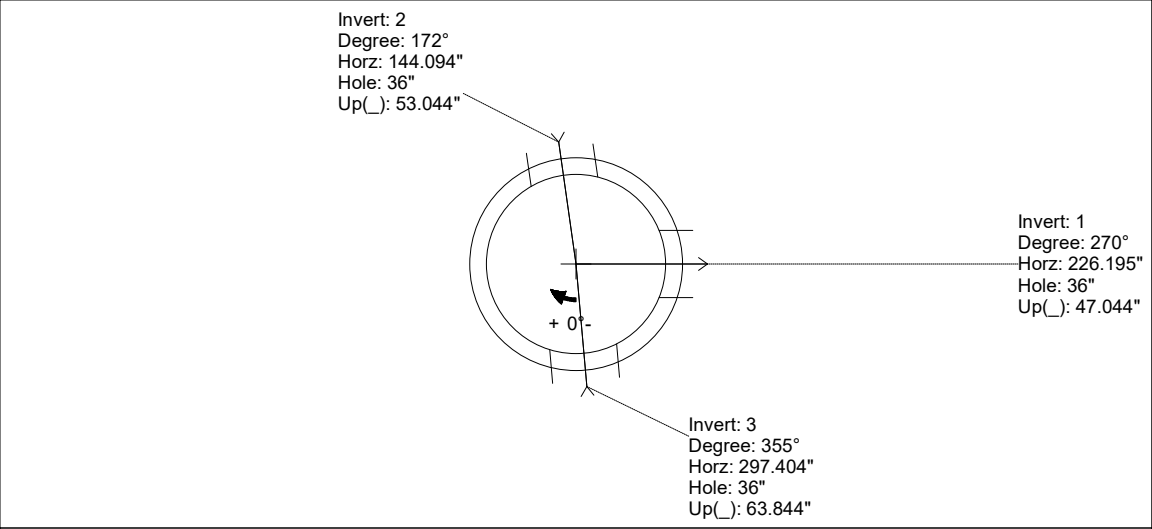

INSIDE WALL DIMENSIONS

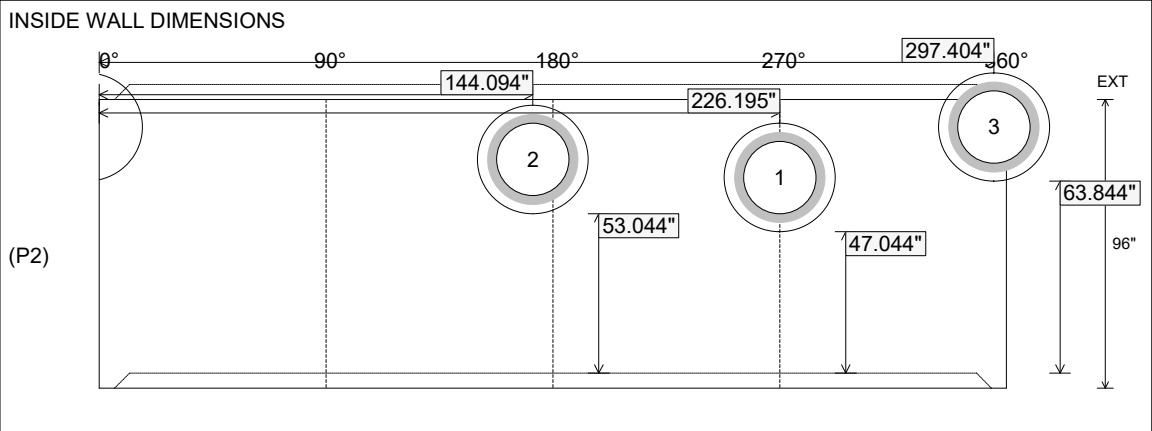

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 9" Floor Height: 0"	Height (Int): 96" Height (Ext): 96"	Weight (Net): 21710 lb Volume (Net): 5.54cu.yd
----------------------------------	------------------------------------	--	--	---
