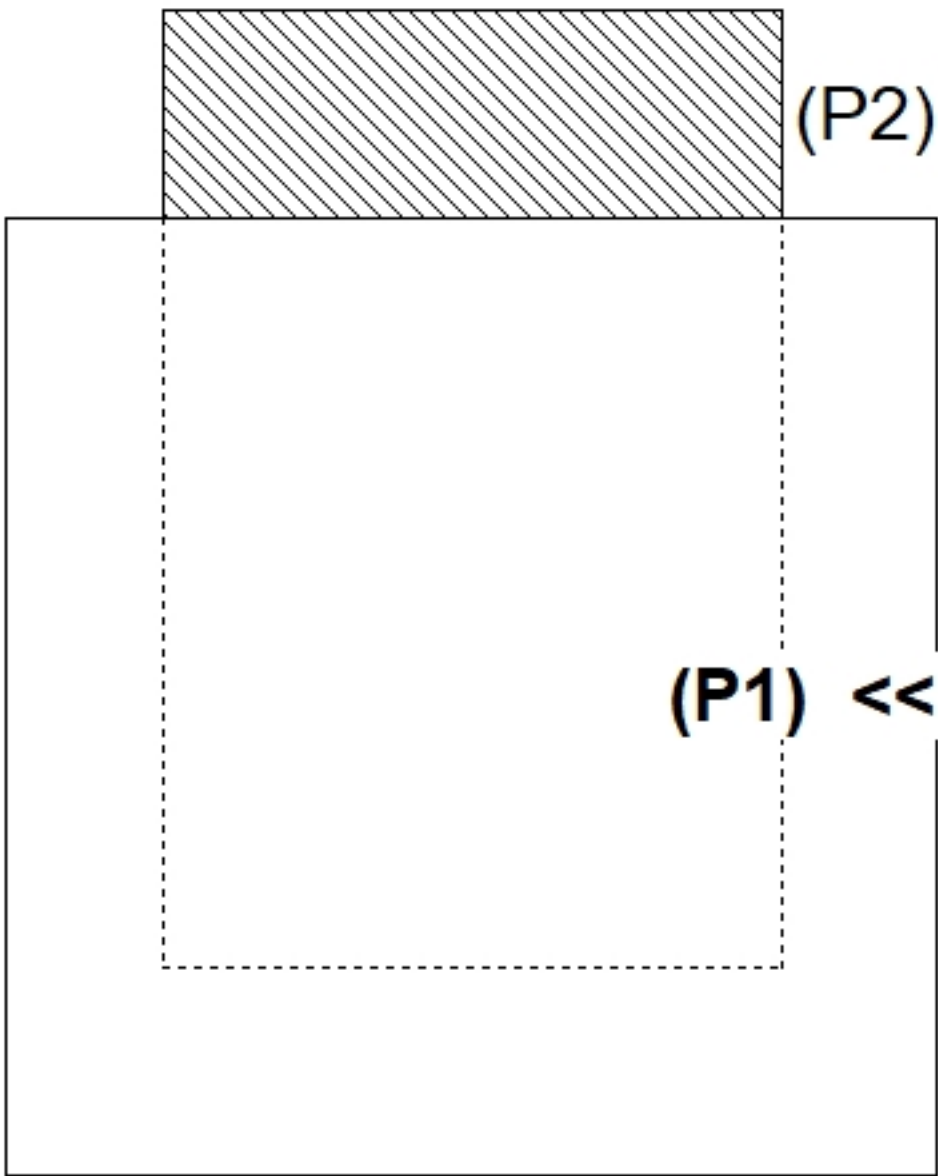
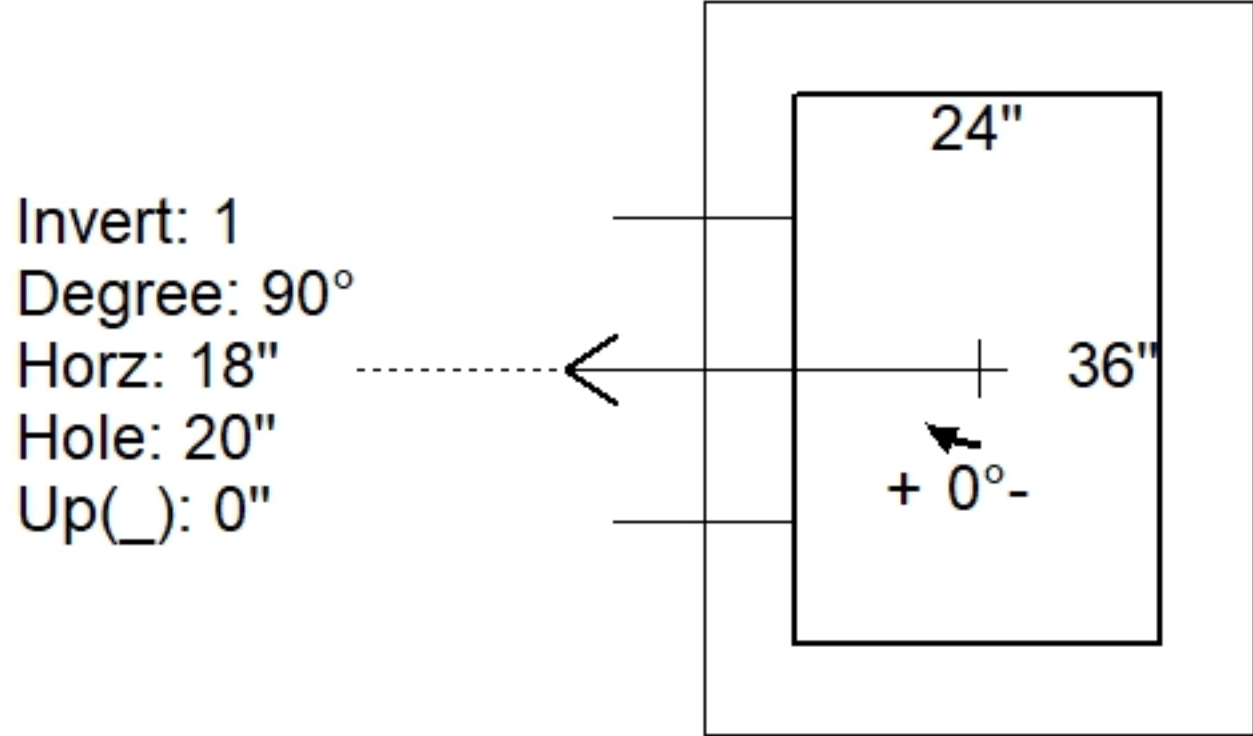
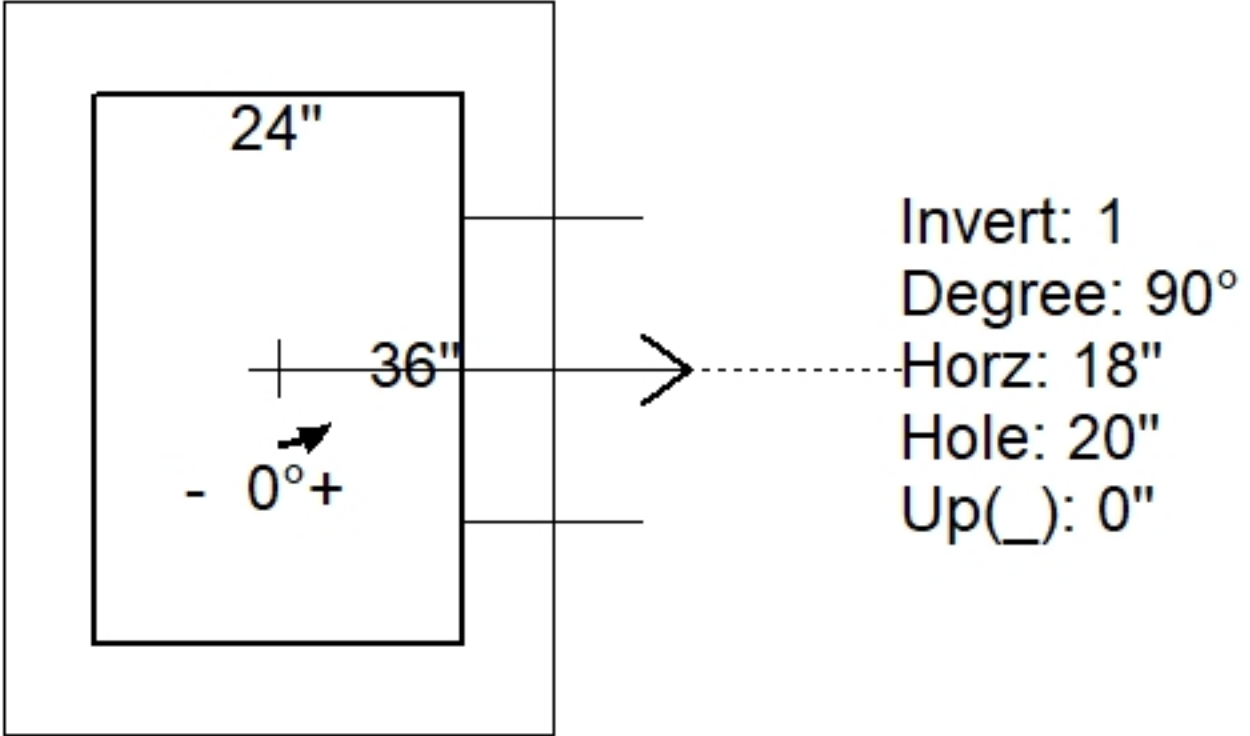
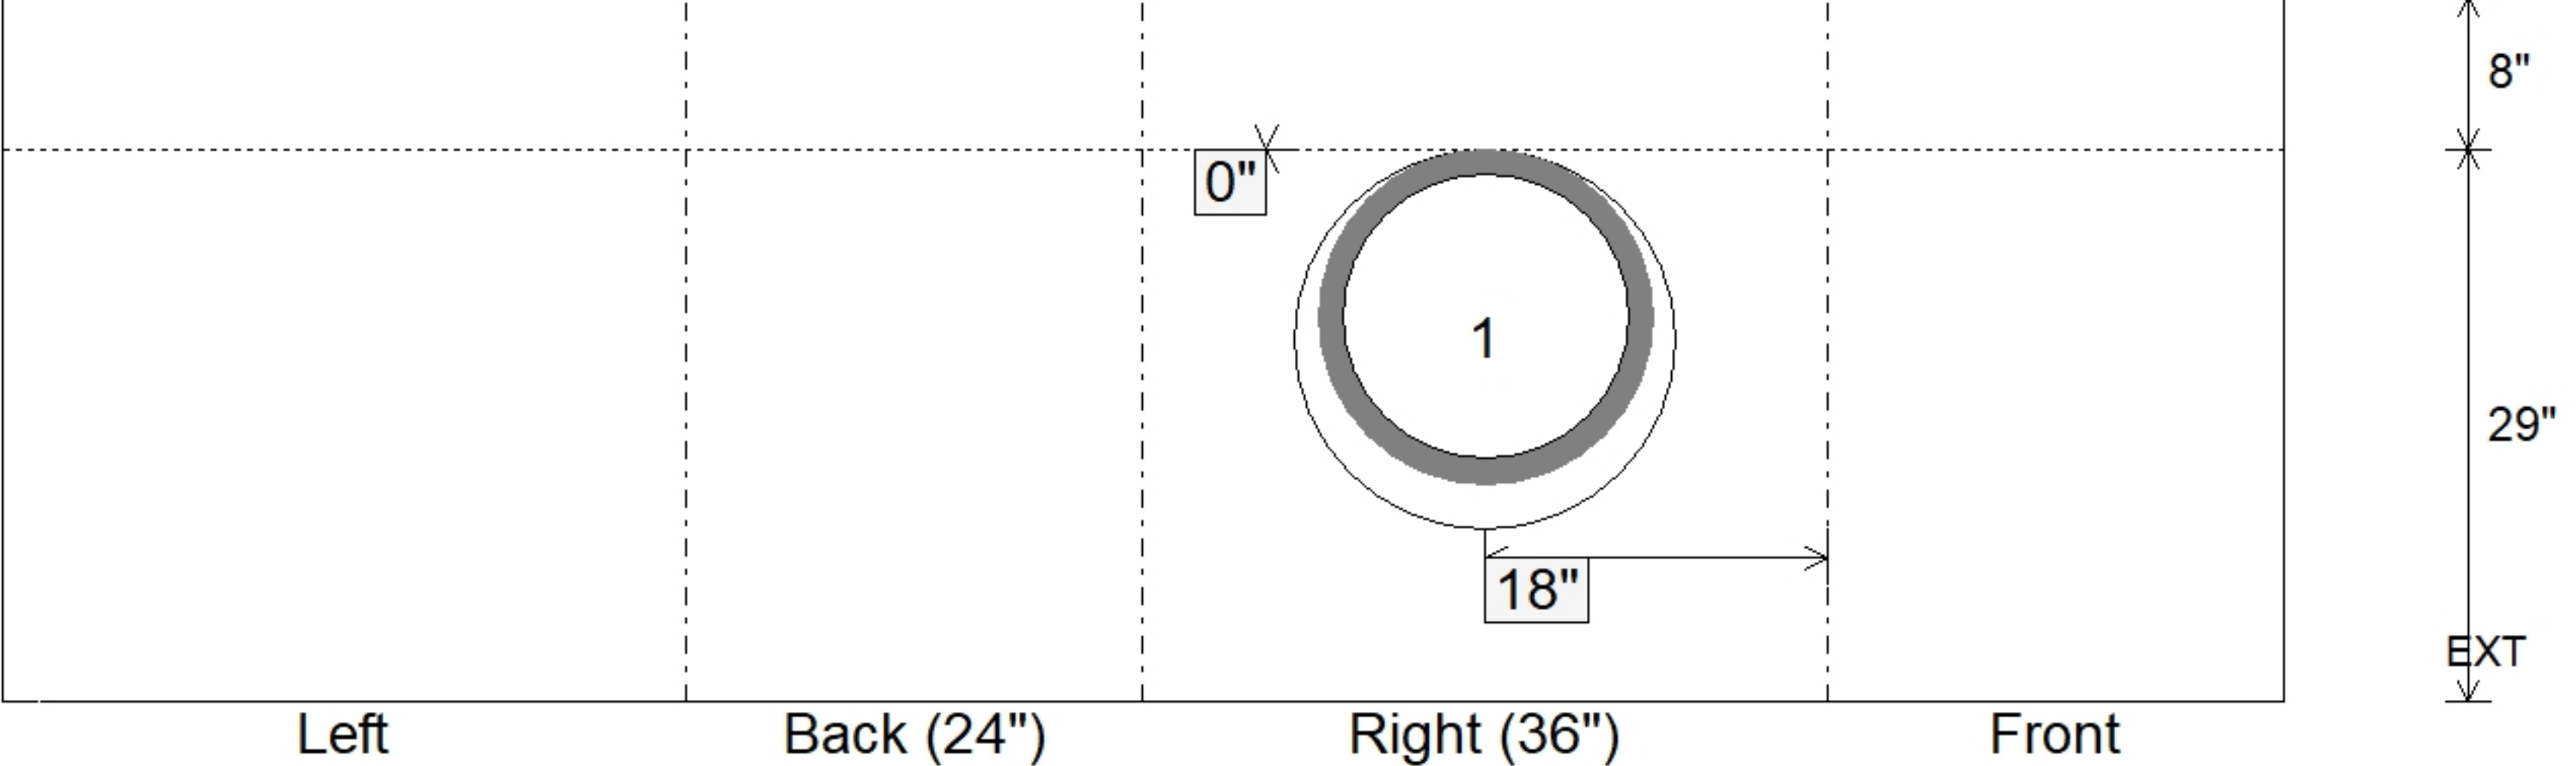


Job Name: 26-1852 - Oakland City CCMG Job Location: Oakland City, IN Contractor: SAMM Trucking & Excavating, Inc.				Plant: 100 7/15/2026 12:46:32 PM		Tech: J. Horsley PC: J. Jarvis					
Structure ID: QL3 INJ10 - Madison & Columbia Streets											
P1		BX2436-06W08F-BAVF			BOX BASE 6inW, 8inF, Variable Ht F/n						
P2) 24" x 36" - CASTING HEIGHT - 8" P1) 24" x 36" - BOX BASE 6inW, 8inF, Variable Ht F/n - 29" 1) 24" x 36" - Con Seal CS-102 1.00" 1) Hole - 20					0 lb 3104 lb 0 lb 0 lb ----- 3104 lb		Structure Notes: 1. INDOT INLET TYPE J / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE R-3827-10V F/G/H) SUPPLIED BY ICAST. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 3'					Rim to Invert: 3'		Slack: 0.296"		Sump: 1.296"		Step Position:
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	0'	90°	24"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											UPSIDE-DOWN VIEW (int. dimensions)
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 29" Height (Ext): 37"		Weight (Net): 3104 lb Volume (Net): 0.79cu.yd		
