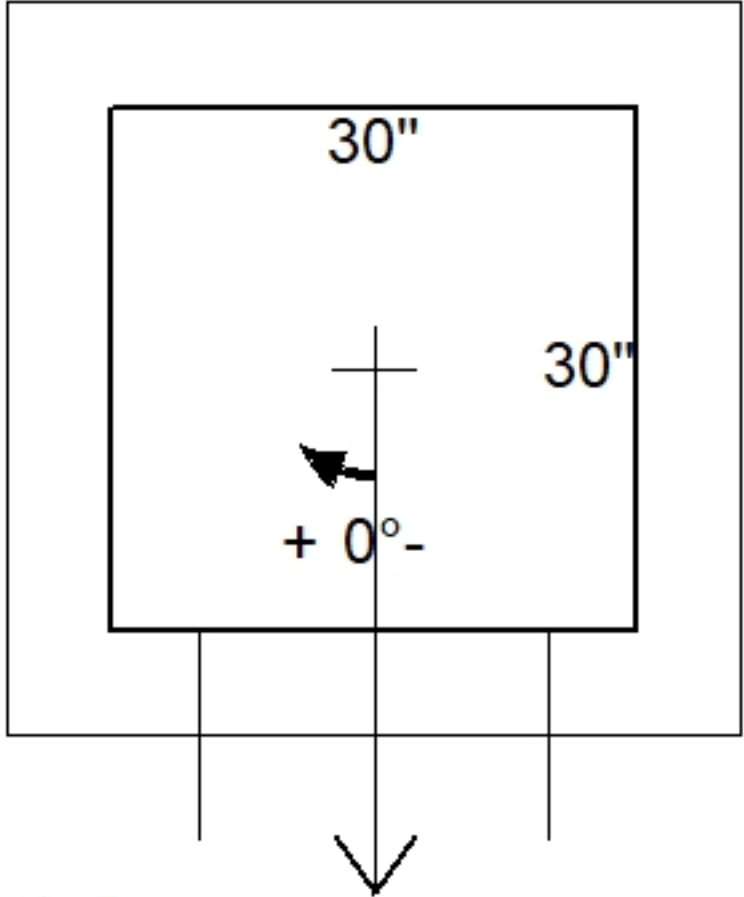
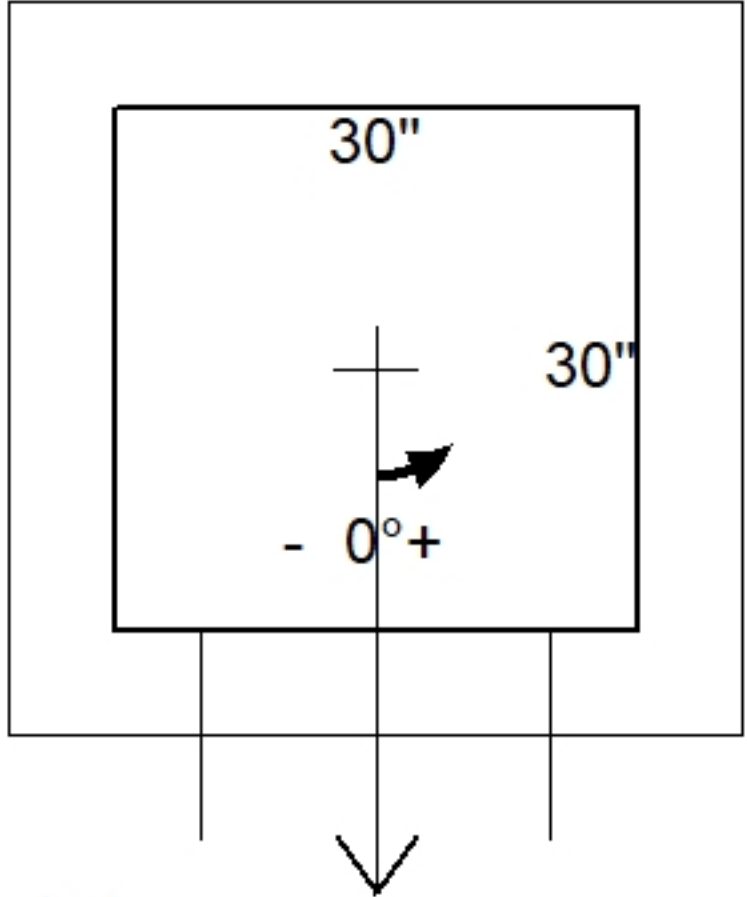
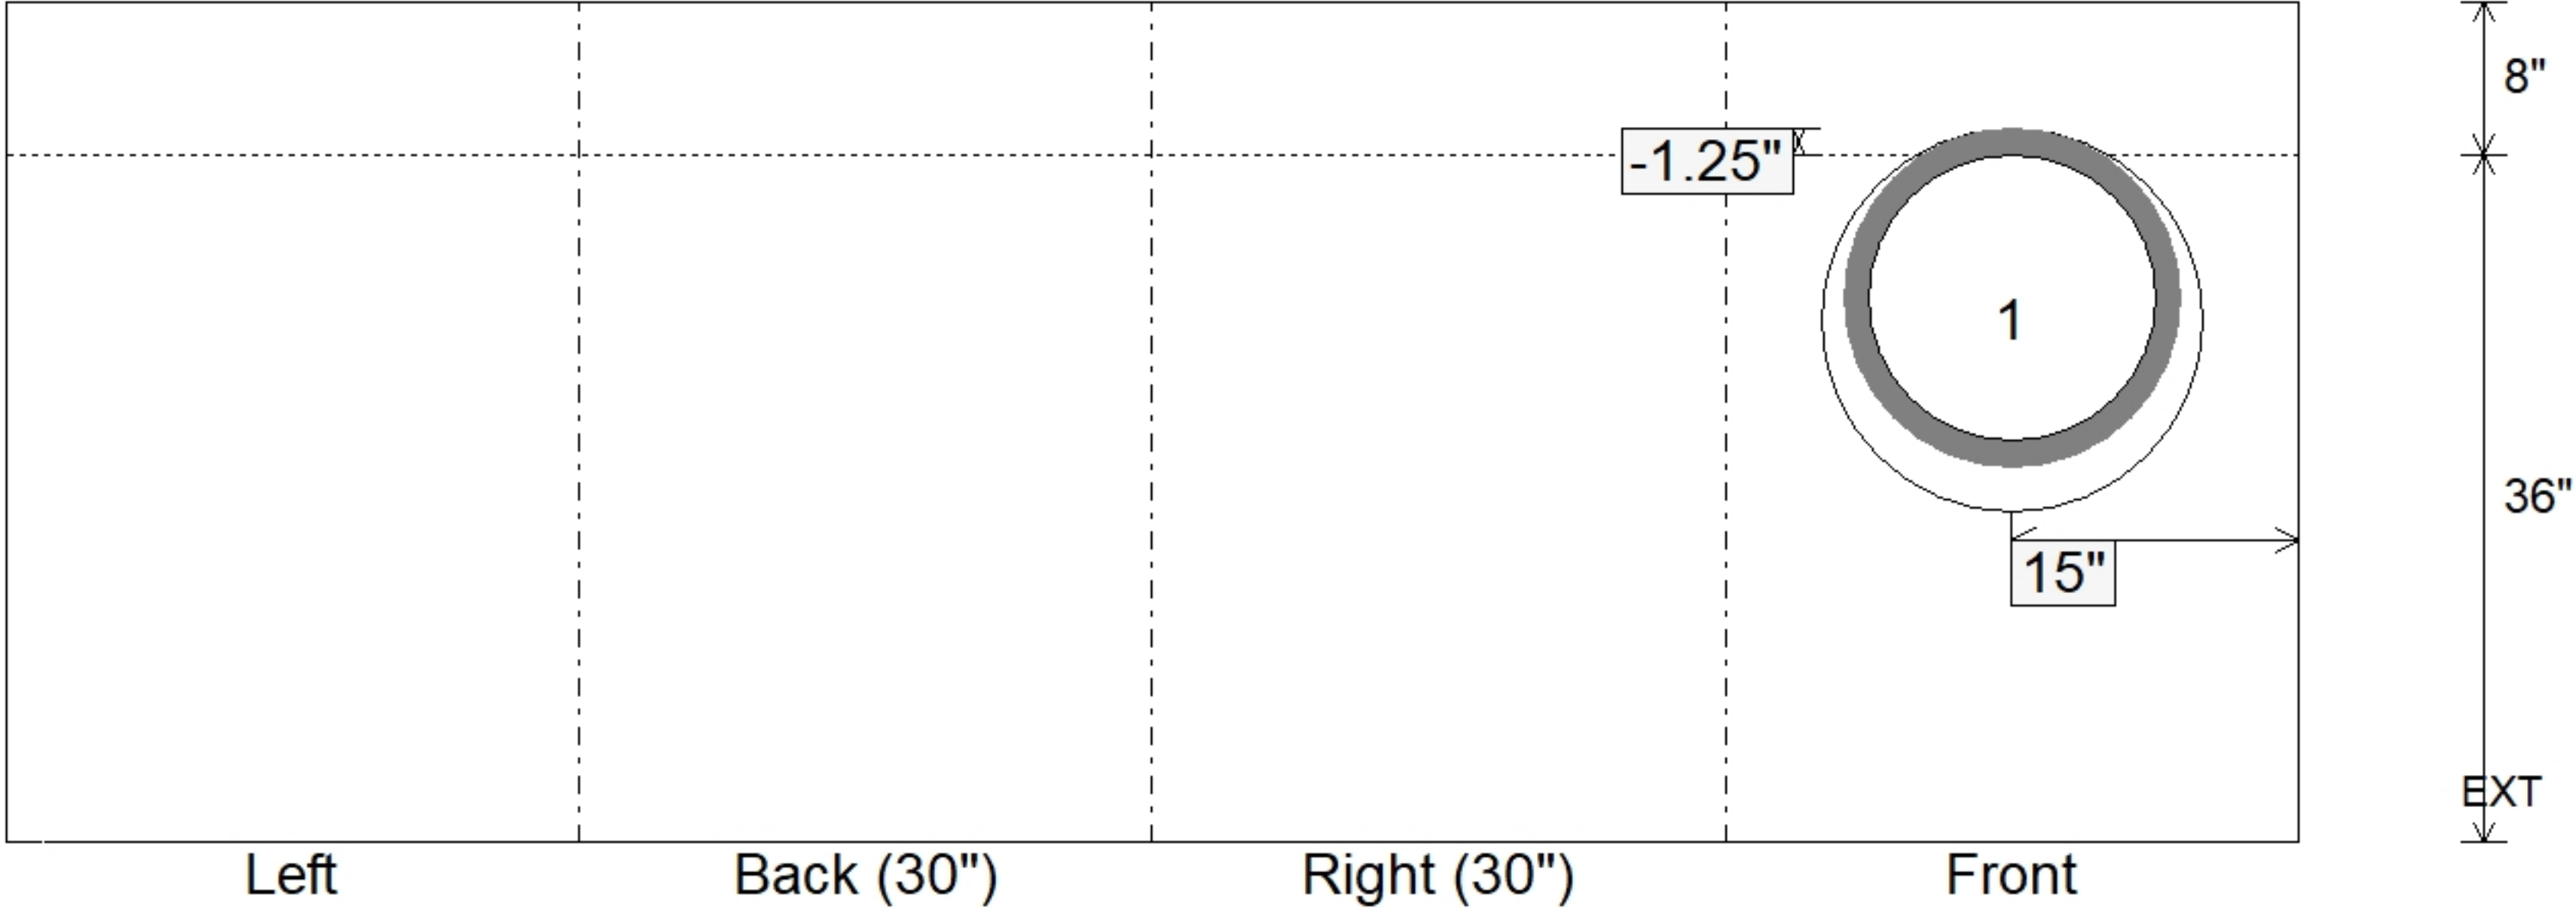


Job Name: 26-1852 - Oakland City CCMG Job Location: Oakland City, IN Contractor: SAMM Trucking & Excavating, Inc.				Plant: 100 7/15/2026 12:46:33 PM		Tech: J. Horsley PC: J. Jarvis					
Structure ID: QL5 INE7 - Trusler & Walnut Streets											
P1		BX3030-06W08F-BAVF			BOX BASE 6inW, 8inF, Variable Ht F/n						
P2) 30" x 30" - CASTING HEIGHT - 0" P1) 30" x 30" - BOX BASE 6inW, 8inF, Variable Ht F/n - 36" 1) 30" x 30" - SGL 1"x14.5' Butyl 1) Hole - 20					0 lb 3636 lb 0 lb 0 lb ----- Structure Total: 3636 lb		Structure Notes: .. 1. INDOT INLET TYPE E / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING (HOE R-4215C GRATE) BY ICAST. 4. RECESS/GRATE SEAT (34.5"x34.5"x1" DEEP) IN TOP OF WALLS. . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 3'		Rim to Invert: 3'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	0'	0°	21"	15" HDPE	17.6"	Hole 20	20"	20"	-1.25"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 											
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 3636 lb Volume (Net): 0.93cu.yd	
