



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:24 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 61 ST-CI											
P1 MH048BA42		MH BASE T/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE T/n - 42" 1) CASTING - HOE 525 SET FLAT GRATE (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 26"						0 lb 1300 lb 3798 lb 442 lb 0 lb 0 lb 0 lb ----- 5540 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)). 5. CITY OF BGKY-CBI TYPE F. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 706.93'		Rim to Invert: 5'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	701.93'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 2	701.93'	180°	91.125"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

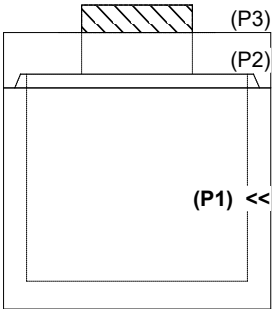

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 26"
Up(_): -2.5"



Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(_): -2.5"


UPSIDE-DOWN VIEW (int. dimensions)

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 26"
Up(_): -2.5"



Invert: 1
Degree: 0°
Horz: 0"
Hole: 26"
Up(_): -2.5"

INSIDE WALL DIMENSIONS

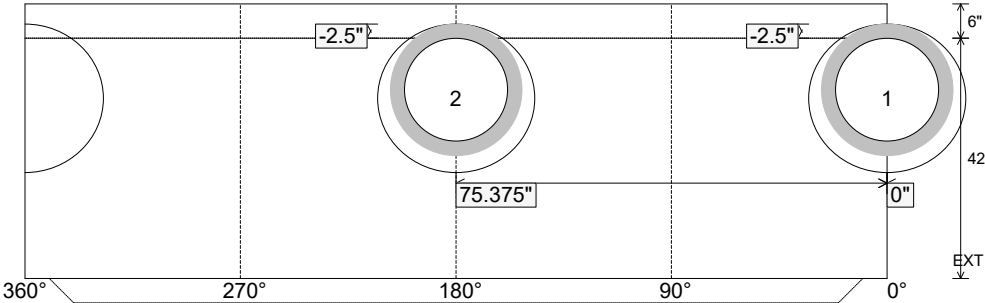

(P1)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 42" Height (Ext): 48"	Weight (Net): 3798 lb Volume (Net): 0.97cu.yd
----------------------------------	---------------------------------	--	--	--
