


Job Name: 25-4212 - Greentree Lane Sewer
Job Location: Mt. Washington, KY
Contractor: Citgo Waterworks

Plant: 100

6/30/2026 12:37:18 PM

Tech: J. Horsley - F

PC: C. Goff



Structure ID: A10 REV.A

P1 MH060BAVF

MH BASE Custom Ht

- P4) 24" - CASTING HEIGHT - 4.75"
P3) 48" - ECC CONE w/ 24" HOLE NO STEP - 24"
P2) 60" - MH Transition Slab 48" Hole - 13"
P1) 60" - MH BASE Custom Ht - 58"
1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 60" - MH INVERT CHANNEL - FULL HEIGHT
1) SPECIAL EXTERNAL COATING - CARBOLINE 300M
1) 60" - Conseal CS-102 1.00" (Double)
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) Kor-N-Seal2 - S206-22
179.3 SqFt) Carboline Bitumastic 300M [EXT]

- Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS.
4. CASTING SUPPLIED BY OTHERS.
5. CARBOLINE 300M >>EXTERIOR COATING ONLY<<
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- TRANSITION SLAB (As .31) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.




Structure Total: 14580 lb

Rim: 694.04' Rim to Invert: 8.17' Slack: 0.294" Sump: 2.004" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	685.87'	0°	0"	18" PVC SDR35	18.75"	Kor-N-Seal2 S206-22	22"	22.525"	0.004"	0"
Invert 2	685.97'	180°	113.097"	18" PVC SDR35	18.75"	Kor-N-Seal2 S206-22	22"	22.525"	1.204"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

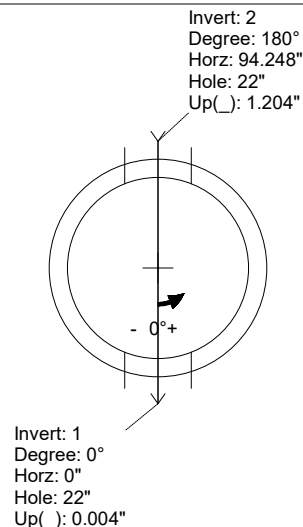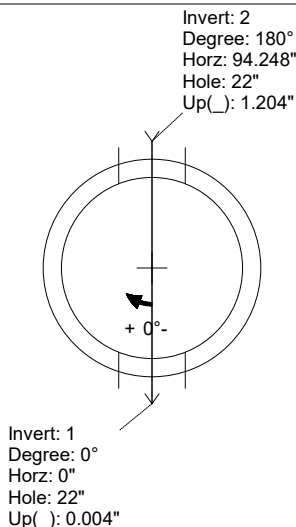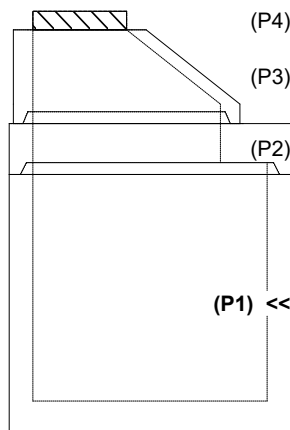

INSIDE WALL DIMENSIONS

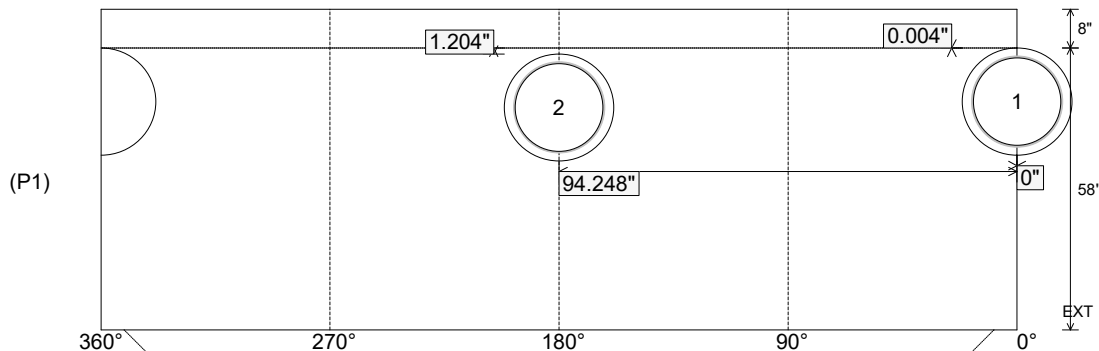

Coating (Int):
Coating (Ext): Carboline Bitumastic 300M

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 8"

Height (Int): 58"
Height (Ext): 66"

Weight (Net): 8397 lb
Volume (Net): 2.14cu.yd


Job Name: 25-4212 - Greentree Lane Sewer
Job Location: Mt. Washington, KY
Contractor: Citgo Waterworks

Plant: 100

6/30/2026 12:37:18 PM

Tech: J. Horsley - F

PC: C. Goff



Structure ID: A10 REV.A

P1 MH060BAVF

MH BASE Custom Ht

- P4) 24" - CASTING HEIGHT - 4.75"
P3) 48" - ECC CONE w/ 24" HOLE NO STEP - 24"
P2) 60" - MH Transition Slab 48" Hole - 13"
P1) 60" - MH BASE Custom Ht - 58"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 60" - MH INVERT CHANNEL - FULL HEIGHT
1) SPECIAL EXTERNAL COATING - CARBOLINE 300M
1) 60" - Conseal CS-102 1.00" (Double)
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) Kor-N-Seal2 - S206-22
179.3 SqFt) Carboline Bitumastic 300M [EXT]

- 0 lb
1550 lb
1928 lb
8397 lb
0 lb
0 lb
2692 lb
0 lb
0 lb
0 lb
0 lb
13 lb
0 lb
- Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS.
4. CASTING SUPPLIED BY OTHERS.
5. CARBOLINE 300M >>EXTERIOR COATING ONLY<<
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- TRANSITION SLAB (As .31) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

Structure Total: 14580 lb




**INVERT CHANNEL DRAWING
FULL HEIGHT INVERT**

Rim: 694.04' Rim to Invert: 8.17' Slack: 0.294" Sump: 2.004" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	685.87'	0°	0"	18" PVC SDR35	18.75"	Kor-N-Seal2 S206-22	22"	22.525"	0.004"	0"
Invert 2	685.97'	180°	113.097"	18" PVC SDR35	18.75"	Kor-N-Seal2 S206-22	22"	22.525"	1.204"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

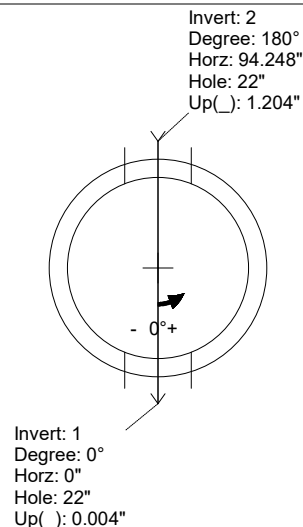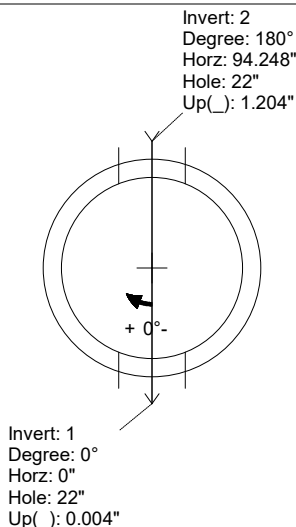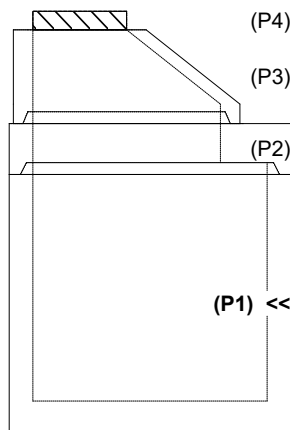

INSIDE WALL DIMENSIONS

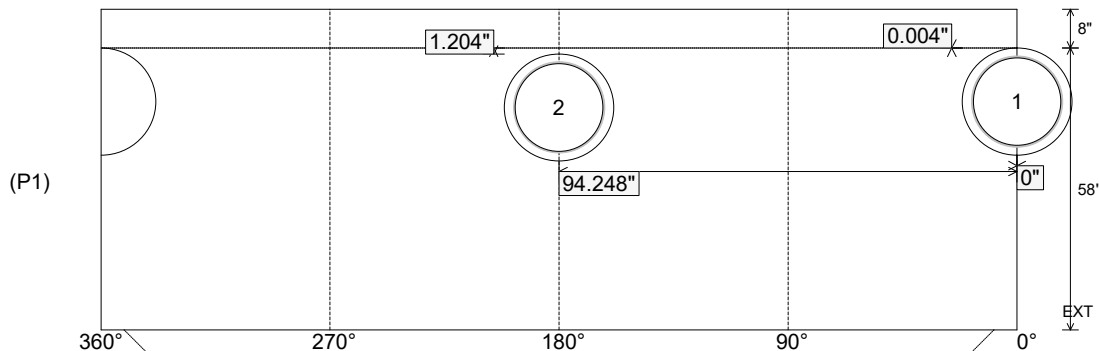

Coating (Int):
Coating (Ext): Carboline Bitumastic 300M

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 8"

Height (Int): 58"
Height (Ext): 66"

Weight (Net): 8397 lb
Volume (Net): 2.14cu.yd
