

Job Name: 26-1733 - Liberty Power Station
Job Location: Liberty, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/20/2026 8:30:33 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: CB-38

P2 MH060LD13CC

MH FLAT TOP w/24" Ctr. Hole

- P3) 24" - CASTING HEIGHT - 4"
P2) 60" - MH FLAT TOP w/24" Ctr. Hole - 13"
P1) 60" - MH BASE - 72"
1) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 46
6) MH Step ML-10-TDS-NCR - 10"

Structure Total:



0 lb
2674 lb
8388 lb
0 lb
0 lb
0 lb
0 lb
11062 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

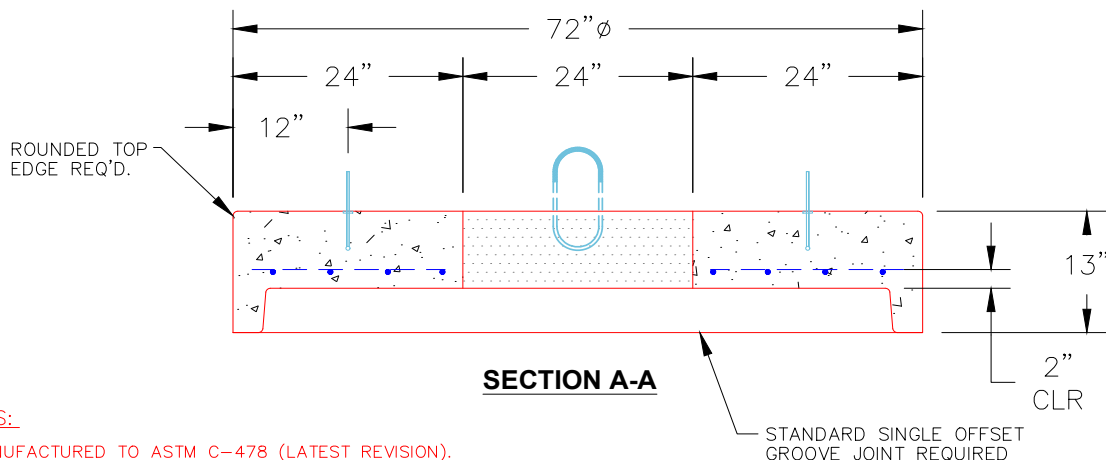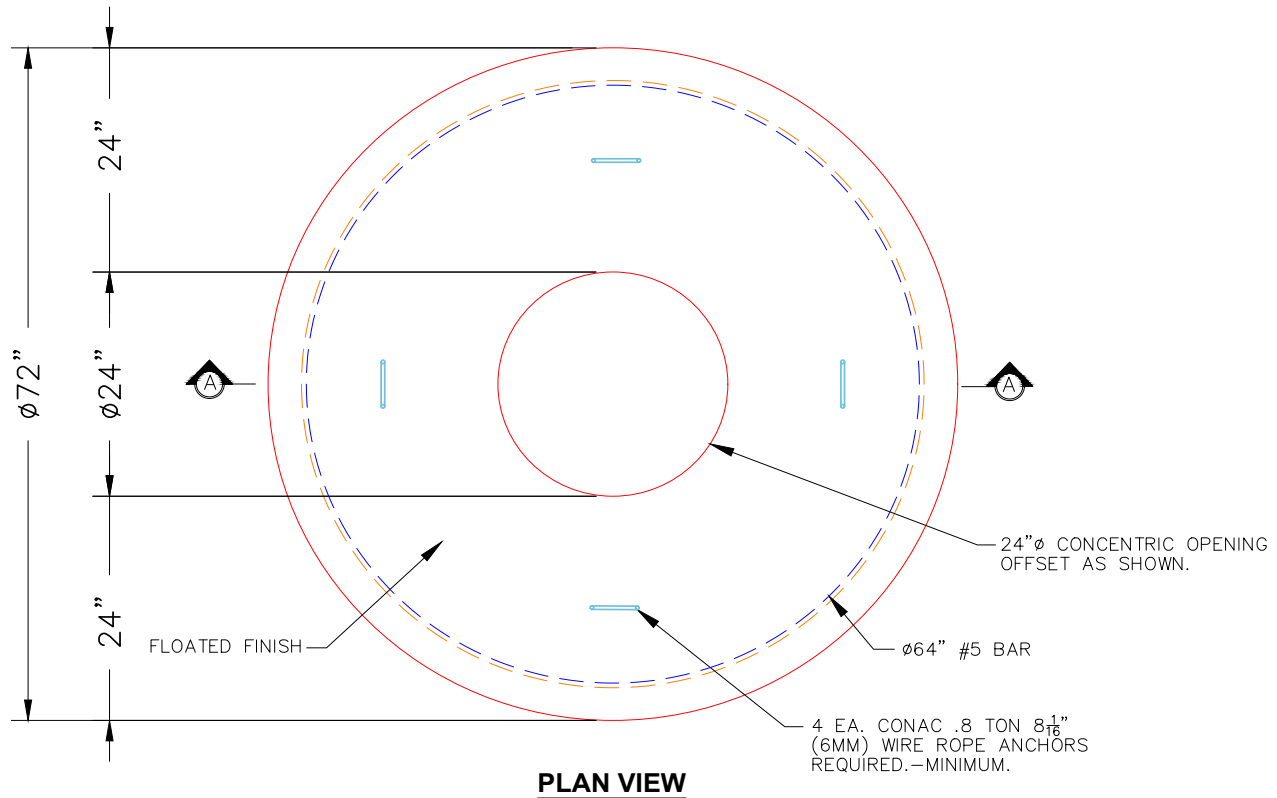

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2674 lb
Volume (Net): 0.68cu.yd
