

Job Name: 26-1733 - Liberty Power Station
Job Location: Liberty, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/20/2026 8:30:34 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: MH-2

P2 MH048CN24



ECC CONE w/ 24" HOLE

- P3) 24" - CASTING HEIGHT - 5"
P2) 48" - ECC CONE w/ 24" HOLE - 24"
P1) 48" - MH BASE Custom Ht - 40"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 32
5) MH Step ML-10-TDS-NCR - 10"

0 lb
1550 lb
3398 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 4948 lb

Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIES BY OTHERS.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

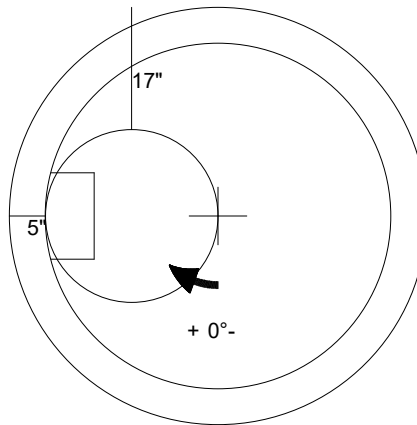

48" - ECC CONE w/ 24" HOLE - 24" - (P2)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 24"

Weight (Net): 1550 lb
Volume (Net): 0.33cu.yd
