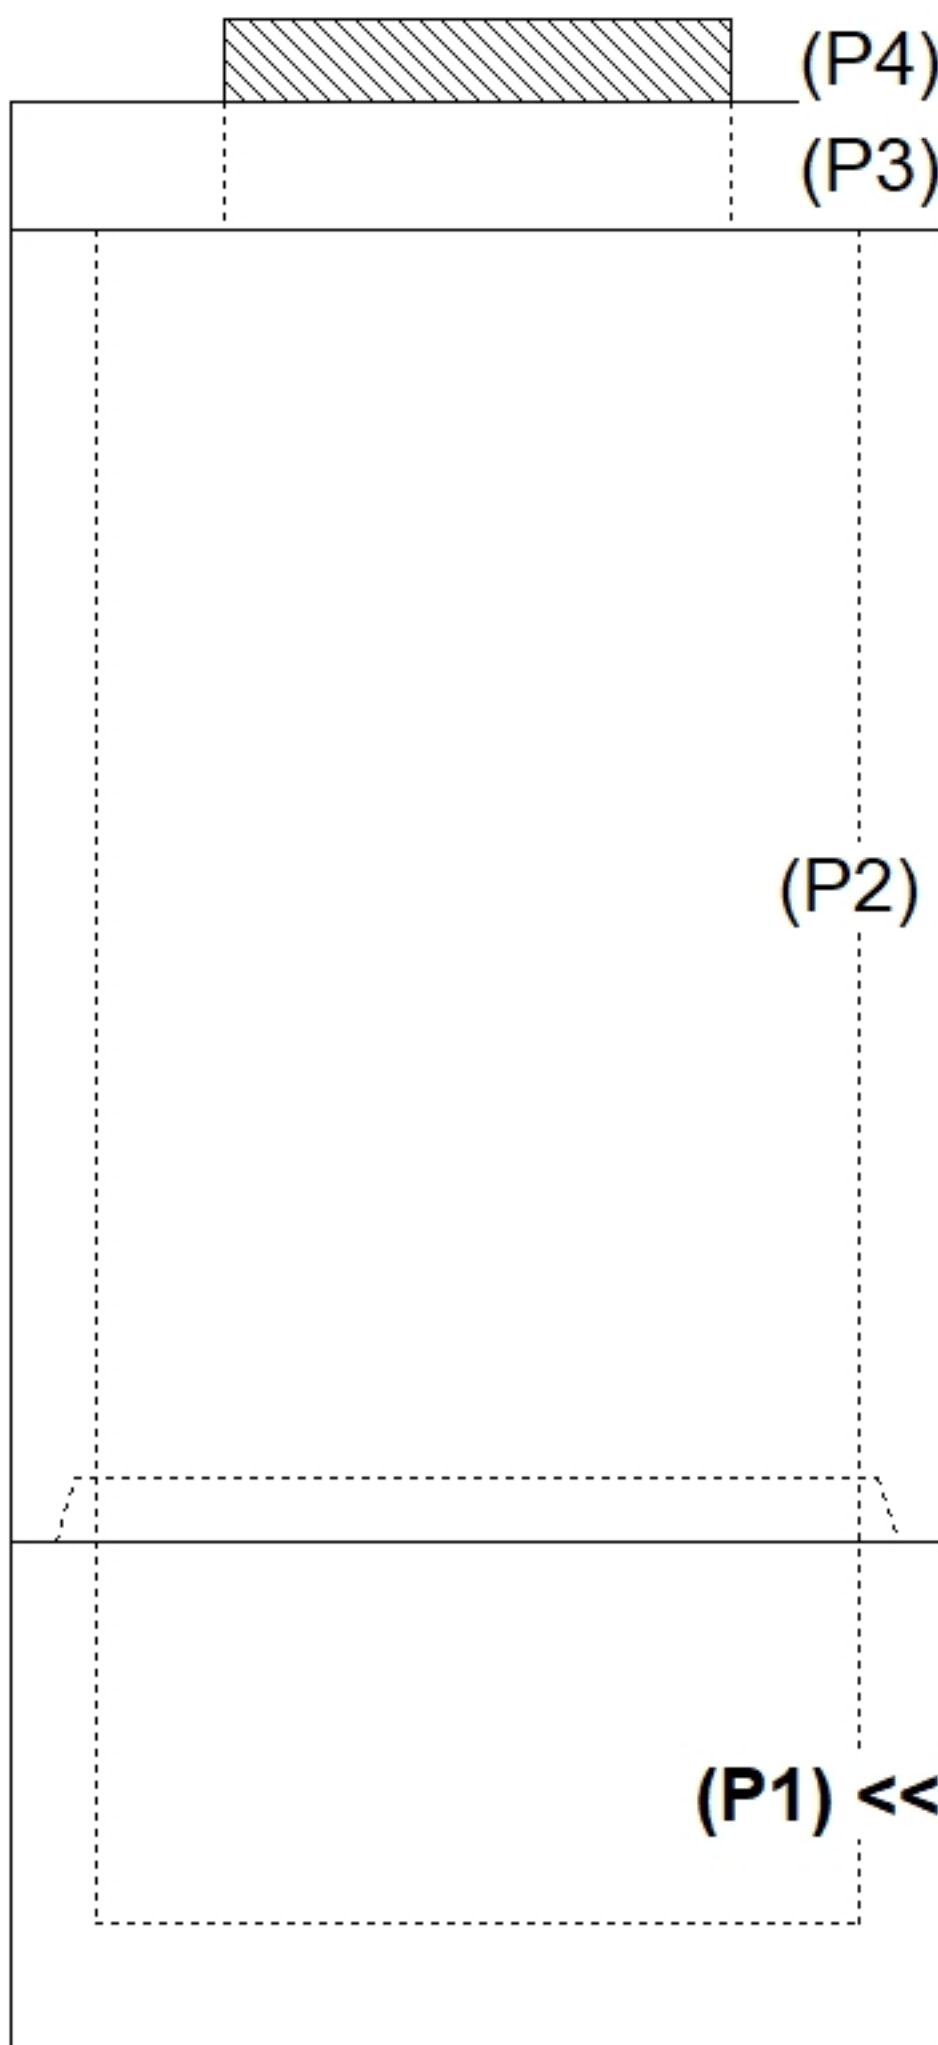
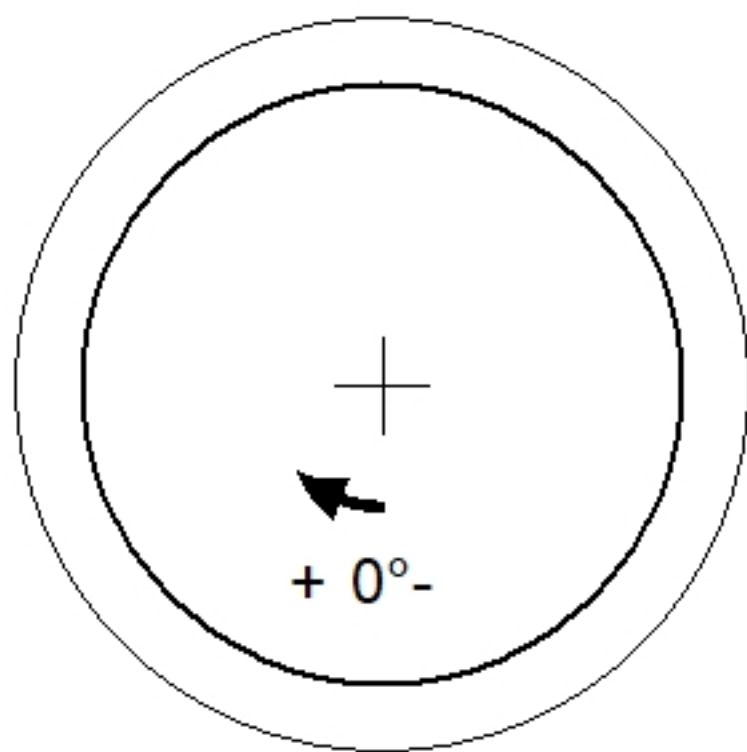


Job Name: 26-3183 ADS Freedom's Way Commons Job Location: Shelbyville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 8/14/2026 12:26:08 PM		Tech: S. Felletter PC: T. Ryan				
Structure ID: STR-23											
P1		MH036BA18		MH BASE T/n							
P4) 24" - CASTING HEIGHT - 4" P3) 36" - MH FLAT TOP w/ 24" Ctr. Hole F/F - 6" P2) 36" - MH RISER Custom Ht F/G - 62" P1) 36" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-285 F/C Storm 2) 36" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 16					0 lb 538 lb 2476 lb 1525 lb 0 lb 0 lb 0 lb 284 lb 0 lb 0 lb 0 lb ----- 4823 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-285 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 733.7'		Rim to Invert: 2.95'		Slack: 0.36"		Sump: 54.96"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimenions)					
											
INSIDE WALL DIMENSIONS											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 4" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 1525 lb Volume (Net): 0.39cu.yd		
