

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)

Job Location: Indiana, KY

Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:09:27 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 73

P1 BX24300808VF

BOX BASE 8inW, 8inF, Variable Ht T/n

P4) 15" x 27" - P.I.P. - BY OTHERS - 8"

P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"

P2) 24" x 30" - BOX RISER 8inW F/G - 30"

P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38"

2) 24" x 30" - Conseal CS-102 1.00"

1) 15" x 27" - Conseal CS-102 1.00"

1) Hole - 18

2) Hole - 4

0 lb

963 lb

2803 lb

4636 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 8402 lb

Structure Notes:

\*\* KYTC STATE PROJECT \*\*

1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS


3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS


Rim: 551.7' Rim to Invert: 7' Slack: 0" Sump: 0" Step Position:

| Position | Elev   | Angle | Ext. (cw) | Pipe     | Pipe OD | Connector | Hole | Horz Size | Up ( ) | Offset |
|----------|--------|-------|-----------|----------|---------|-----------|------|-----------|--------|--------|
| Invert 1 | 544.7' | 90°   | 23"       | 12" HDPE | 14.5"   | Hole 18   | 18"  | 18"       | -3"    | 0"     |
| Invert 2 |        |       |           |          |         |           |      |           |        |        |
| Invert 3 |        |       |           |          |         |           |      |           |        |        |
| Invert 4 |        |       |           |          |         |           |      |           |        |        |
| Invert 5 |        |       |           |          |         |           |      |           |        |        |
| Invert 6 |        |       |           |          |         |           |      |           |        |        |
| Invert 7 |        |       |           |          |         |           |      |           |        |        |
| Invert 8 |        |       |           |          |         |           |      |           |        |        |


RIGHT-SIDE UP VIEW (int. dimensions)

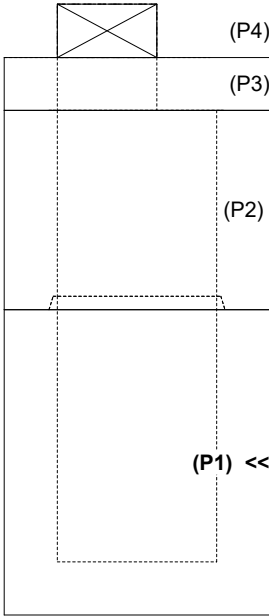

UPSIDE-DOWN VIEW (int. dimenions)



INSIDE WALL DIMENSIONS

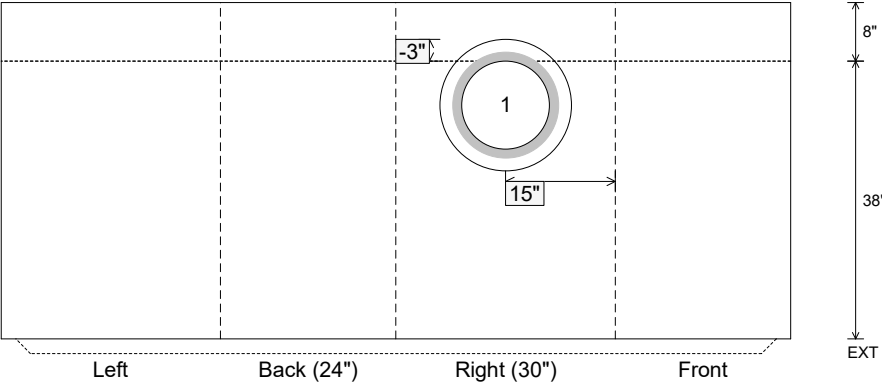

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 38"

Height (Ext): 46"

Weight (Net): 4636 lb

Volume (Net): 1.18cu.yd
