



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:02 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 17 ST-CI											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 49" 1) CASTING - HOE 525 SET FLAT GRATE (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 26"						0 lb 1300 lb 2515 lb 4287 lb 442 lb 0 lb 0 lb 0 lb ----- 8544 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)). 5. CITY OF BGKY-CBI TYPE F. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 678.02' Rim to Invert: 8.66' Slack: 0.92" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	669.36'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 2	669.36'	90°	45.5"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

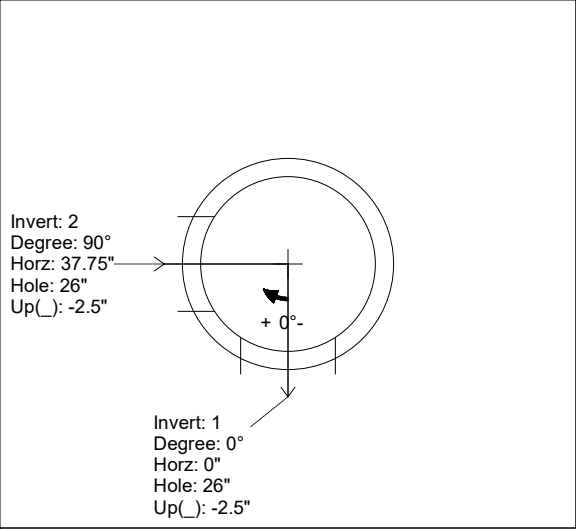

UPSIDE-DOWN VIEW (int. dimenions)

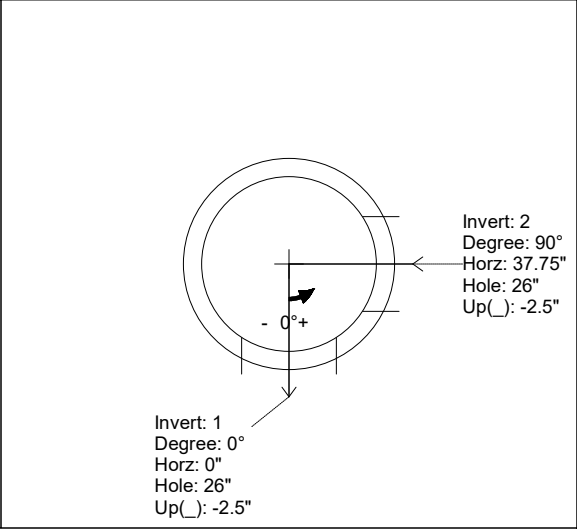

INSIDE WALL DIMENSIONS

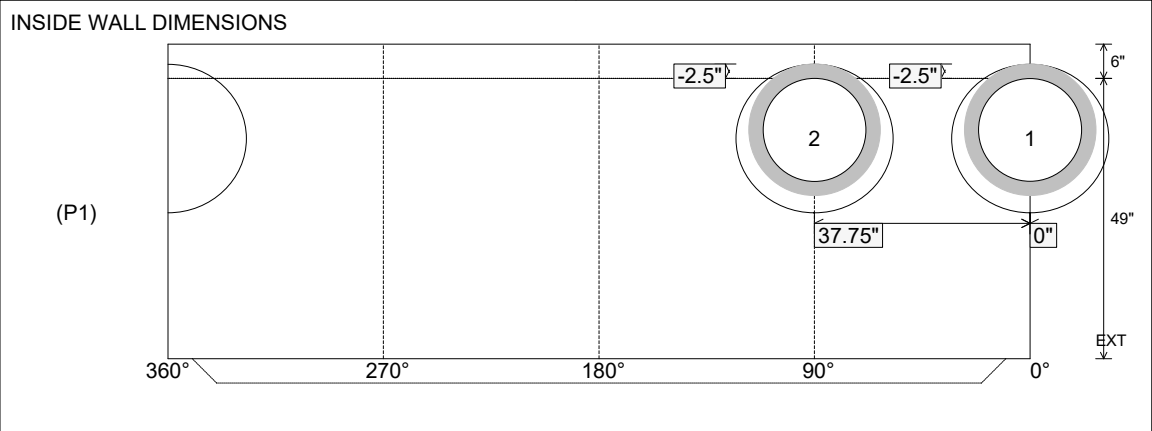

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 49" Height (Ext): 55"	Weight (Net): 4287 lb Volume (Net): 1.1cu.yd
----------------------------------	---------------------------------	--	--	---
