

Job Name: 25-1431P5 - Georgetown Commons Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.					Plant: Beaver Dam		Tech: J. Horsley					
					7/18/2026 8:59:22 AM		PC: A. Chambers					
Structure ID: SSMH-236 (Base Remake)												
P1 MH048BAVF			MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 36" P1) 48" - MH BASE Custom Ht T/n - 34" 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375-SS F/C Self-Sealing Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285						0 lb 3000 lb 3642 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb ----- Structure Total: 8355 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STEPS 5. INVERT CHANNEL REQUIRED 6. HOE MC-375 FRAME & SELF-SEALING COVER "SANITARY" SUPPLIED BY ICAST ** BASE REMAKE ONLY **				
Rim: 870.85' Rim to Invert: 6.25' Slack: 0" Sump: 2" Step Position:												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	864.6'	0°	0"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	1.125"	0"		
Invert 2	864.7'	200°	101.25"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 34"	Weight (Net): 3642 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 6"	Height (Ext): 40"	Volume (Net): 0.93cu.yd

Job Name: 25-1431P5 - Georgetown Commons Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.					Plant: Beaver Dam 7/18/2026 8:59:22 AM		Tech: J. Horsley PC: A. Chambers				
Structure ID: SSMH-236 (Base Remake)											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP F/G - 36" P1) 48" - MH BASE Custom Ht T/n - 34" 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375-SS F/C Self-Sealing Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285						0 lb 3000 lb 3642 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 2 lb ----- Structure Total: 8355 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STEPS 5. INVERT CHANNEL REQUIRED 6. HOE MC-375 FRAME & SELF-SEALING COVER "SANITARY" SUPPLIED BY ICAST ** BASE REMAKE ONLY **			
Rim: 870.85'		Rim to Invert: 6.25'		Slack: 0"		Sump: 2"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	864.6'	0°	0"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	1.125"	0"	
Invert 2	864.7'	200°	101.25"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

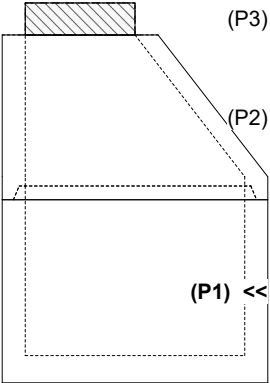


(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

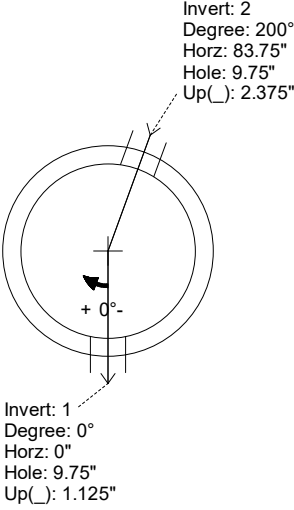


Invert: 2
Degree: 200°
Horz: 83.75"
Hole: 9.75"
Up(): 2.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 9.75"
Up(): 1.125"

UPSIDE-DOWN VIEW (int. dimensions)

INVERT CHANNEL DRAWING

INSIDE WALL DIMENSIONS

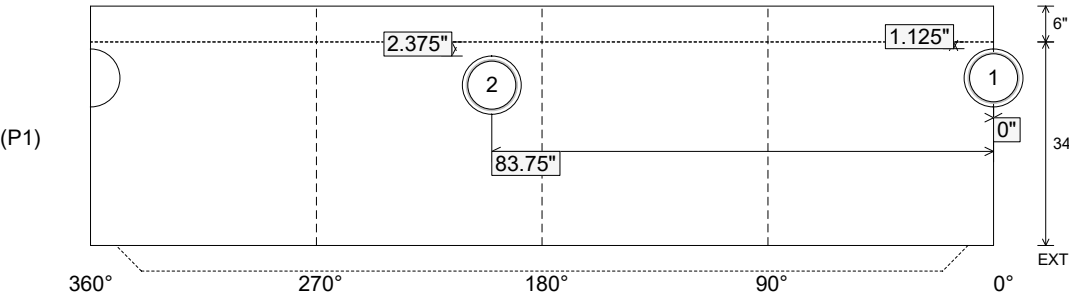

(P1)

360° 270° 180° 90° 0°

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 34" Height (Ext): 40"	Weight (Net): 3642 lb Volume (Net): 0.93cu.yd
----------------------------------	---------------------------------	--	--	--
