

Job Name: 26-1787 - Kroger Expansion
Job Location: Murray, KY
Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:26:56 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: C7 ST-CI

P3 BX048072-08LD08-SP

CB FLAT TOP 8"W w/30"x36" HOLE F/F

- P5) 6" x 36" - CASTING - Curb Back/Hood - 3.50"
P4) 30" x 36" - CASTING - Frame&Grate F/F - 6.50"
P3) 48" x 72" - CB FLAT TOP 8"W w/30"x36" HOLE F/F - 8"
P2) 48" x 72" - BOX RISER 8inW, Variable Ht F/G - 72"
P1) 48" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 65"
1) SECONDARY POUR
1) CASTING - JBS 2064-V SET (F/G/H)
2) 48" x 72" - Conseal CS-102 1.00"
2) Hole - 30
1) Hole - 20
4) Hole - 6
11) MH Step ML-10-TDS-NCR - 10"

0 lb
0 lb
3056 lb
12846 lb
14037 lb
0 lb
500 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 30439 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (JBS 2064 F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

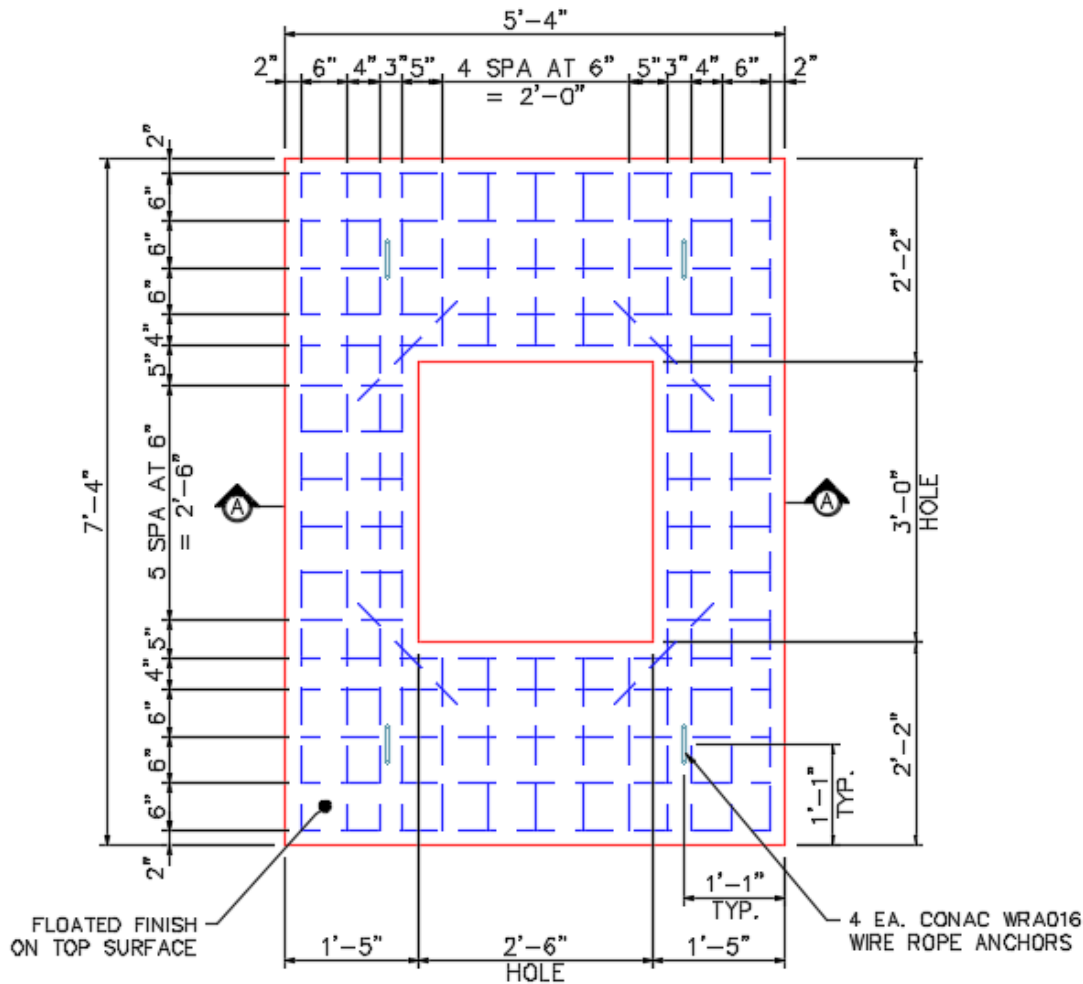

PLAN VIEW



SECTION A-A

#5 BAR CUT LIST

- 8 EA. @ 74" LG.
- 5 EA. @ 22" LG.
- 10 EA. @ 60" LG.
- 12 EA. @ 13" LG.
- 4 EA. @ 16" LG.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 3056 lb
Volume (Net): 0.78cu.yd
