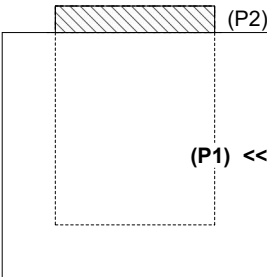

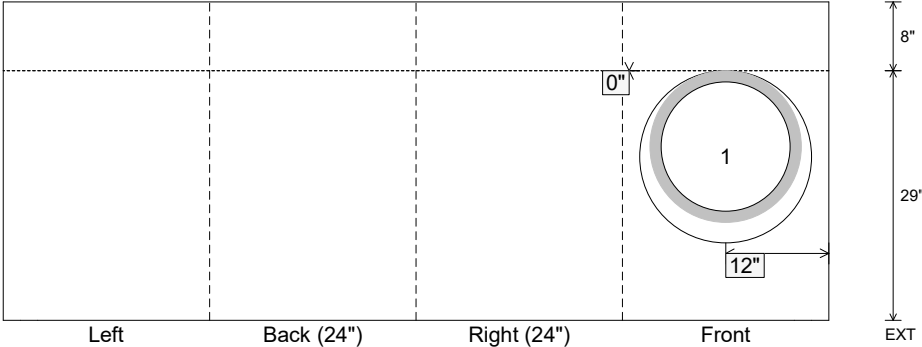


Job Name: 26-2564 - Taubensee Steel Job Location: Henderson, KY Contractor: K&K Excavating Inc.					Plant: 100 6/24/2026 6:15:13 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 202 ST-AD											
P1 BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n								
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 29" 1) CASTING - HOE-326-BH F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20						0 lb 3355 lb 289 lb 0 lb 0 lb ----- Structure Total: 3644 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE-326-BH FRAME & BEEHIVE GRATE SUPPLIED BY ICAST			
Rim: 387.25' Rim to Invert: 2.65' Slack: 0.1" Sump: 1.3" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	384.6'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 29" Height (Ext): 37"		Weight (Net): 3355 lb Volume (Net): 0.86cu.yd		
