




Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100 7/24/2026 12:45:30 PM		Tech: Jared - A PC: C. Goff				
Structure ID: Wet Well											
P2 MH072RSVF			MH RISER Custom Ht								
P4) 30" x 48" - HATCH (CAST FLUSH) - 3" P3) 72" - MH FLAT TOP w/30"x48" Hatch - 15" P2) 72" - MH RISER Custom Ht - 69" P1) 72" - MH BASE EF Cust. Ht. 08"F (8"EF =102"OD) - 24" 1) HATCH (Alum.) - HALLIDAY S1R 30"x48" 1) This Structure Includes a Cast-in Item - Halliday S1R 30" x 48" Hatch (Supplied by iCast) 2) JOINT WRAP - 12" WD x 072" MAC WRAP 1) SECONDARY POUR - Extended Flange 2) 72" - Conseal CS-231 1.00" (Double) 3) PSX - 8QRS-S NYLO 1) PSX - 12M NYLO					100 lb 4186 lb 9900 lb 8984 lb 71 lb 0 lb 0 lb 0 lb 0 lb 20 lb 8 lb ----- Structure Total: 23269 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: - FLAT LID TOP MAT: #4 BAR @ 18" C.C. E.W. (GRADE 60) - FLAT LID BOTTOM MAT: #4 BAR @ 9" C.C. E.W. (GRADE 60) - BASE WALLS & RISER: PER ASTM A615 - BASE FLOOR: #5 BAR @ 8" C.C. E.W. (GRADE 60) 4. NO STEPS 5. HALLIDAY S1R 30" X 48" HATCH SUPPLIED BY ICAST - TO BE CAST INTO FLAT LID				
Rim: 786.5'		Rim to Invert: 5.5'		Slack: 0"		Sump: 42"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	782.38'	0°	-12.161"	3" DI	3.5"	PSX 8QRS-S NYLO	8"	8.513"	27.06"	-12"	
Invert 2	782.38'	0°	12.161"	3" DI	3.5"	PSX 8QRS-S NYLO	8"	8.513"	27.06"	12"	
Invert 3	781'	0°	0"	3" DI	3.5"	PSX 8QRS-S NYLO	8"	8.017"	10.5"	0"	
Invert 4	781.1'	180°	135.088"	8" DI	9"	PSX 12M NYLO	12"	12.056"	12.2"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

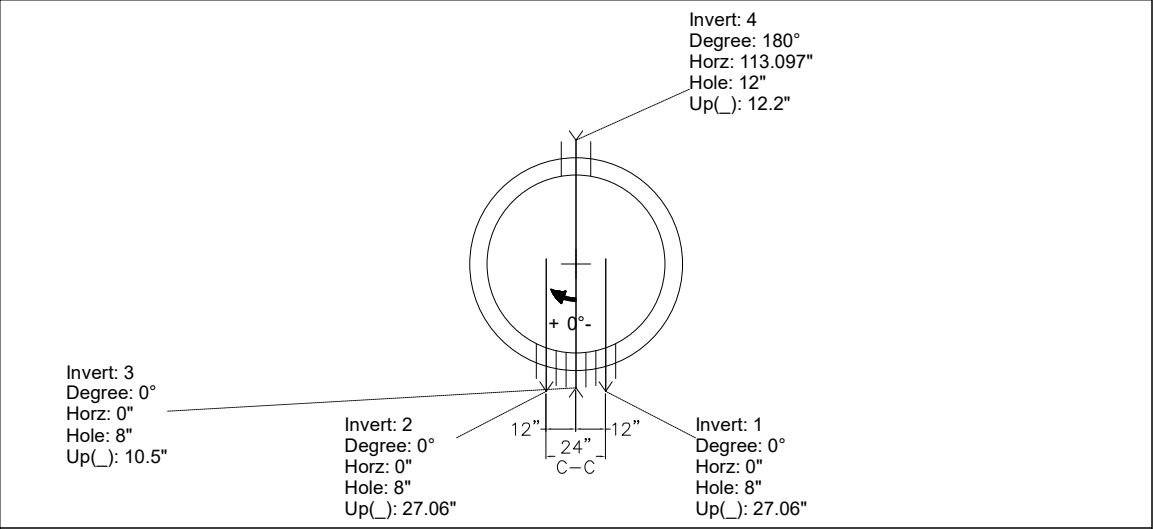

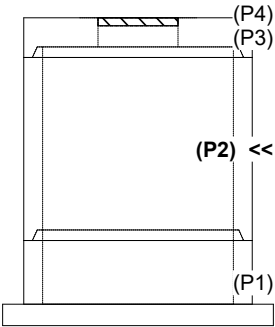

INSIDE WALL DIMENSIONS

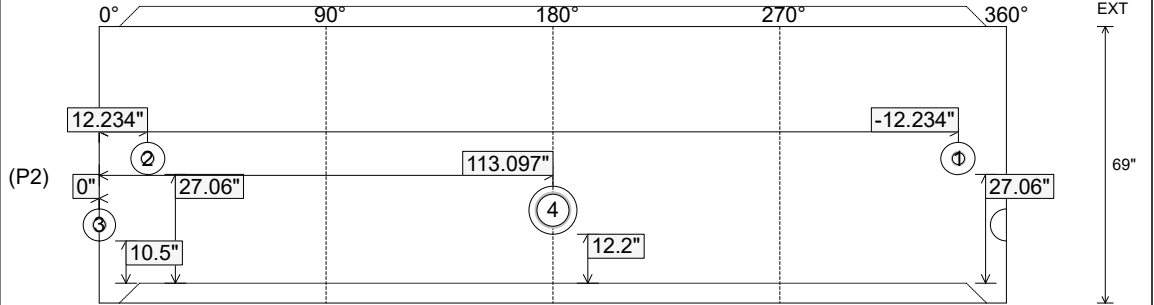

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 7" Floor Height: 0"	Height (Int): 69" Height (Ext): 69"	Weight (Net): 9900 lb Volume (Net): 2.53cu.yd
----------------------------------	------------------------------------	--	--	--
