
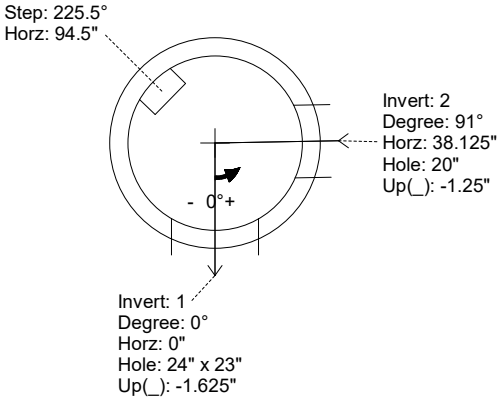
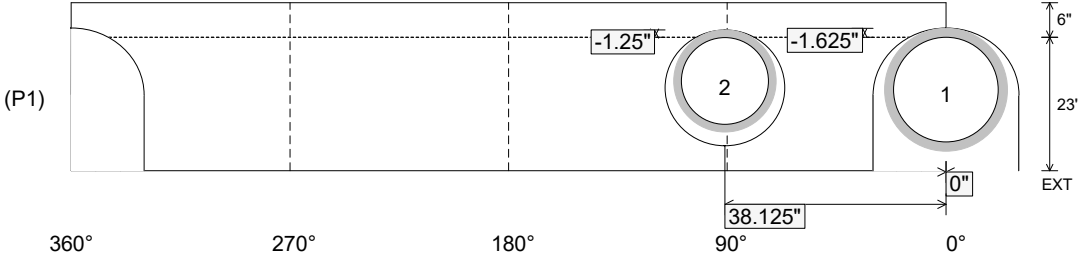


Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:23:27 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: C6 ST-MH											
P1		MH048BAVF		MH BASE Custom Ht F/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 23" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 24"x23" 1) Hole - 20 2) MH Step ML-10-TDS-NCR - 10"						0 lb 1286 lb 2570 lb 271 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4127 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS AT 225.5 DEGREES 5. HOE MC-375 FRAME & COVER "STORM" SUPPLIED BY ICAST			
Rim: 531.06' Rim to Invert: 3.13' Slack: 0.56" Sump: 0" Step Position: 225.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	527.93'	0°	0"	18" HDPE	21.2"	DOGHOUSE INVRTD 24"x23"	24" x 23"	25.133"	-1.625"	0"	
Invert 2	527.93'	91°	46"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 23" Height (Ext): 29"		Weight (Net): 2570 lb Volume (Net): 0.66cu.yd	
