

Job Name: 26-3054 ADS Couchville Online
Job Location: Nashville, TN
Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam

7/23/2026 12:30:22 PM

Tech: S. Felletter

PC: T. Ryan



Structure ID: WQU1

P5 MH120LD18

MH FLAT LID w/24in CON Hole F/G



- P6) 24" - CASTING HEIGHT - 7"
P5) 120" - MH FLAT LID w/24in CON Hole F/G - 18"
P4) 120" - MH RISER T/G - 24"
P3) 120" - MH RISER T/G - 96"
P2) 120" - MH RISER T/G - 84"
P1) 120" - MH BASE T/n - 24"
1) ASSEMBLY REQUIRED - BRACKETS ONLY
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-375 F/C Storm
4) 120" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) Hole - 34

- 0 lb
16678 lb
9117 lb
34772 lb
31909 lb
25064 lb
0 lb
0 lb
0 lb
271 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-375 F/C "STORM").
4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE.
5. ASSEMBLY REQUIRED - BRACKETS ONLY.
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Structure Total: 117811 lb

GENERAL NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE 5,000 PSI AT 28 DAYS.
3. REINFORCING: #4 & #5 BAR AS SHOWN (GRADE 60).
4. WEIGHT: 16,678 LBS.

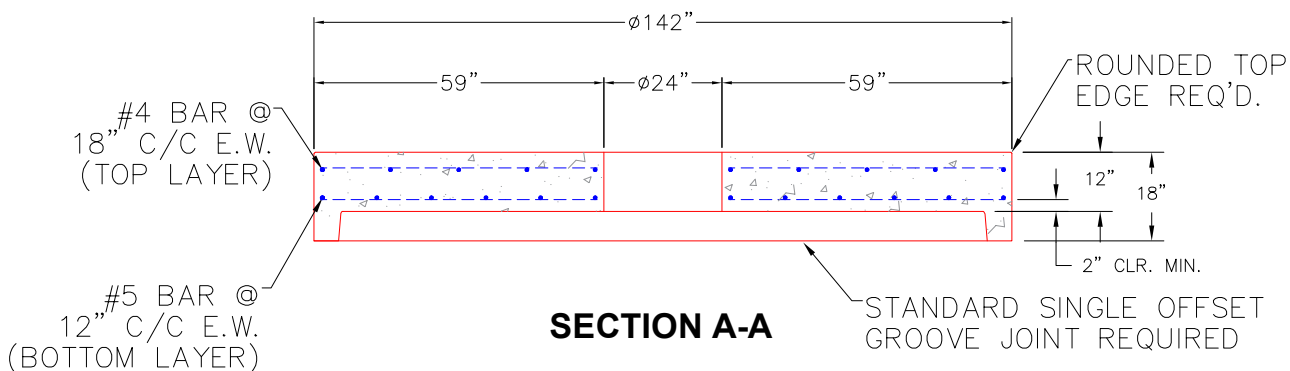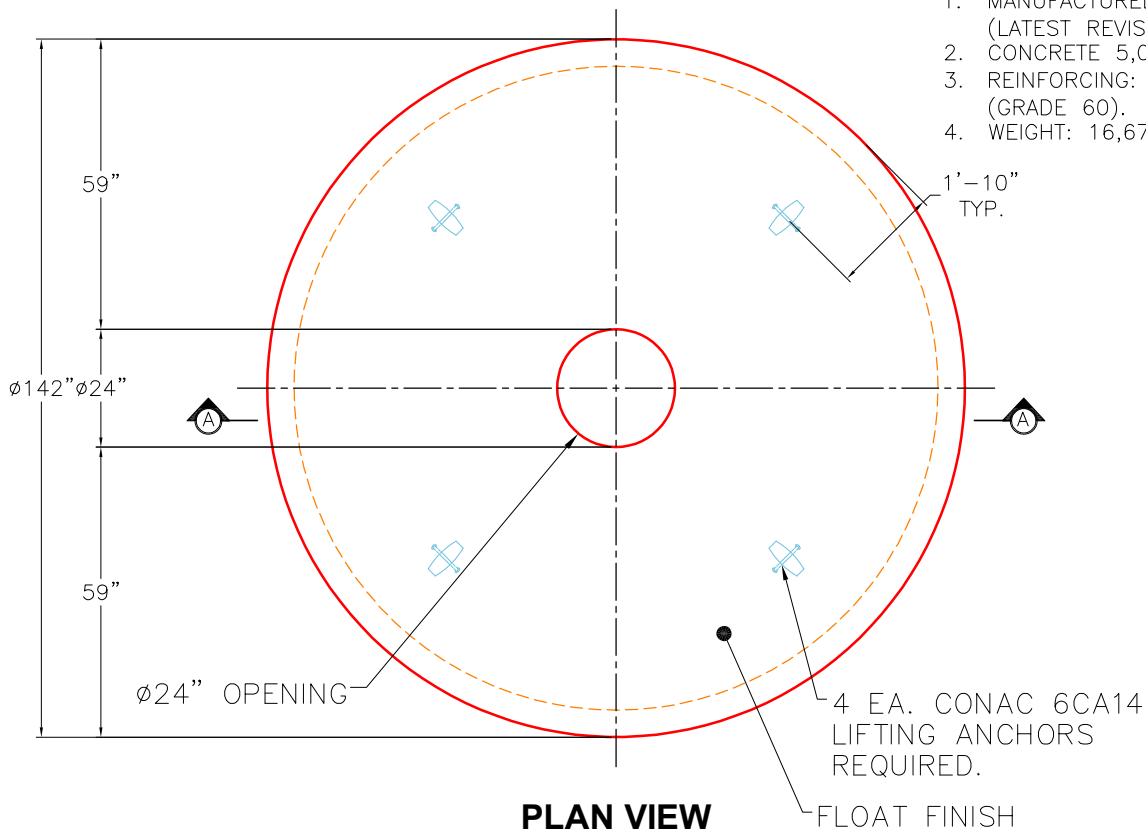

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 11"

Height (Ext): 18"

Weight (Net): 16678 lb
Volume (Net): 4.26cu.yd

Job Name: 26-3054 ADS Couchville Online

Job Location: Nashville, TN

Contractor: ADS Advanced Drainage Systems, Inc.

Plant: Beaver Dam

7/23/2026 12:30:37 PM

Tech: S. Felletter

PC: T. Ryan



Structure ID: WQU2

P4MH120RS24MH RISER T/G

P6) 24" - CASTING HEIGHT - 7"

P5) 120" - MH FLAT LID w/24in CON Hole F/G - 18"

P4) 120" - MH RISER T/G - 24"

P3) 120" - MH RISER T/G - 96"

P2) 120" - MH RISER Custom Ht T/G - 91"

P1) 120" - MH BASE T/n - 24"

1) ASSEMBLY REQUIRED - BRACKETS ONLY

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-375 F/C Storm

4) 120" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

2) Hole - 34

0 lb

16678 lb

9117 lb

34772 lb

34568 lb

25064 lb

0 lb

0 lb

0 lb

271 lb

0 lb

0 lb

0 lb

Structure Total: 120470 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. CASTING BY ICAST (HOE MC-375 F/C "STORM").

4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE.

5. ASSEMBLY REQUIRED - BRACKETS ONLY.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- RISER/WALLS (As .36)

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 554.82'

Rim to Invert: 8.2'

Slack: 0.4"

Sump: 162"

Step Position: 0°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

(P6)


(P5)

(P4) <<

(P3)

(P2)

(P1)

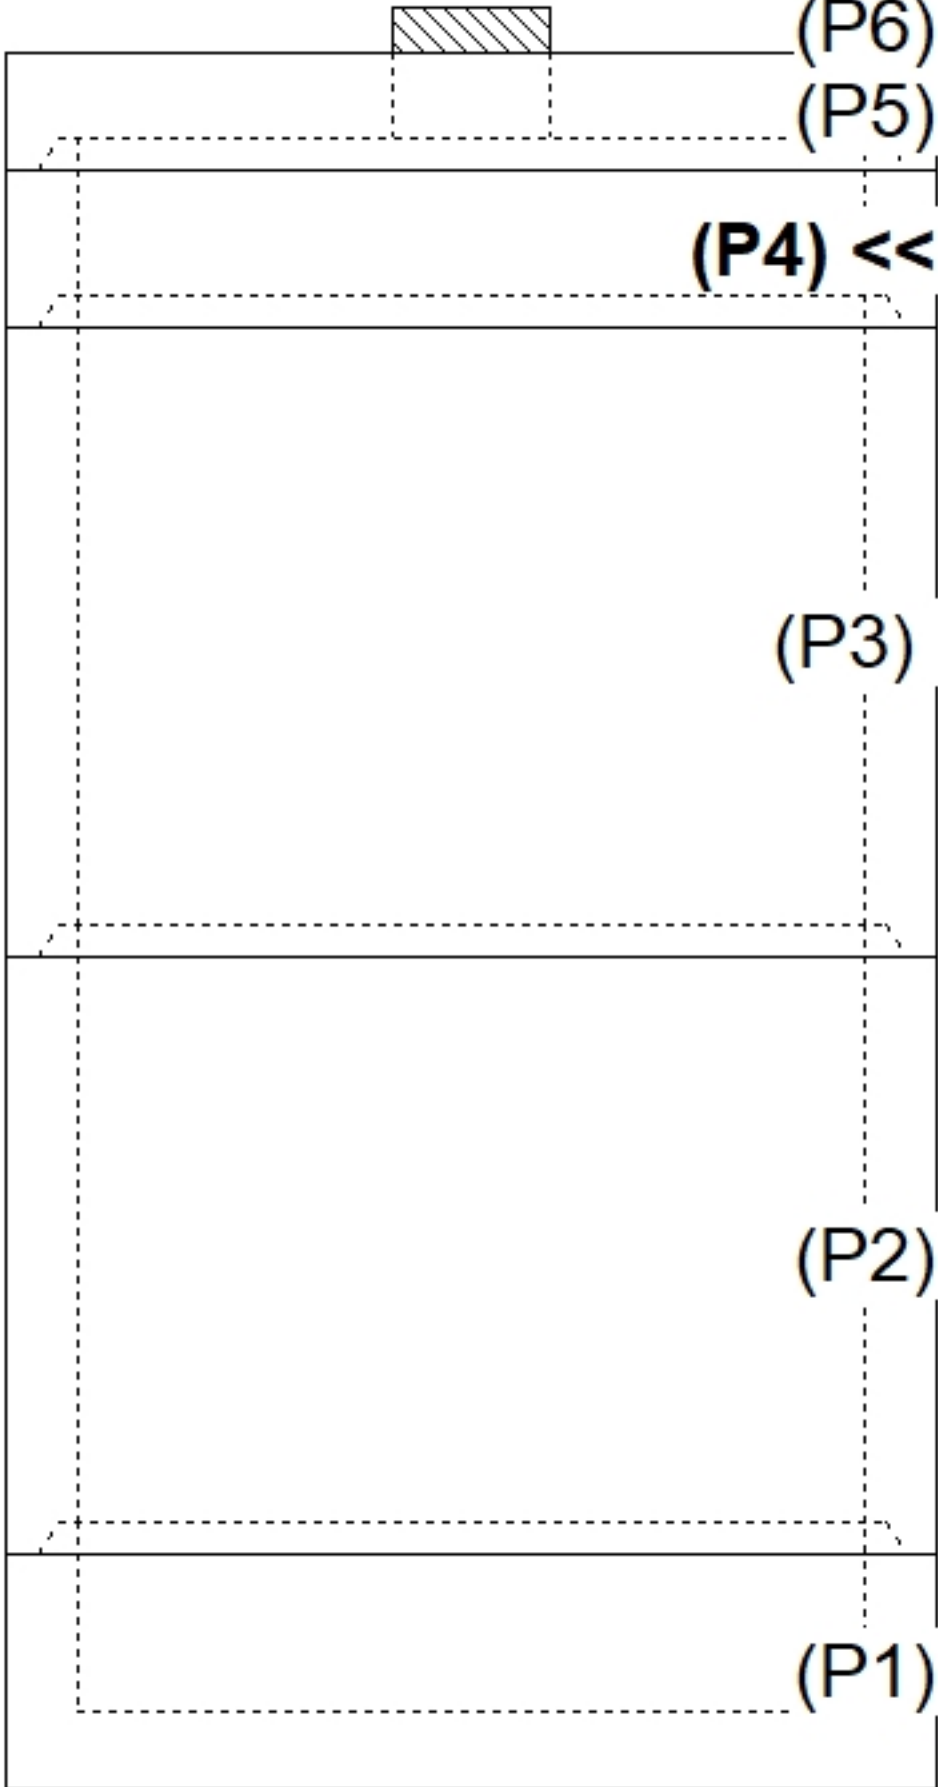

INSIDE WALL DIMENSIONS

0°


90°

180°

270°

360°

(P4)

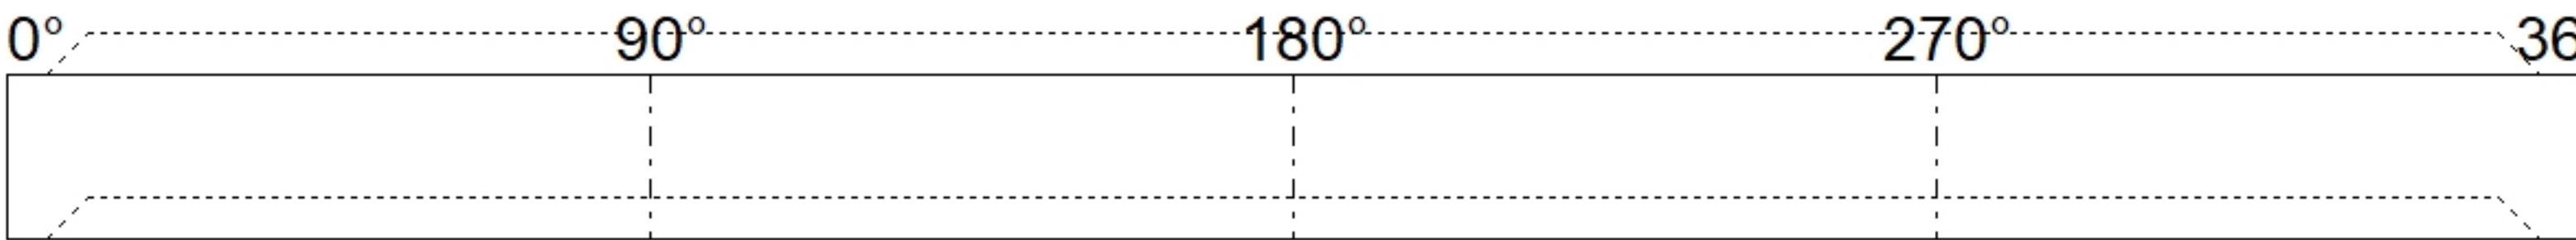

EXT 24"

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: Groove

Wall Thickness: 11"

Floor Height: 0"

Height (Int): 24"

Height (Ext): 24"

Weight (Net): 9117 lb

Volume (Net): 2.33cu.yd

Job Name: 26-3046 903454 2026 Street Reconstruction
Job Location: Elk River, MN
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
7/17/2026 1:18:26 PM

Tech: S. Felletter
PC: C. Goff



Structure ID: Riser Set 4

P2 MH036LD10-30ECC

MH FLAT LID w/30in ECC Hole F/G



- P4) 30" - CASTING HEIGHT - 4"
P3) 30" - GRADE RING F/F - 3"
P2) 36" - MH FLAT LID w/30in ECC Hole F/G - 10"
P1) 36" - MH RISER T/F - 54"
1) CVSTENCILING
1) 36" - Conseal CS-102 1.00"
5) MH Step ML-10-TDS-NCR - 10"

0 lb
138 lb
683 lb
2278 lb
0 lb
0 lb
0 lb

Structure Total: 3099 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. 4" CASTING PROVIDED BY OTHERS.
 4. CONTECH'S LOGO TO BE STENCILED ONTO THE OUTSIDE OF THE STRUCTURE.
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)

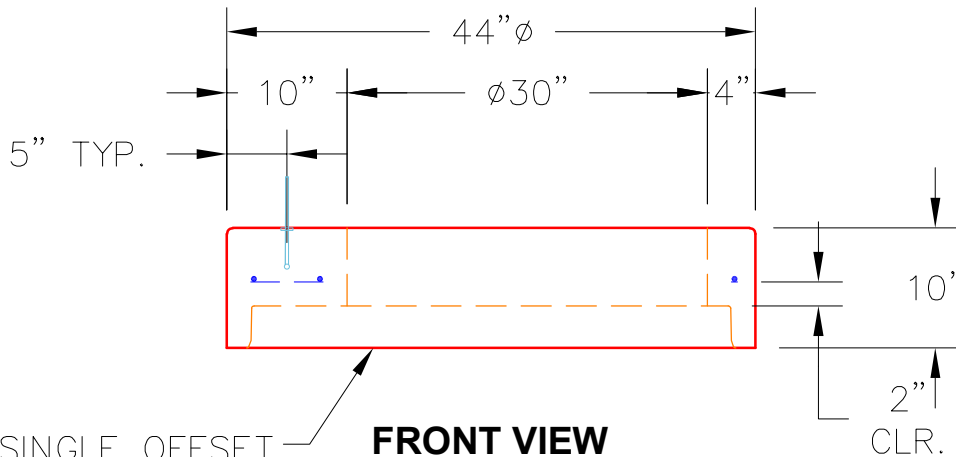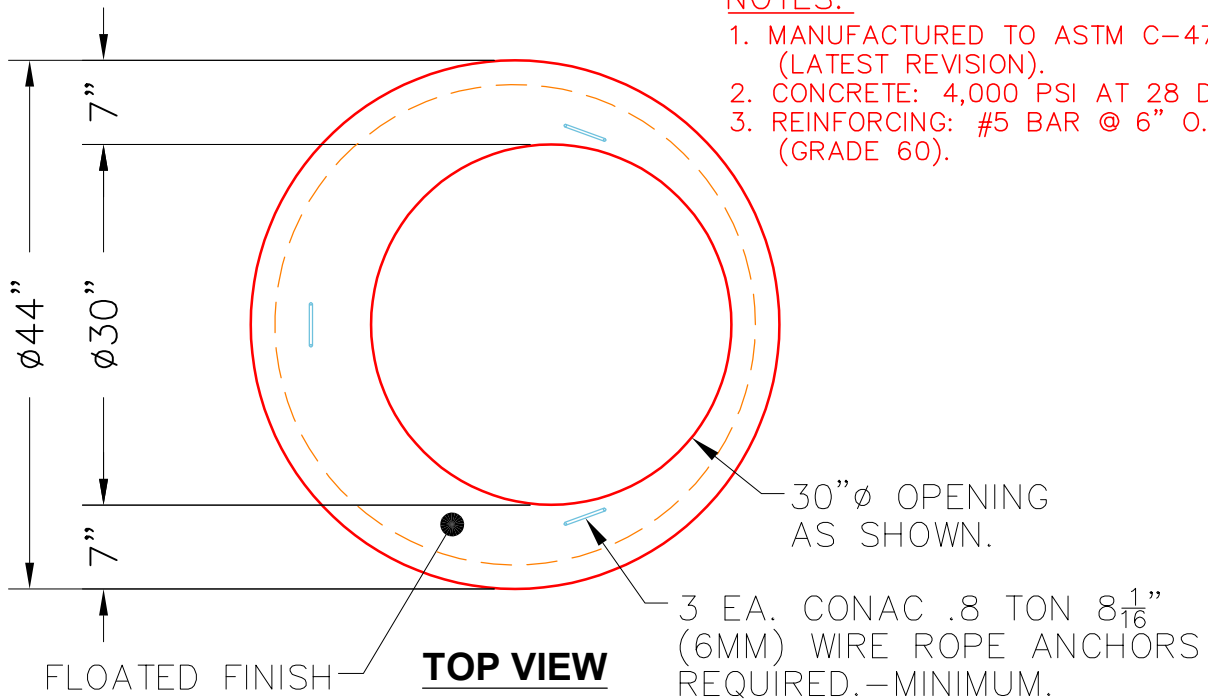

STANDARD SINGLE OFFSET
GROOVE JOINT REQUIRED

Coating (Int):
Coating (Ext):


Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 4"

Height (Ext): 10"


Weight (Net): 683 lb
Volume (Net): 0.17cu.yd

Job Name: 25-4490P1 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/23/2026 12:03:35 PM		Tech: Jared - A PC: Celina Goff			
Structure ID: MH 1-7 (2)										
P1 MH048BA24		MH BASE								
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 30" P2) 48" - MH RISER - 24" P1) 48" - MH BASE - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 2911 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 8365 lb		Structure Notes: . 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 865.25' Rim to Invert: 7.16' Slack: 2.92" Sump: 2" Step Position: 265.5°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	858.09'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	858.19'	171°	86.551"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

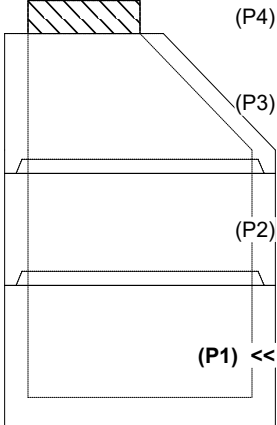


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

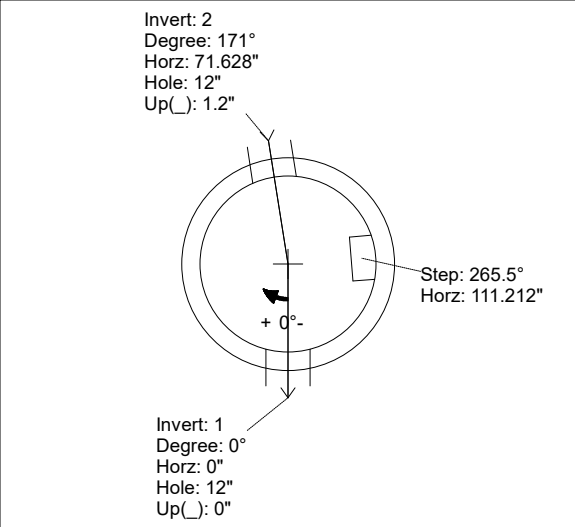

INSIDE WALL DIMENSIONS



UPSIDE-DOWN VIEW (int. dimensions)

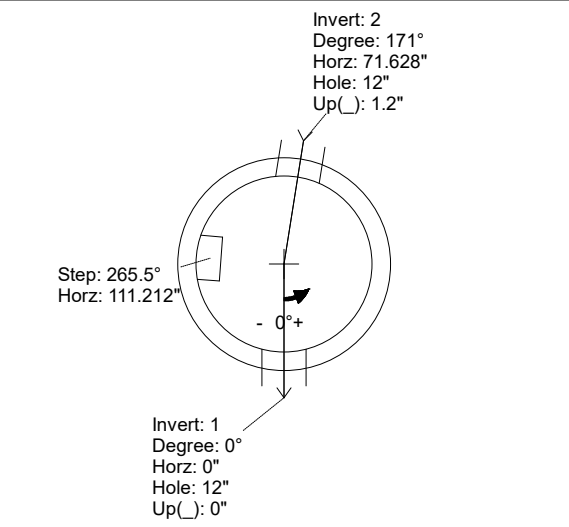


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-4490P1 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/23/2026 12:03:35 PM		Tech: Jared - A PC: Celina Goff						
Structure ID: MH 1-7 (2)													
P1 MH048BA24		MH BASE											
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE - 30" P2) 48" - MH RISER - 24" P1) 48" - MH BASE - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 2911 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 16 lb 0 lb Structure Total: 8365 lb		Structure Notes: 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					INVERT CHANNEL DRAWING	
Rim: 865.25' Rim to Invert: 7.16' Slack: 2.92" Sump: 2" Step Position: 265.5°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	858.09'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"			
Invert 2	858.19'	171°	86.551"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:35 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 17 ST-DCB											
P1 MH048BA30		MH BASE									
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole - 7" P1) 48" - MH BASE - 30" 1) 48" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 20 1) Hole - 16						0 lb 1171 lb 3008 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4179 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 580 F/G) . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1058.88' Rim to Invert: 3.63' Slack: 1.06" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1055.25'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"	
Invert 2	1055.25'	150°	75.922"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 3	1055.25'	233°	117.932"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

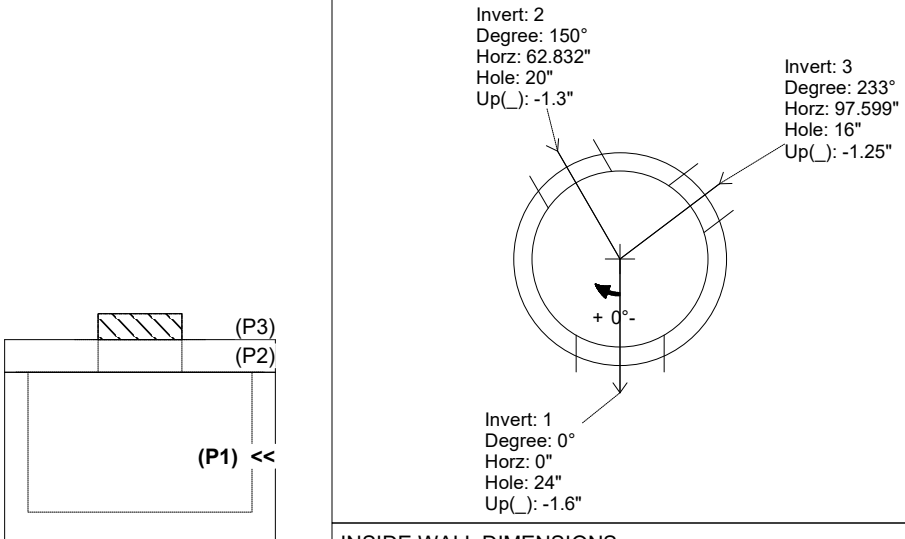

UPSIDE-DOWN VIEW (int. dimensions)

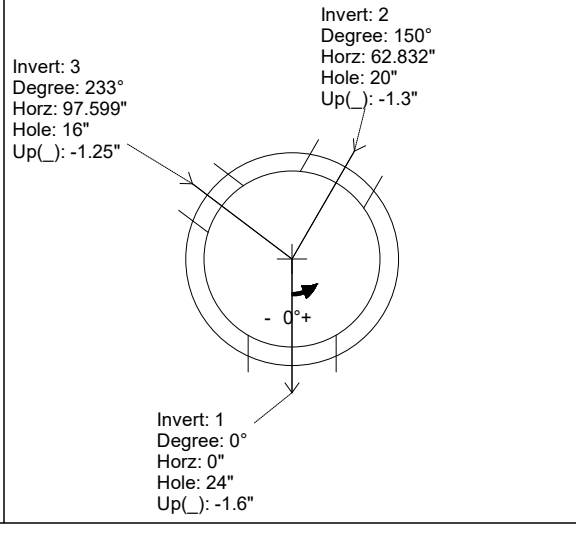

INSIDE WALL DIMENSIONS

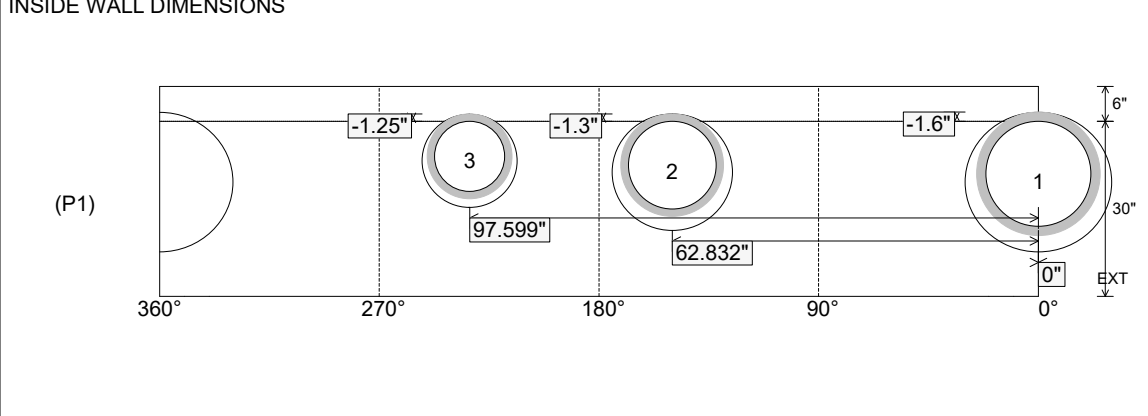

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3008 lb Volume (Net): 0.77cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 25-3241P2 - Buck Hills Subdivision Job Location: Lawrenceburg, KY 40342 Contractor: Edmonson Plumbing & Heating Supply					Plant: 100		Tech: Jared - A			
					7/24/2026 12:43:56 PM		PC: C. Goff			
Structure ID: MH B2										
P1 MH048BAEVF			MH BASE w/FLANGE (08F/08EF)							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 36" P1) 48" - MH BASE w/FLANGE (08F/08EF) - 31" 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-420 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) Quik-Lok - QL-08-C 2) PSX - 12-08 NYLO					0 lb 3000 lb 4919 lb 0 lb 0 lb 1440 lb 340 lb 0 lb 0 lb 1 lb 16 lb Structure Total: 9716 lb		Structure Notes: 1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 805' Rim to Invert: 6' Slack: 0" Sump: 2" Step Position: 0"										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	799'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"
Invert 2	799.1'	90°	45.553"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	799.1'	230°	116.413"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 8"	Height (Int): 31" Height (Ext): 39"	Weight (Net): 4919 lb Volume (Net): 1.26cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-3241P2 - Buck Hills Subdivision

Job Location: Lawrenceburg, KY 40342

Contractor: Edmonson Plumbing & Heating Supply

Plant: 100

7/24/2026 12:43:56 PM

Tech: Jared - A

PC: C. Goff

Structure ID: MH B2

P1 MH048BAEVF

MH BASE w/FLANGE (08F/08EF)

P3) 24" - CASTING HEIGHT - 7"

P2) 48" - ECC CONE w/ 24" HOLE - 36"

P1) 48" - MH BASE w/FLANGE (08F/08EF) - 31"

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) CASTING - HOE MC-420 F/C Sanitary

1) 48" - Conseal CS-102 1.00" (Double)

1) 24" - Conseal CS-102 1.00" (Double)

1) Quik-Lok - QL-08-C

2) PSX - 12-08 NYLO

0 lb

3000 lb

4919 lb

0 lb

0 lb

1440 lb

340 lb

0 lb

0 lb

1 lb

16 lb

9716 lb

Structure Notes:

1. HOE MC-420 F/C SANITARY PROVIDED BY ICAST

2. PER ASTM C478 SPECIFICATIONS.

3. CONCRETE = 4,000 PSI AT 28 DAYS.

4. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

INVERT CHANNEL DRAWING

FULL HEIGHT INVERT

Structure Total:

9716 lb

Rim: 805'

Rim to Invert: 6'

Slack: 0"

Sump: 2"

Step Position: 0"

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	799'	0°	0"	8" PVC SDR35	8.5"	Quik-Lok QL-08-C	10.75"	10.842"	0.625"	0"
Invert 2	799.1'	90°	45.553"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 3	799.1'	230°	116.413"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 2
Degree: 90°
Horz: 37.699"
Hole: 12"
Up(): 1.2"

Invert: 3
Degree: 230°
Horz: 96.342"
Hole: 12"
Up(): 1.2"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 10.75"
Up(): 0.625"

Step: 0°
Horz: 0"

UPSIDE-DOWN VIEW (int. dimenions)

Invert: 3
Degree: 230°
Horz: 96.342"
Hole: 12"
Up(): 1.2"

Invert: 2
Degree: 90°
Horz: 37.699"
Hole: 12"
Up(): 1.2"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 10.75"
Up(): 0.625"

Step: 0°
Horz: 0"

INSIDE WALL DIMENSIONS

1.2"

1.2"

0.625"

8"

31"

EXT

360°

270°

180°

90°

0°

96.342"

37.699"

0"

3

2

1

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"


Floor Height: 8"

Height (Int): 31"

Height (Ext): 39"

Weight (Net): 4919 lb


Volume (Net): 1.26cu.yd




Weight (Net): 3086 lb
Volume (Net): 0.79cu.yd

Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:39 AM		Tech: J. Horsley PC: M. Sullivan			
Structure ID: 24 ST-SCB										
P1 MH048BAVF		MH BASE Custom Ht								
P3) 32" x 32" - CASTING HEIGHT - 3" P2) 48" - MH FLAT TOP w/32"x32" Hole - 7" P1) 48" - MH BASE Custom Ht - 29" 1) 48" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 16 1) Hole - 18					0 lb 950 lb 2767 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 3717 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1057.33' Rim to Invert: 3.28' Slack: 0.36" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1054.05'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"
Invert 2	1054.05'	185°	93.637"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"
Invert 3	1054.05'	279°	141.215"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"
Invert 4	1054.05'	90°	45.553"	12" HDPE	14.5"	Hole 18	18"	18.451"	-1.25"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

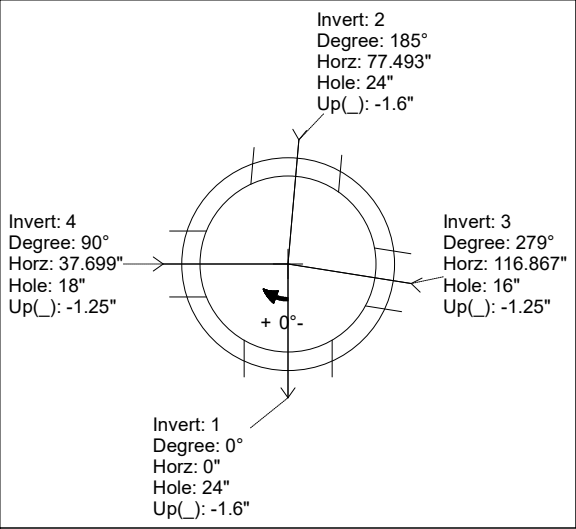

UPSIDE-DOWN VIEW (int. dimensions)

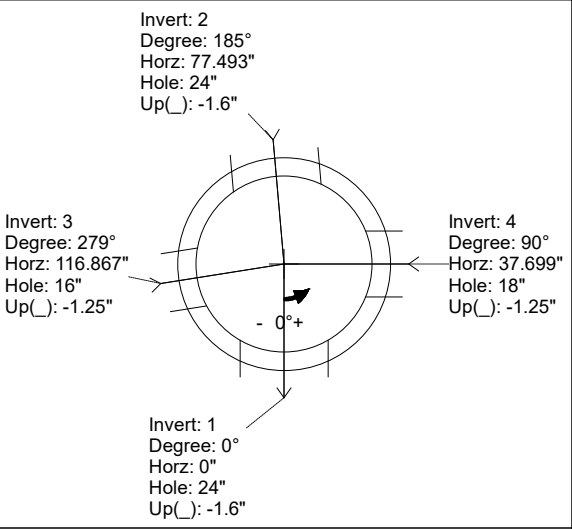


INSIDE WALL DIMENSIONS

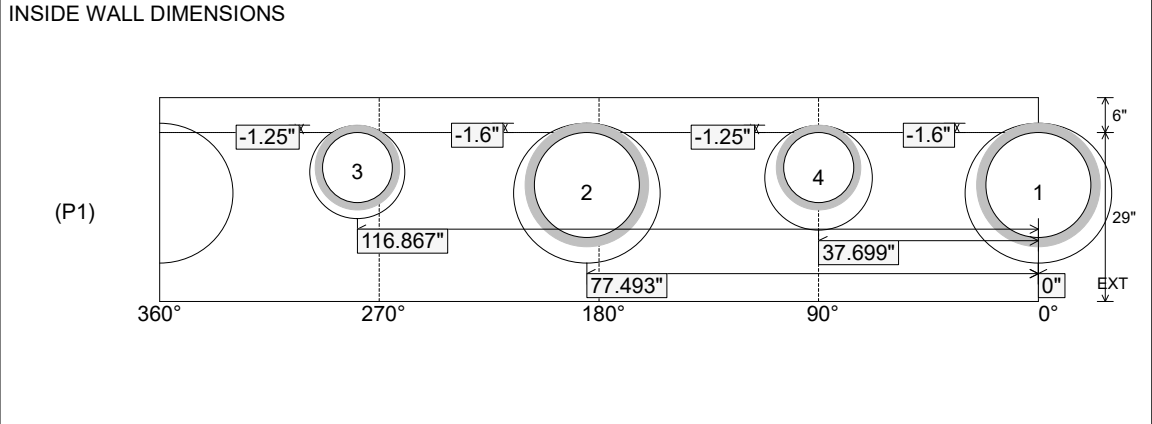


Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 29" Height (Ext): 35"	Weight (Net): 2767 lb Volume (Net): 0.71cu.yd
----------------------------------	-------------------------------	--	--	--


Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:37 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 21 ST-DCB											
P1 MH048BAVF		MH BASE Custom Ht									
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole - 12" P1) 48" - MH BASE Custom Ht - 41" 1) 48" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16						0 lb 2008 lb 3973 lb 0 lb 0 lb 0 lb ----- Structure Total: 5981 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 580 F/G) . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER (As .12). - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1069.88' Rim to Invert: 4.88' Slack: 0.06" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	1065'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 2	1065'	202°	102.241"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

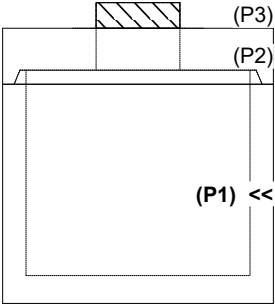


RIGHT-SIDE UP VIEW (int. dimensions)

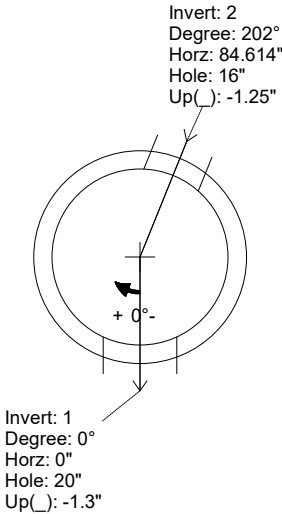

UPSIDE-DOWN VIEW (int. dimensions)

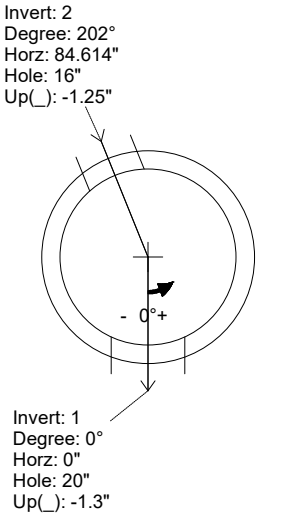


INSIDE WALL DIMENSIONS

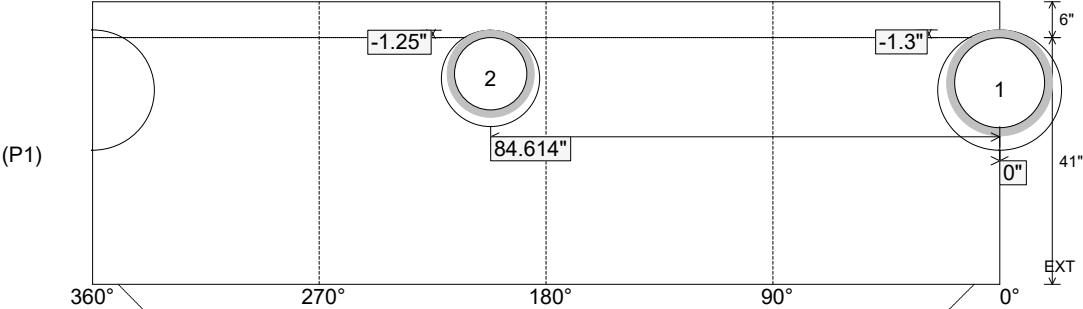


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 41" Height (Ext): 47"	Weight (Net): 3973 lb Volume (Net): 1.01cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:36 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 19 ST-DCB											
P1 MH048BAVF		MH BASE Custom Ht									
P3) 32" x 32" - CASTING HEIGHT - 3" P2) 48" - MH FLAT TOP w/32"x32" Hole - 7" P1) 48" - MH BASE Custom Ht - 23" 1) 48" - Conseal CS-102 1.00" 2) Hole - 20 Structure Total: 3647 lb						Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 1061.64' Rim to Invert: 2.78' Slack: 0.36" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1058.86'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 2	1058.86'	243°	122.993"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											




RIGHT-SIDE UP VIEW (int. dimensions)

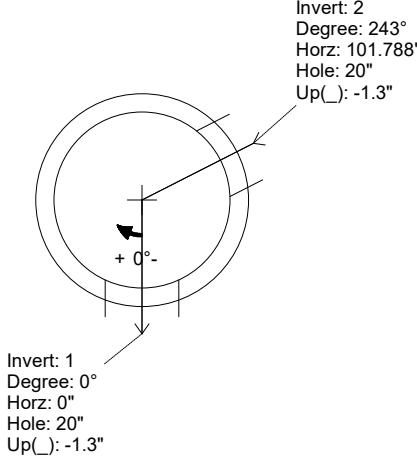





UPSIDE-DOWN VIEW (int. dimensions)

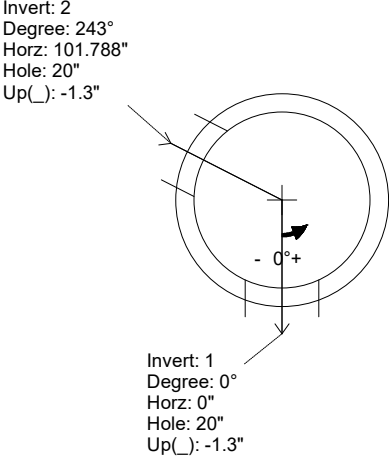

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 23" Height (Ext): 29"	Weight (Net): 2696 lb Volume (Net): 0.69cu.yd
----------------------------------	-------------------------------	--	--	--

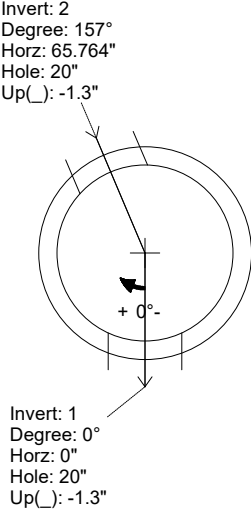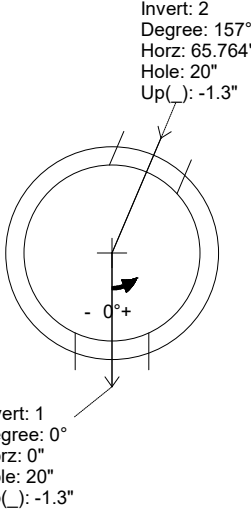Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:35 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 18 ST-DCB											
P1 MH048BAVF		MH BASE Custom Ht									
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 48" - MH FLAT TOP w/18"x36" Hole - 7" P1) 48" - MH BASE Custom Ht - 21" 1) 48" - Conseal CS-102 1.00" 2) Hole - 20						0 lb 1171 lb 2527 lb 0 lb 0 lb ----- Structure Total: 3698 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 580 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1061.3'		Rim to Invert: 2.8'		Slack: 0.1"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	1058.5'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 2	1058.5'	157°	79.465"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.3"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions) INSIDE WALL DIMENSIONS											
   											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 21" Height (Ext): 27"		Weight (Net): 2527 lb Volume (Net): 0.64cu.yd		

Job Name: 26-2146 - Fairview Apartments
Job Location: Russell Springs, KY 42642
Contractor: Dirt Design Construction LLC

Plant: 100

8/3/2026 11:45:33 AM

Tech: J. Horsley

PC: M. Sullivan



Structure ID: 14 ST-SCB

P1 MH048BAVF

MH BASE Custom Ht

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 48" - MH FLAT TOP w/18"x36" Hole - 12"
P1) 48" - MH BASE Custom Ht - 46"
1) 48" - Conseal CS-102 1.00"
2) Hole - 16
1) Hole - 8

0 lb
2008 lb
4351 lb
0 lb
0 lb
0 lb

Structure Total: 6359 lb

Structure Notes:




1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY OTHERS (HOE 580 F/G)
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 1070.95' Rim to Invert: 5.3' Slack: 0.1" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1065.65'	0°	0"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"
Invert 2	1065.65'	155°	78.453"	12" HDPE	14.5"	Hole 16	16"	16.312"	-1.25"	0"
Invert 3	1066'	90°	45.553"	8" Hole	8"	Hole 8	8"	8.038"	4.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

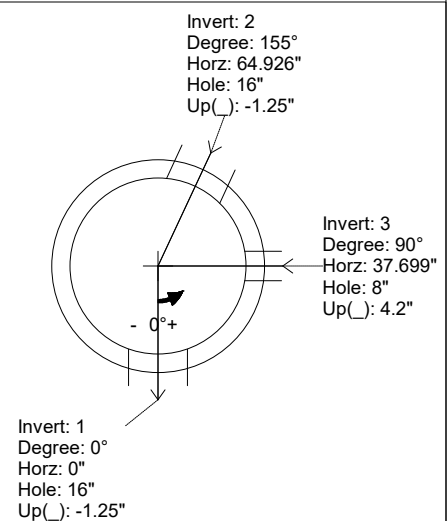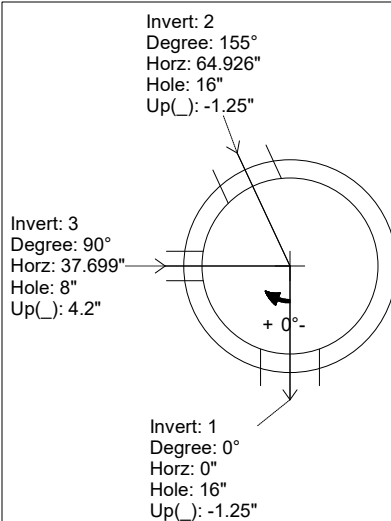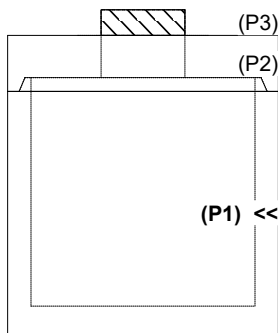

INSIDE WALL DIMENSIONS

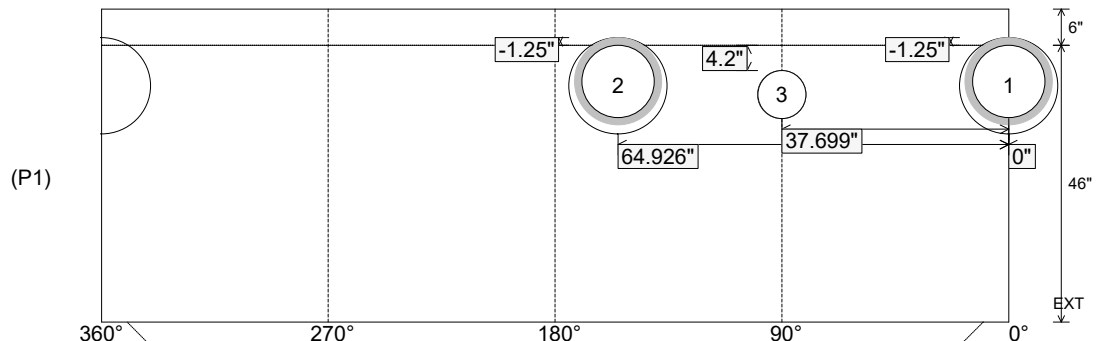

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 46"
Height (Ext): 52"

Weight (Net): 4351 lb
Volume (Net): 1.11cu.yd

MH BASE Custom Ht

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 580 F/G)




REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB = H20 LOADING.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Structure Total:

[illegible]

UPSIDE-DOWN VIEW (int. dimensions)

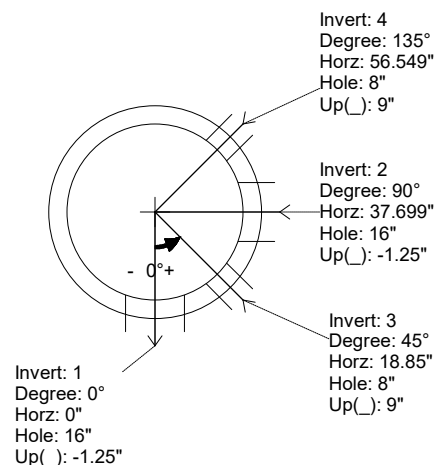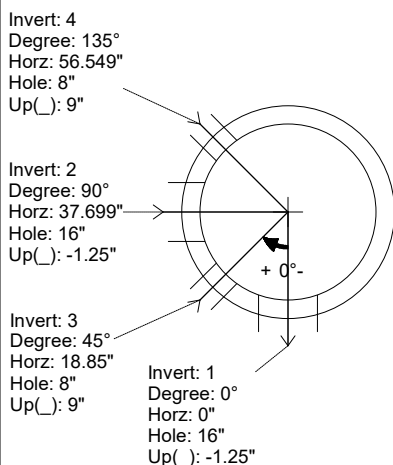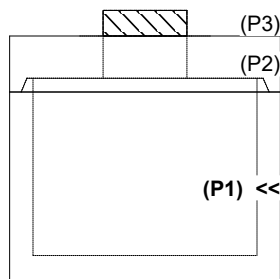


INSIDE WALL DIMENSIONS

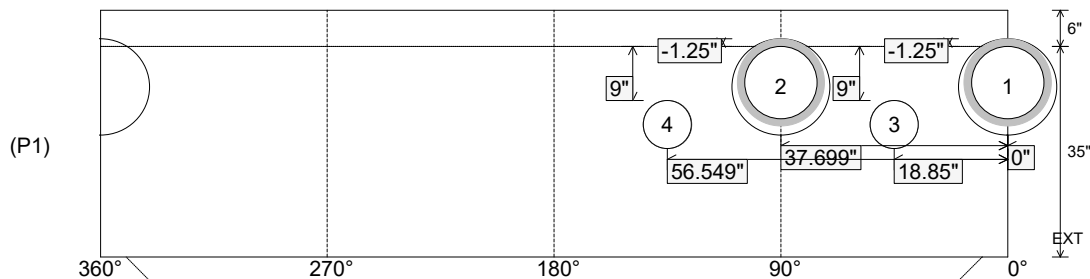


Weight (Net): 3561 lb
Volume (Net): 0.91cu.yd

Job Name: 24-3511 Coles Ferry Section 18 & 19 Job Location: Lebanon, TN Contractor: Covenant Constructors, LLC				Plant: Beaver Dam, KY 8/4/2026 3:08:36 PM		Tech: J. Horsley PC: A. Chambers				
Structure ID: JB3										
P1		MH048BAVF		MH BASE Custom Ht F/n						
P3) 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 20" 1) CASTING - JBS 1072 F/C STORM 1) 48" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 26"x24" 2) DOGHOUSE INVRTD - 22"x20.25" 1) MH Step ML-10-TDS-NCR - 10"						0 lb 798 lb 2193 lb 250 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 3242 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (JBS 1072 F/C). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 571.95'		Rim to Invert: 2.4'		Slack: 0.3"		Sump: 2.5"		Step Position: 90°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	569.55'	0°	0"	18" RCP B WALL	23"	DOGHOUSE INVRTD 26"x24"	26" x 24"	27.476"	0"	0"
Invert 2	569.55'	180°	91.125"	15" RCP B WALL	19.5"	DOGHOUSE INVRTD 22"x20.25"	22" x 20.25"	22.854"	0.25"	0"
Invert 3	569.55'	270°	136.625"	15" RCP B WALL	19.5"	DOGHOUSE INVRTD 22"x20.25"	22" x 20.25"	22.854"	0.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

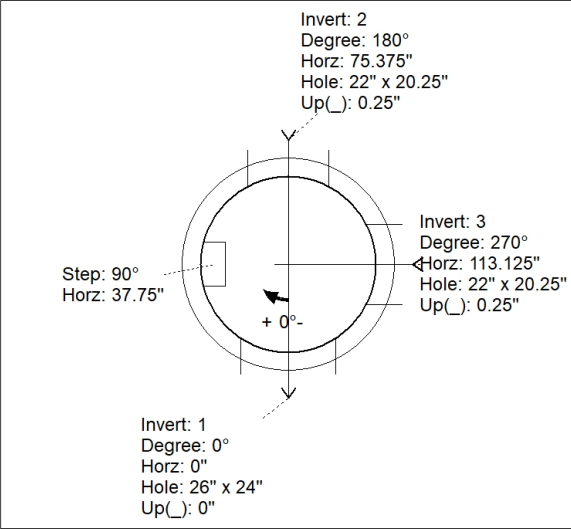

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 22" x 20.25"
Up(): 0.25"


Invert: 3
Degree: 270°
Horz: 113.125"
Hole: 22" x 20.25"
Up(): 0.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26" x 24"
Up(): 0"

Step: 90°
Horz: 37.75"

+ 0°-

UPSIDE-DOWN VIEW (int. dimensions)

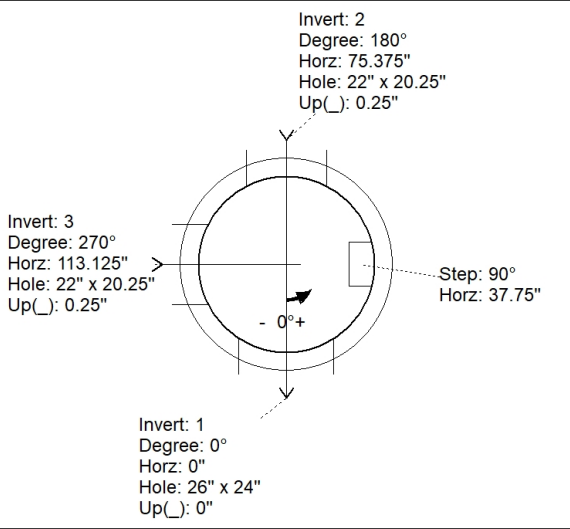

Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 22" x 20.25"
Up(): 0.25"


Invert: 3
Degree: 270°
Horz: 113.125"
Hole: 22" x 20.25"
Up(): 0.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 26" x 24"
Up(): 0"

Step: 90°
Horz: 37.75"

- 0°+

INSIDE WALL DIMENSIONS

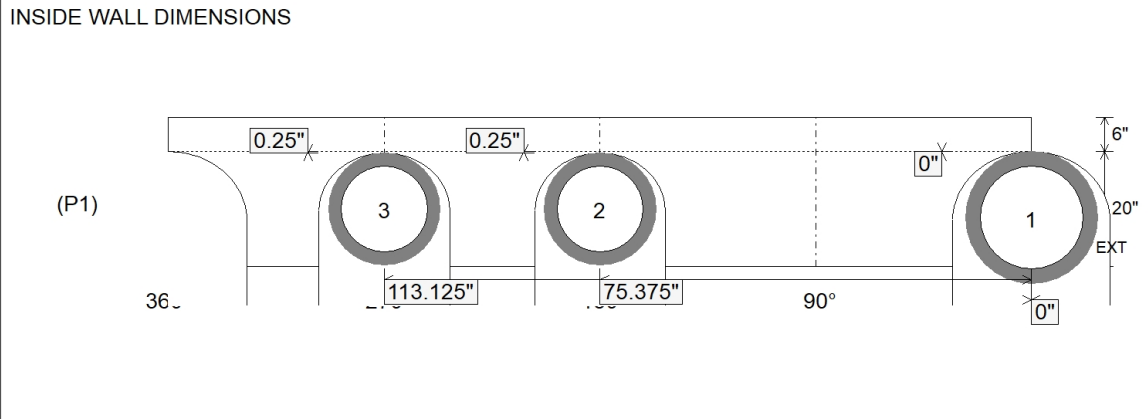

(P1)

36

0.25"

0.25"

0"

3

2

1

113.125"

75.375"

90°

0"

6"

20"

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 20" Height (Ext): 26"	Weight (Net): 2193 lb Volume (Net): 0.56cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 25-4490P1 Heartland Meadows Subdivision

Job Location: Elizabethtown, KY 40165

Contractor: Kauffeld Brothers Construction

Plant: 100

7/23/2026 12:36:46 PM

Tech: Jared - A

PC: Celina Goff

Structure ID: MH 1-8 (9)

P1 MH048BAVF-D

MH BASE w/DROP Custom Ht

P6) 24" - CASTING HEIGHT - 7"

P5) 24" - GRADE RING - 4"

P4) 48" - ECC CONE w/ 24" HOLE - 42"

P3) 48" - MH RISER - 36"

P2) 48" - MH RISER w/DROP - 48"

P1) 48" - MH BASE w/DROP Custom Ht - 30"

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-375 F/C Sanitary

3) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-06 NYLO

1) Drop Elbow - 6" PVC

1) Drop Tee - 6" PVC

13) MH Step ML-10-TDS-NCR - 10"

0 lb

270 lb

3200 lb

2515 lb

5403 lb

4866 lb

1440 lb

0 lb

0 lb

271 lb

0 lb

0 lb

0 lb

16 lb

0 lb

0 lb

0 lb

0 lb

Structure Notes:

1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.

2. PER ASTM C478 SPECIFICATIONS.

3. CONCRETE = 4,000 PSI AT 28 DAYS.

4. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 897.51'

Rim to Invert: 13.71'

Slack: 0.52"

Sump: 3"

Step Position: 90°

Structure Total: 17981 lb

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	883.8'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"
Invert 2	883.9'	147°	74.403"	6" PVC SDR35	6.25"	Drop Elbow 6" PVC	6.5"	6.52"	3.95"	0"
Invert 3										
Invert 4	883.9'	242°	122.487"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"

Floor Height: 6"

Height (Int): 30"

Height (Ext): 36"

Weight (Net): 4866 lb

Volume (Net): 1.24cu.yd

Job Name: 25-4490P1 Heartland Meadows Subdivision

Job Location: Elizabethtown, KY 40165

Contractor: Kauffeld Brothers Construction

Plant: 100

7/23/2026 12:36:46 PM

Tech: Jared - A

PC: Celina Goff

Structure ID: MH 1-8 (9)

P1 MH048BAVF-D

MH BASE w/DROP Custom Ht

P6) 24" - CASTING HEIGHT - 7"

P5) 24" - GRADE RING - 3"

P4) 48" - ECC CONE w/ 24" HOLE - 42"

P3) 48" - MH RISER - 36"

P2) 48" - MH RISER w/DROP - 48"

P1) 48" - MH BASE w/DROP Custom Ht - 30"

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212

1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)

1) CASTING - HOE MC-375 F/C Sanitary

3) 48" - Conseal CS-102 1.00" (Double)

2) 24" - Conseal CS-102 1.00" (Double)

2) PSX - 12-06 NYLO

1) Drop Elbow - 6" PVC

1) Drop Tee - 6" PVC

13) MH Step ML-10-TDS-NCR - 10"

0 lb

202 lb

3200 lb

2515 lb

5403 lb

4866 lb

1440 lb

0 lb

0 lb

271 lb

0 lb

0 lb

0 lb

16 lb

0 lb

0 lb

0 lb

17914 lb

Structure Notes:

1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.

2. PER ASTM C478 SPECIFICATIONS.

3. CONCRETE = 4,000 PSI AT 28 DAYS.

4. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 897.51'

Rim to Invert: 13.71'

Slack: 1.52"

Sump: 3"

Structure Total: 17914 lb

Step Position: 90°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	883.8'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"
Invert 2	883.9'	147°	74.403"	6" PVC SDR35	6.25"	Drop Elbow 6" PVC	6.5"	6.52"	3.95"	0"
Invert 3										
Invert 4	883.9'	242°	122.487"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 5"



Floor Height: 6"

Height (Int): 30"

Height (Ext): 36"

Weight (Net): 4866 lb

Volume (Net): 1.24cu.yd

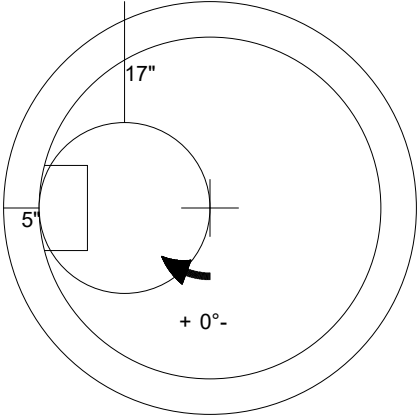Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC		Plant: 100 8/3/2026 11:47:13 AM	Tech: J. Horsley PC: M. Sullivan	
Structure ID: MH 3 SS-MH				
P2 MH048CN30		ECC CONE w/ 24" HOLE		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 30" P1) 48" - MH BASE - 24" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"		0 lb 2050 lb 2911 lb 1440 lb 0 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 6417 lb Structure Total:	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-420 F/C). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE - 30" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd

Weight (Net): 950 lb
Volume (Net): 0.24cu.yd

Job Name: 26-2146 - Fairview Apartments
Job Location: Russell Springs, KY 42642
Contractor: Dirt Design Construction LLC

Plant: 100

8/3/2026 11:47:15 AM

Tech: J. Horsley

PC: M. Sullivan



Structure ID: 08 ST-SCB

P2 MH048LD12-18x36 RECT

MH FLAT TOP w/18"x36" Hole

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 48" - MH FLAT TOP w/18"x36" Hole - 12"
P1) 48" - MH BASE Custom Ht - 27"
1) 48" - Conseal CS-102 1.00"
1) Hole - 16

Structure Total:



0 lb
2008 lb
3131 lb
0 lb
0 lb

5139 lb

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 580 F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB = H20 LOADING.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

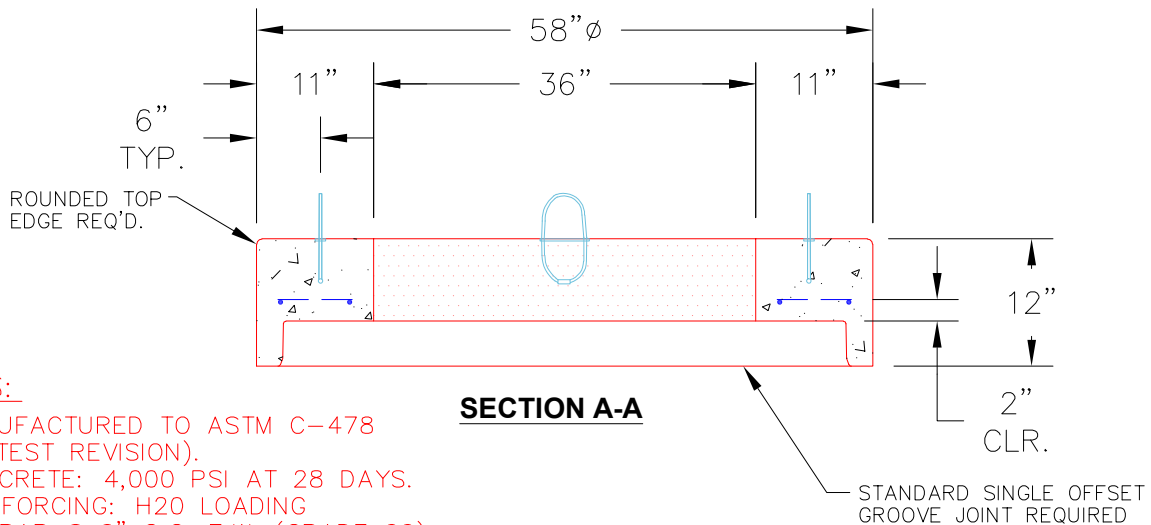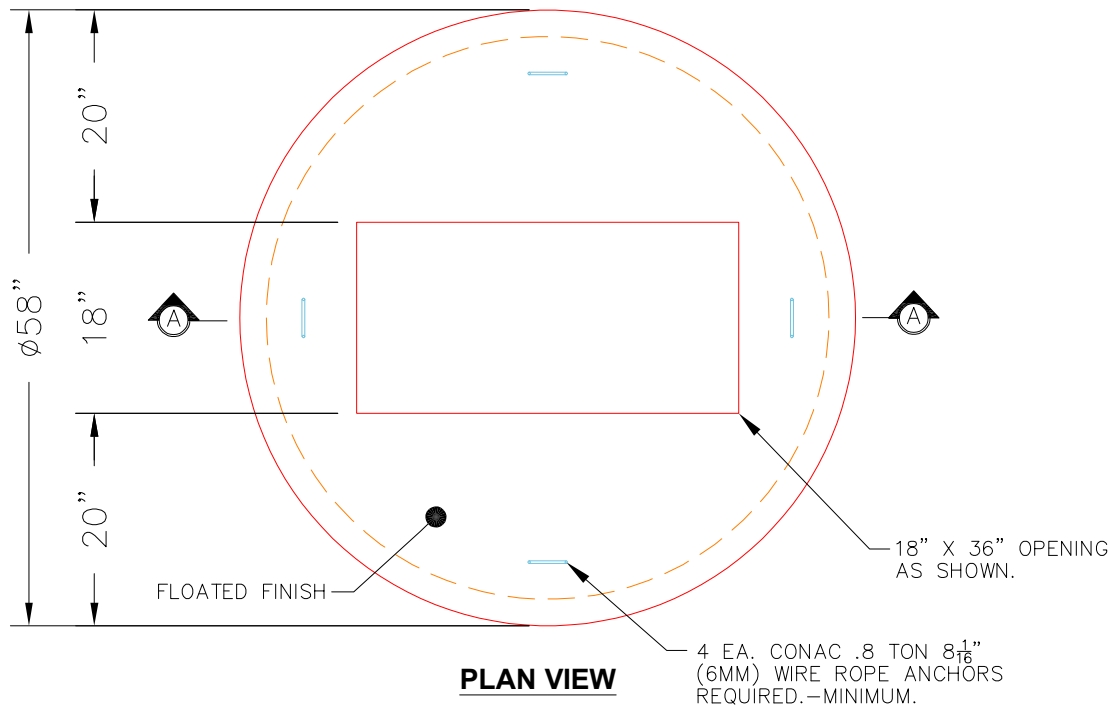

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: H20 LOADING #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 2008 lb
Volume (Net): 0.51cu.yd

Job Name: 26-2146 - Fairview Apartments
Job Location: Russell Springs, KY 42642
Contractor: Dirt Design Construction LLC

Plant: 100

8/3/2026 11:47:14 AM

Tech: J. Horsley

PC: M. Sullivan



Structure ID: 05 ST-SCB

P2 MH048LD12-18x36 RECT

MH FLAT TOP w/18"x36" Hole

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 48" - MH FLAT TOP w/18"x36" Hole - 12"
P1) 48" - MH BASE - 30"
1) 48" - Con Seal CS-102 1.00"
2) Hole - 16

Structure Total:



0 lb
2008 lb
3255 lb
0 lb
0 lb
5262 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 580 F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB = H20 LOADING.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

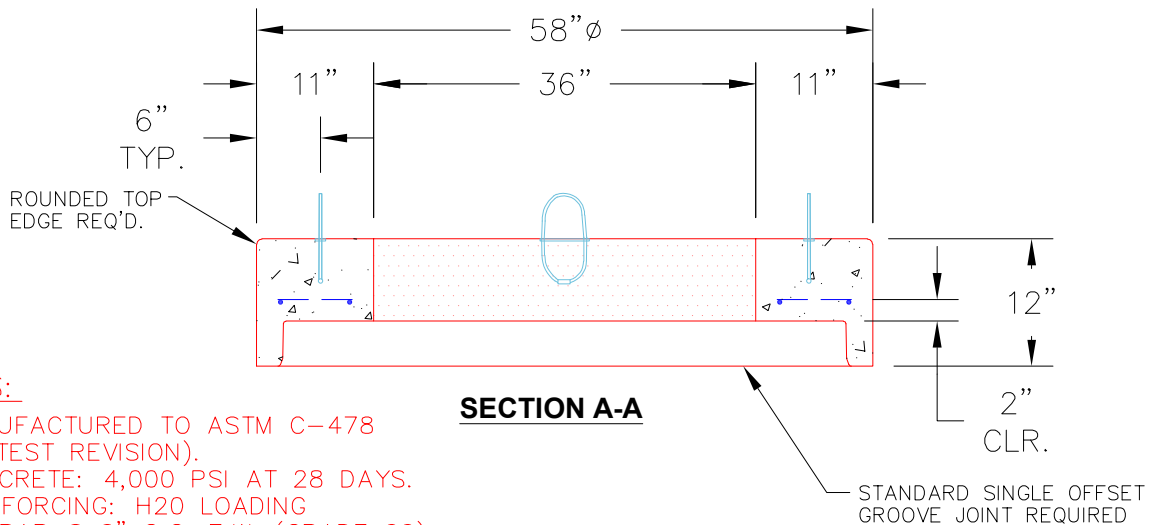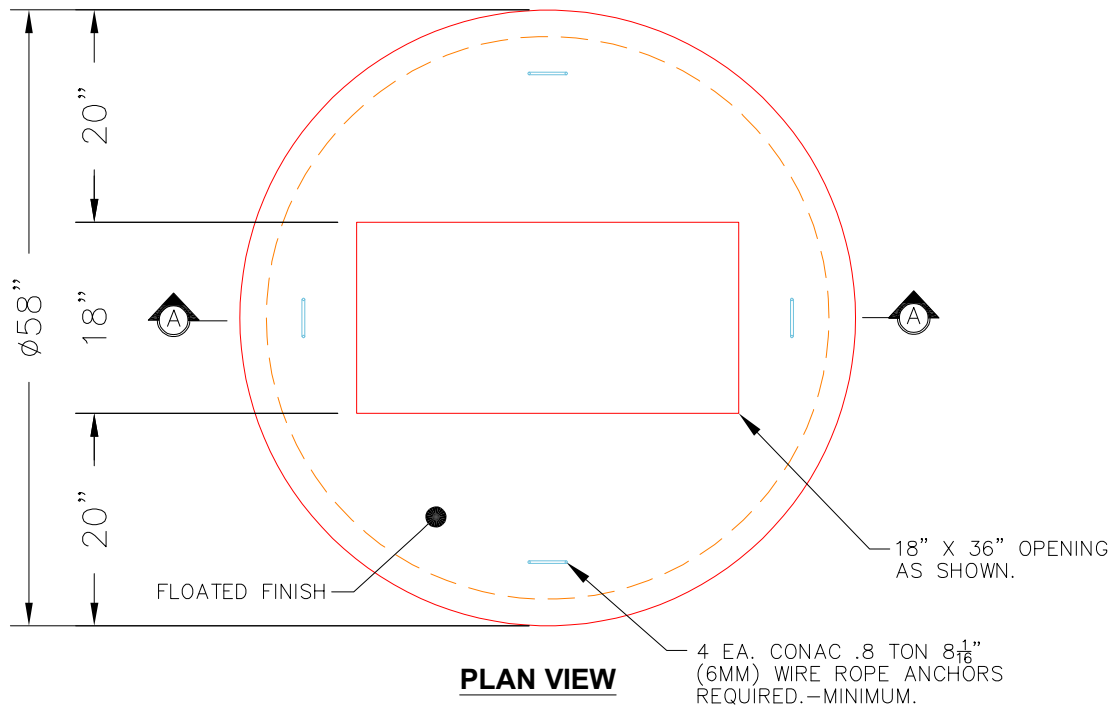

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: H20 LOADING #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 2008 lb
Volume (Net): 0.51cu.yd

Job Name: 26-2146 - Fairview Apartments
Job Location: Russell Springs, KY 42642
Contractor: Dirt Design Construction LLC

Plant: 100

8/3/2026 11:47:13 AM

Tech: J. Horsley

PC: M. Sullivan



Structure ID: 02 ST-SCB

P2 MH048LD12S

MH FLAT TOP w/32"x32" Hole

P3) 32" x 32" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/32"x32" Hole - 12"
P1) 48" - MH BASE Custom Ht - 29"
1) 48" - Con Seal CS-102 1.00"
2) Hole - 20



0 lb
1629 lb
3086 lb
0 lb
0 lb
Structure Total: 4715 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 595 F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB = H20 LOADING.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

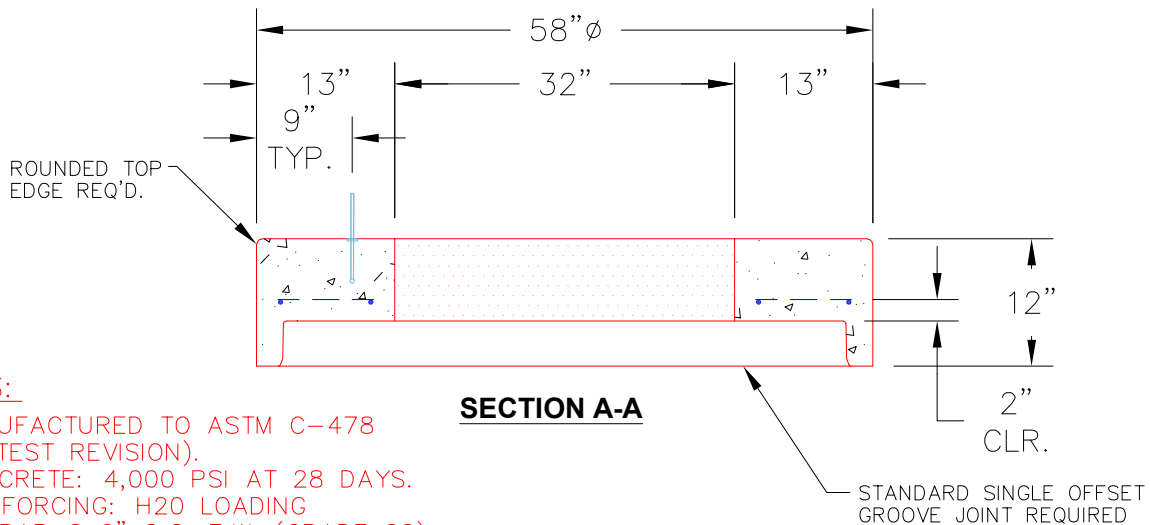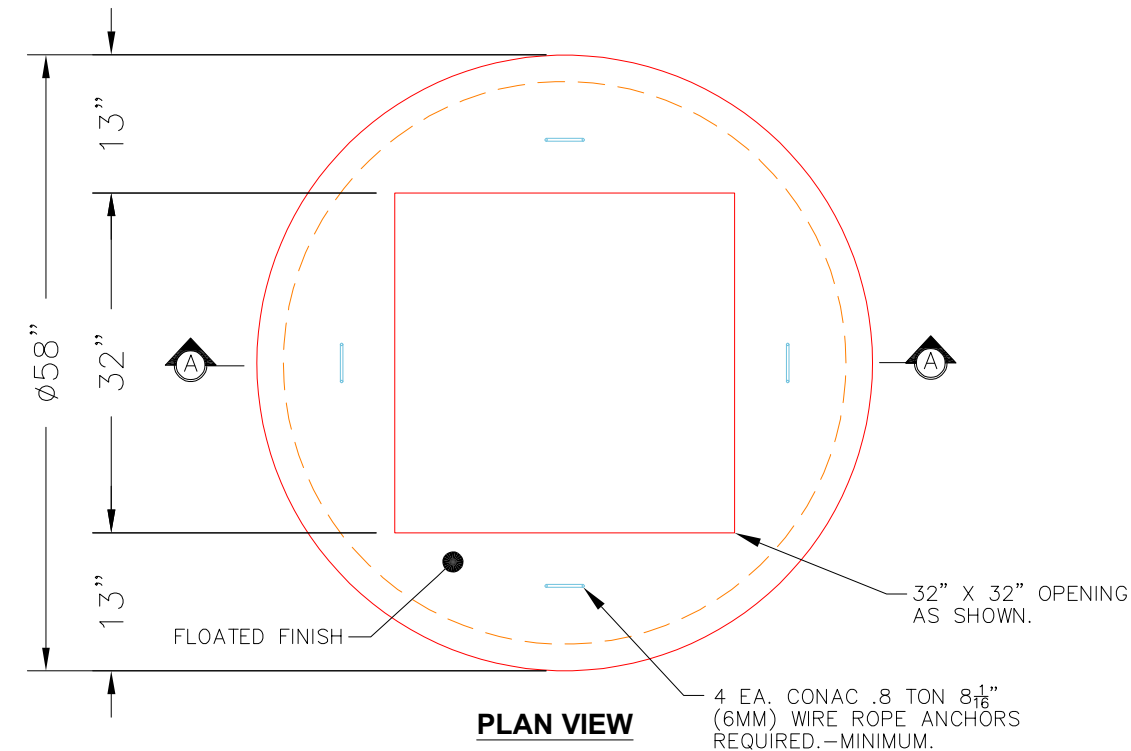

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: H20 LOADING #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1629 lb
Volume (Net): 0.42cu.yd

Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting					Plant: 100		Tech: J. Horsley - A			
					3/20/2026 1:22:17 PM		PC: Celina Goff			
Structure ID: 2301575										
P1 MH060BA48					MH BASE T/n					
P4) 24" - CASTING HEIGHT - 7" P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P2) 60" - MH RISER T/G - 48" P1) 60" - MH BASE T/n - 48" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 2) 60" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 1) PSX - 12-08 NYLO 8) MH Step ML-10-TDS-NCR - 10"					0 lb 2869 lb 5011 lb 7427 lb 2692 lb 0 lb 12 lb 8 lb 0 lb Structure Total: 18019 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - WALLS: PER ASTM A615 - DOUBLE MAT - FLOOR: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. INVERT CHANNEL REQUIRED 5. STEPS AT 270 DEGREES 6. 7" CASTING SUPPLIED BY OTHERS			
Rim: 738.89' Rim to Invert: 9.74' Slack: 2.88" Sump: 2" Step Position: 270°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	729.15'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.282"	0.5"	0"
Invert 2	731.14'	103°	64.75"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.081"	23.875"	0"
Invert 3	729.29'	190°	119.375"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.282"	2.125"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)


INSIDE WALL DIMENSIONS

Coating (Int):	Seam Up: Tongue	Wall Thickness: 6"	Height (Int): 48"	Weight (Net): 7427 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 8"	Height (Ext): 56"	Volume (Net): 1.9cu.yd


Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting					Plant: 100 3/20/2026 1:22:17 PM		Tech: J. Horsley - A PC: Celina Goff				
Structure ID: 2301575											
P1 MH060BA48		MH BASE T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P2) 60" - MH RISER T/G - 48" P1) 60" - MH BASE T/n - 48" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 2) 60" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 1) PSX - 12-08 NYLO 8) MH Step ML-10-TDS-NCR - 10"						0 lb 2869 lb 5011 lb 7427 lb 2692 lb 0 lb 12 lb 8 lb 0 lb ----- Structure Total: 18019 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - WALLS: PER ASTM A615 - DOUBLE MAT - FLOOR: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. INVERT CHANNEL REQUIRED 5. STEPS AT 270 DEGREES 6. 7" CASTING SUPPLIED BY OTHERS			
Rim: 738.89' Rim to Invert: 9.74' Slack: 2.88" Sump: 2" Step Position: 270°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	729.15'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.282"	0.5"	0"	
Invert 2	731.14'	103°	64.75"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.081"	23.875"	0"	
Invert 3	729.29'	190°	119.375"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.282"	2.125"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

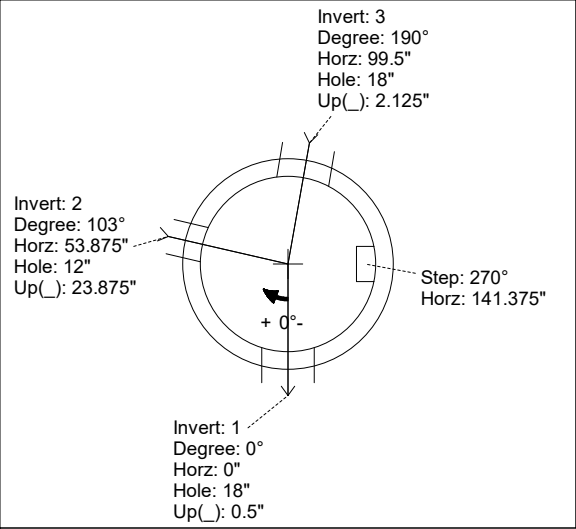

RIGHT-SIDE UP VIEW (int. dimensions)

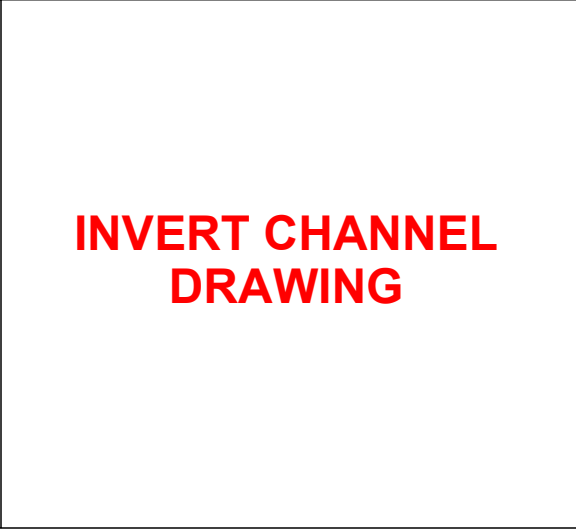

UPSIDE-DOWN VIEW (int. dimensions)

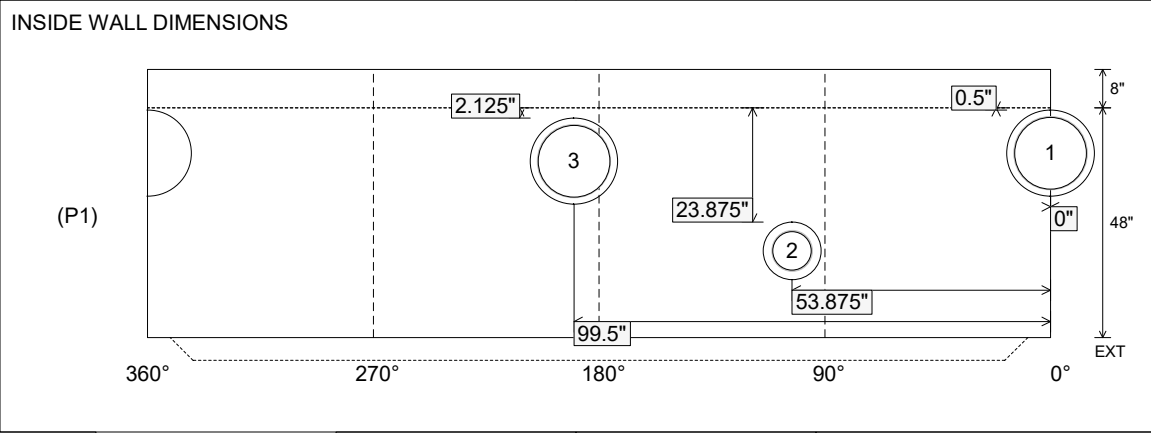

INVERT CHANNEL DRAWING

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 48" Height (Ext): 56"	Weight (Net): 7427 lb Volume (Net): 1.9cu.yd
----------------------------------	---------------------------------	--	--	---

Job Name: 25-3118 - W6 Ph 2-C Force Main Improvements Job Location: Fort Mitchell, KY 41017 Contractor: Lykins Contracting				Plant: 100 3/20/2026 1:22:18 PM		Tech: J. Horsley - A PC: Celina Goff				
Structure ID: 2301576										
P1 MH060BAVF				MH BASE Custom Ht T/n						
P3) 24" - CASTING HEIGHT - 7" P2) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P1) 60" - MH BASE Custom Ht T/n - 58" 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) 60" - Conseal CS-102 1.00" (Double) 1) Kor-N-Seal2 - S206-18L 1) PSX - 12-08 NYLO 5) MH Step ML-10-TDS-NCR - 10"				0 lb 2869 lb 8601 lb 2692 lb 0 lb 6 lb 8 lb 0 lb ----- 14176 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - WALLS: PER ASTM A615 - DOUBLE MAT - FLOOR: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. INVERT CHANNEL REQUIRED 5. STEPS AT 270 DEGREES 6. 7" CASTING SUPPLIED BY OTHERS				
Rim: 737.35' Rim to Invert: 6.46' Slack: 1.52" Sump: 2" Step Position: 270°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	730.89'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.282"	0.5"	0"
Invert 2	731.03'	92°	57.75"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.081"	1.625"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

Step: 270°
Horz: 141.375"

Invert: 2
Degree: 92°
Horz: 48.125"
Hole: 12"
Up(): 1.625"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 18"
Up(): 0.5"

INSIDE WALL DIMENSIONS

(P1)

1.625"

0.5"

48.125"

0"

8"

58"

360°

270°

180°

90°

0°

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 58" Height (Ext): 66"	Weight (Net): 8601 lb Volume (Net): 2.2cu.yd
----------------------------------	---------------------------------	--	--	---



Weight (Net): 8601 lb
Volume (Net): 2.2cu.yd

Job Number:

26-1394

Job Name:

TMMI Ryder Lift Station

Structure:

5 MV (2)

Note:

USF Fabrication 37" x 36" Hatch
Supplied By Others To Be Cast Into
Flat Lid

Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion
Job Location: Shepherdsville, KY
Contractor: Pace Contracting, LLC

Plant: 100

6/4/2026 5:54:53 PM

Tech: Jared - F

PC: J Jarvis



Structure ID: WAS VAULT 2

P2 MH060LD13S

MH FLAT TOP w/36"x36" Hatch F/G

- P3) 36" x 36" - CASTING HEIGHT - 0"
P2) 60" - MH FLAT TOP w/36"x36" Hatch F/G - 13"
P1) 60" - MH BASE Custom Ht T/n - 59"
1) HATCH (Alum.) - HALLIDAY W1S 36"x36"
1) 60" - Conseal CS-102 1.00" (Double)
1) 36" x 36" - Conseal CS-102 1.00" (Double)
2) PSX - 8QRS DD

Structure Total:


0 lb
2132 lb
8842 lb
78 lb
0 lb
0 lb
0 lb
13 lb

11065 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. HATCH SUPPLIED BY I-CAST (HALLIDAY W1S 36"x36")

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .18)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

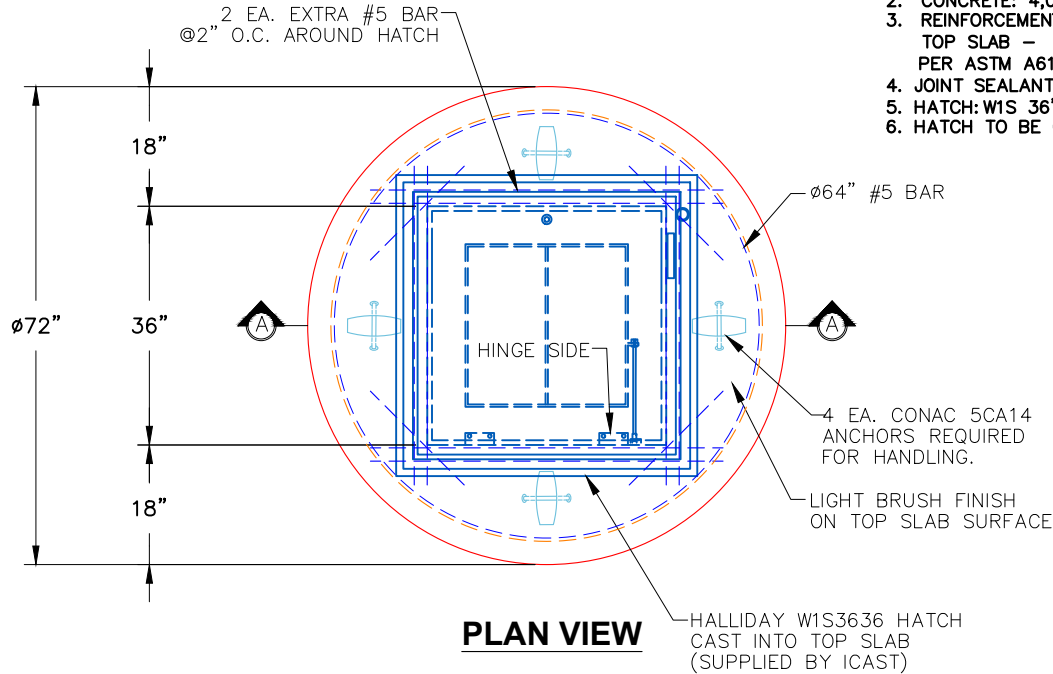

NOTES:

1. PER ASTM C-478 LATEST REVISION
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCEMENT:
TOP SLAB - #5 BAR @ 6" C.C.E.W.
PER ASTM A615 (GRADE 60)
4. JOINT SEALANT - 1" CS-102-DOUBLE
5. HATCH: W1S 36"x36" HATCH IS PROVIDED BY ICAST.
6. HATCH TO BE CAST INTO TOP SLAB.

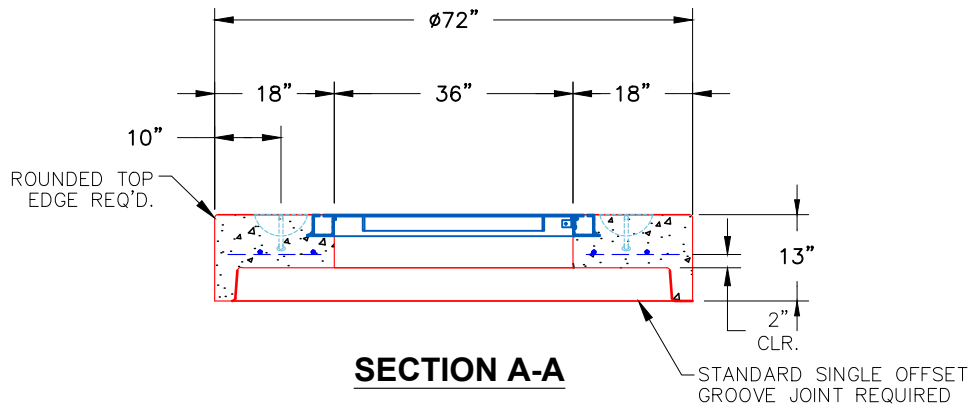

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 2132 lb
Volume (Net): 0.55cu.yd

Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion
Job Location: Shepherdsville, KY
Contractor: Pace Contracting, LLC

Plant: 100

7/31/2026 8:06:18 AM

Tech: Jared - F

PC: J Jarvis



Structure ID: MH-39-01A

P4 MH072TS15-48ECC

MH Transition Slab 48" Hole

- P7) 24" - CASTING HEIGHT - 7"
P6) 48" - ECC CONE w/ 24" HOLE - 30"
P5) 48" - MH RISER - 24"
P4) 72" - MH Transition Slab 48" Hole - 15"
P3) 72" - MH RISER Custom Ht - 61"
P2) 72" - MH RISER - 72"
P1) 72" - P.I.P. BY OTHERS - BTM SLAB - 0"
1) Chimney Seal - Cretex Chimney Seal
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-375-WT F/C Sanitary
3) 72" - Conseal CS-102 1.00" (Double)
2) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) DOGHOUSE - 28"x30"
1) Kor-N-Seal2 - S206-22
12) MH Step ML-10-TDS-NCR - 10"


- 0 lb
2050 lb
1677 lb
3864 lb
8666 lb
9541 lb
0 lb
10 lb
0 lb
0 lb
271 lb
0 lb
0 lb
0 lb
0 lb
0 lb
6 lb
0 lb
- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING SUPPLIED BY I-CAST (HOE MC-375-WT F/C SANITARY).
4. INTERNAL DROP INLET SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- TRANS.SLAB AS SHOWN BELOW.
- RISER/WALLS (As .18)


Structure Total: 26086 lb

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 & #5 BAR AS SHOWN (GRADE 60).
4. TONGUE REQUIRED OFFSET FOR 48"Ø COMPONENTS.

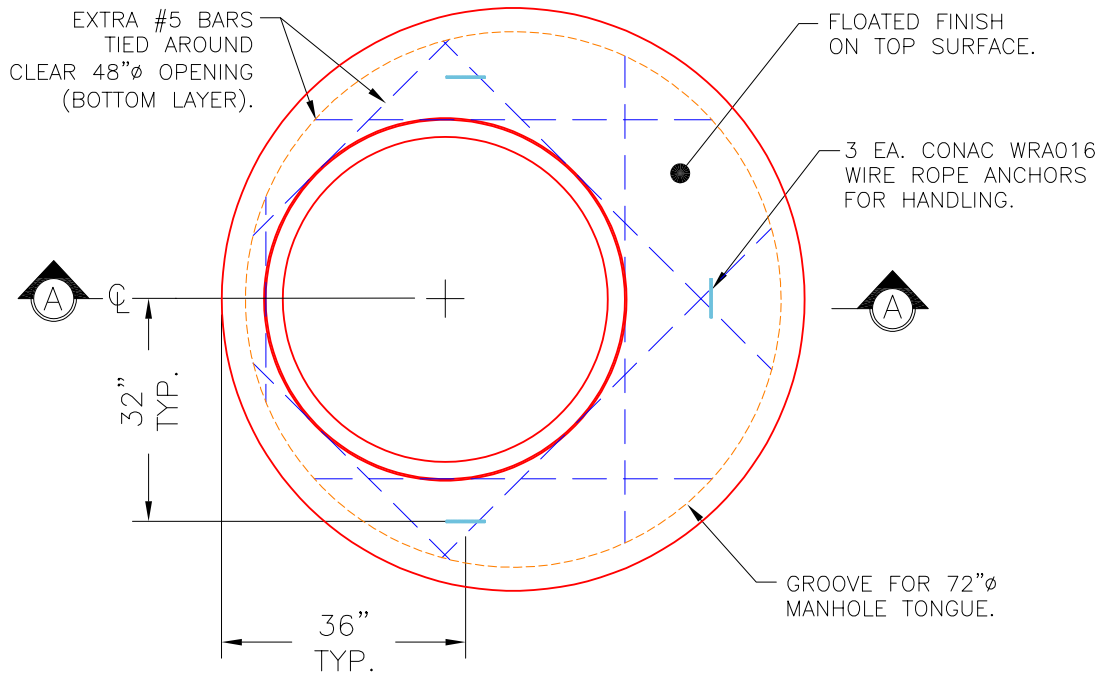

PLAN VIEW

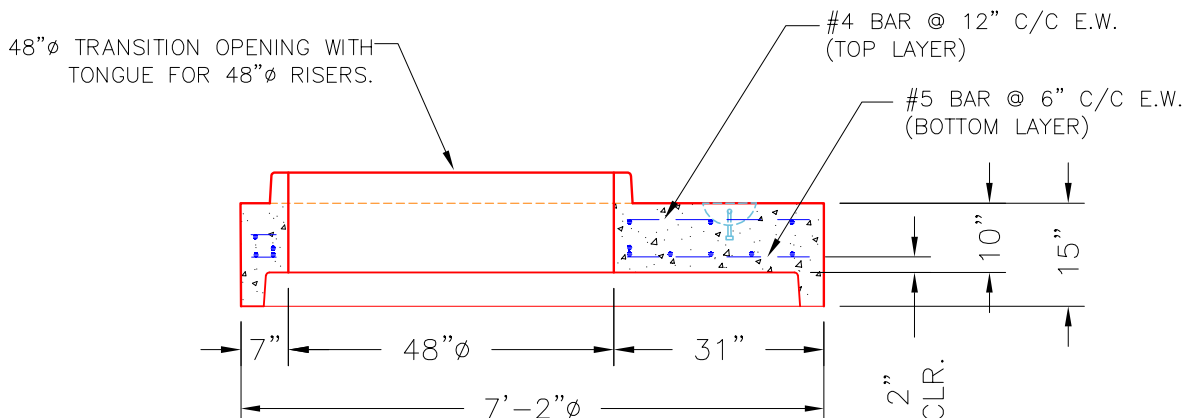

SECTION A-A

Coating (Int):
Coating (Ext):


Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"


Weight (Net): 3864 lb
Volume (Net): 0.99cu.yd

- NOTES:
1. BOX CULVERT IS DESIGNED PER ATTACHED PE STAMPED DRAWINGS & CALCULATIONS.
 2. LOAD REQUIREMENTS PER KY-HL93 (KY TABLE 1)
 3. COVER DEPTH = 15' - 0"
 4. CONCRETE: 5,000 PSI AT 28 DAYS.
 5. REINFORCING: AS SHOWN BY MATT CHILDS ENGINEERING.
 6. BOX CULVERT TO BE SEALED WITH CS-102 ROLL BUTYL MASTIC & CS-212 12" WRAP. (SUPPLIED BY ICAST).
 7. WEIGHT: 48,363 LBS.

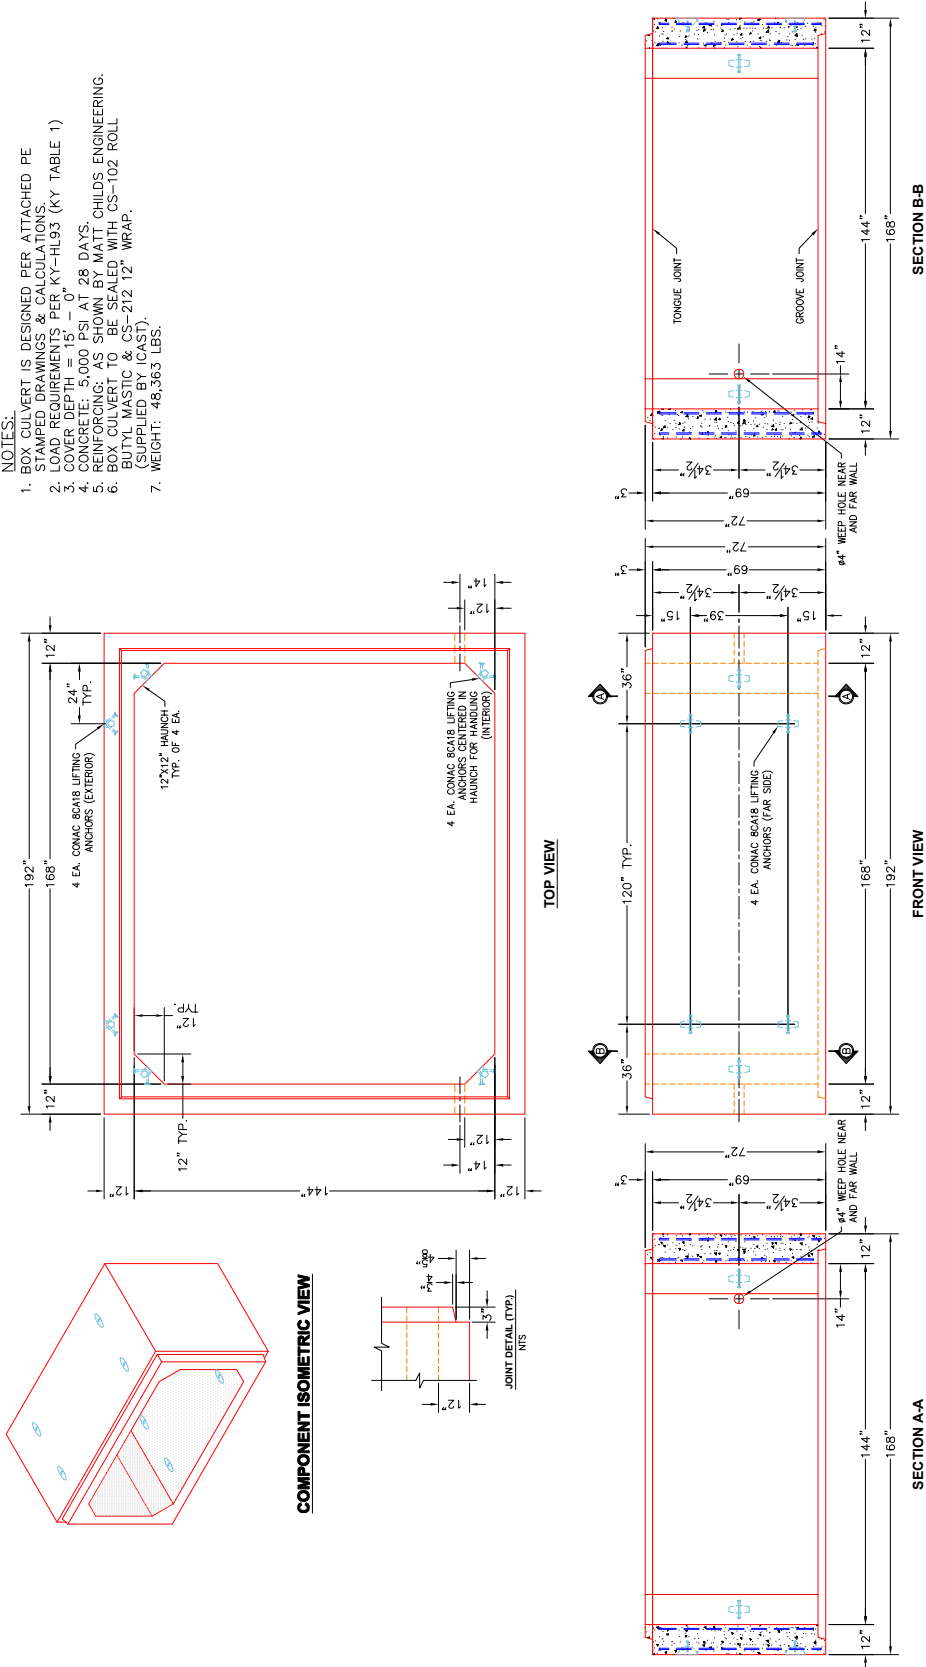

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 12" Floor Height: 0"	Height (Int): 69" Height (Ext): 69"	Weight (Net): 48363 lb Volume (Net): 12.35cu.yd
----------------------------------	------------------------------------	---	--	--

Project: Mooch Road
Product: 14' x 12' Box Culvert
Job: 26-2254
Design No.:
Location: Wilder, KY
Reference #:



MATT CHILDS ENGINEERING, PLLC

Project : City of Wilder
Task : 14x12 15' Fill
Job No. :

Client: ICast
File: 20260605-ICast-CityofWilder-14x12(15'Fill).etcx

Sht ____ of ____
By:MBJ
Ck:
6/5/2026 4:35:08 PM
p. 1 of 2

Spec.: LRFD 9th ed.
Type of Culvert: Precast

Physical Dimensions

Clear Span:	14'-0"
Clear Height:	12'-0"
Top Slab:	1'-0"
Bottom Slab:	1'-0"
Ext. Wall:	1'-0"
Fill Depth:	15.00 ft
Length:	4'-0"
Skew Angle:	0.00 deg
Bottom Slab Support:	Full Slab
Top Haunch, Width:	1'-0"
Top Haunch, Height:	1'-0"
Bottom Haunch, Width:	1'-0"
Bottom Haunch, Height:	1'-0"

Material Properties

Concrete	
Strength, f _c :	5.000 ksi
Density:	0.150 kcf
Elasticity, E _c :	3834 ksi
Type:	Normal wt
Steel	
Yield, f _y :	65 ksi
Allow Stress:	39 ksi
Elasticity, E _s :	29000 ksi
Soil	
Density:	0.120 kcf
Exposure Factor	
Class 2 Exposure	
Reinforcement Covers	
Ext. Cover Top Slab:	1"
Ext. Cover Bottom Slab	1"
Ext. Cover Walls	1"
Int. Cover Walls	1"
Int. Cover Top Slab	1"
Int. Cover Bottom Slab	1"

Controlling Ratings



Inventory Rating: 5.85
Operating Rating: 7.59

Loads

Live Load	
Vehicle Names:	HL-93
Traffic Direction:	Parallel
Eq. Height of Soil:	2.00 ft (Calc'd)
Dead Load	
Future Wearing Surface:	0.000 klf
Additional Dead Load:	0.000 klf
Concentrated Loads:	none

Lateral Soil Loads	
Eq. Fluid Press. Max:	60.00 pcf
Eq. Fluid Press. Min:	30.00 pcf

Interior Water Pressure:	yes, head pressure = 0 ft
Exterior Water Pressure:	no

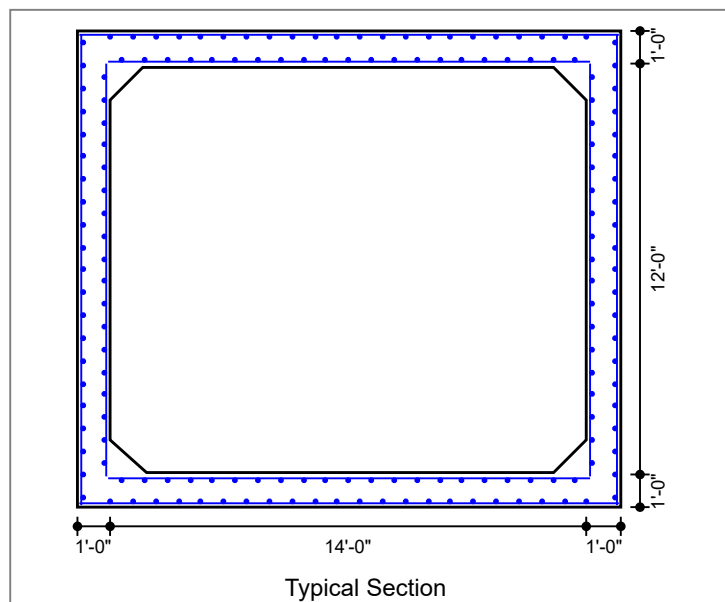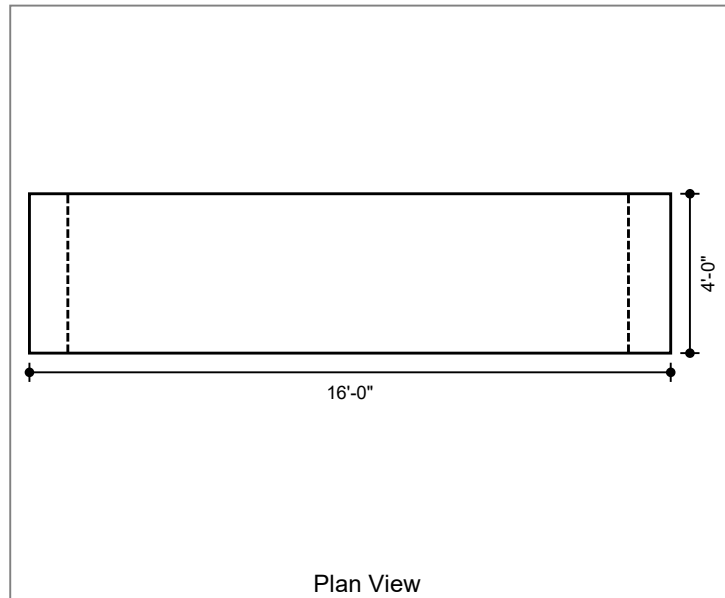

MATT CHILDS ENGINEERING, PLLC

Sht ____ of ____

By:MBJ

Ck:_____

6/5/2026 4:35:09 PM

p. 2 of 2

Project : City of Wilder

Task : 14x12 15' Fill

Client: ICast

Job No. :

File: 20260605-ICast-CityofWilder-14x12(15'Fill).etcx

Concrete Summary

Volume of Concrete: 2.148 cy/ft Total Volume of Concrete: 8.593 cy

Reinforcing Steel Bar Schedule (lb)

Location	Mark	Sheets Included	As Provided
Top Slab(Int)	A100 (AS2)	Top	1.200
Bot Slab(Int)	A200 (AS3)	Bot	1.290
Top Slab(Ext)	A300 (AS7)	Top	0.300
Bot Slab(Ext)	A400 (AS8)	Bot	0.300
Corner(Top)	A1 (AS1)	Top	0.780
Corner(Bot)	A2 (AS1)	Bot	0.780
Wall(Int)	B1 (AS4)	L&R	0.300
Wall(Ext)	B2 (AS1)	L&R	0.780
Longit. Top (Int)	C100 (AS5)	Top	0.150
Longit. Bot (Int)	C200	Bot	0.150
Longit. Top (Ext)	C1 (AS6)	Top	0.150
Longit. Bot (Ext)	C1 (AS6)	Bot	0.150
Longit. Wall (Ext)	C1 (AS6)	L&R	0.150
Longit. Wall (Int)	C1 (AS6)	L&R	0.150

Job Name: 26-1394 - TMMI Ryder Lift Station
Job Location: Princeton, IN
Contractor: Koberstein Contracting, Inc.

Plant: 100

7/16/2026 2:28:59 PM

Tech: Jared - A

PC: A. Chambers



Structure ID: 4 VV

P2 BX060096-08LD08SP

BX FLAT LID 8"W w/37"x36" HATCH F/F


- P3) 37" x 36" - HATCH (CAST FLUSH) - 3"
P2) 60" x 96" - BX FLAT LID 8"W w/37"x36" HATCH F/F - 8"
P1) 60" x 96" - BX BASE w/FLANGE 08W/08F/06EF F/n - 85"
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212
1) This Structure Includes a Cast-in Item - 37" x 36" Hatch (Supplied by Others)
1) SECONDARY POUR
1) LADDER (Alum.) - HALLIDAY L1D 84in Floor-Ceiling Mount Ladder
1) 60" x 96" - Conseal CS-102 1.00" (Double)
8) PSX - 8QRS-S NYLO

Structure Total:


0 lb
4820 lb
26684 lb
0 lb
0 lb
0 lb
0 lb
65 lb
0 lb
52 lb
31621 lb

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. USF FABRICATION 37" X 36" (36" X 36" CLEAR OPENING) HATCH SUPPLIED BY OTHERS - TO BE CAST INTO FLAT LID
5. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN
6. TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH

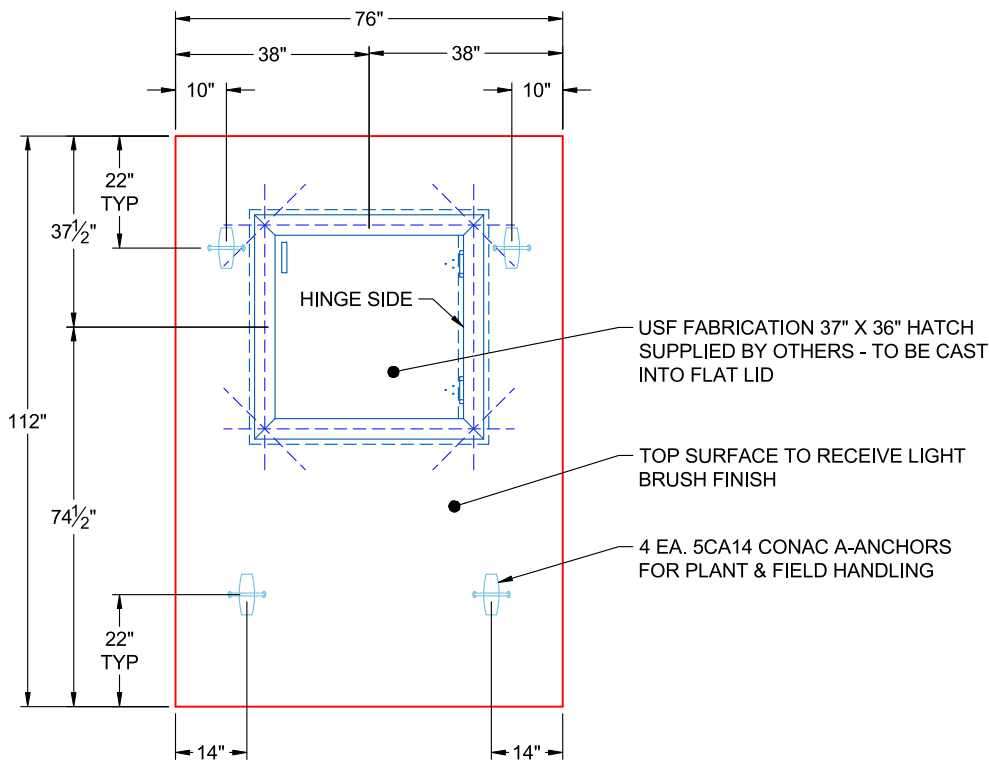


**PLAN VIEW
(RIGHT SIDE UP)**



**FRONT VIEW
(RIGHT SIDE UP)**

#5 BAR @ 6" C.C. E.W. (GRADE 60)



**SIDE VIEW
(RIGHT SIDE UP)**

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 4820 lb
Volume (Net): 1.23cu.yd

Job Number:

26-1394

Job Name:

TMMI Ryder Lift Station


Structure:

4 VV


Note:

USF Fabrication 37" x 36" Hatch
Supplied By Others To Be Cast Into
Flat Lid


Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:28 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 07 ST-SCB											
P1 BX2436-08BA36 BOX BASE 8inW, 8inF											
P3) 18" x 36" - CASTING HEIGHT - 5.5" P2) 24" x 36" - CB FLAT TOP 8"W (18"x36" HOLE) - 8" P1) 24" x 36" - BOX BASE 8inW, 8inF - 36" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 16 1) Hole - 10						0 lb 961 lb 4739 lb 0 lb 0 lb 0 lb ----- Structure Total: 5700 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 580 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 1069.65' Rim to Invert: 4.16' Slack: 0.42" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1065.49'	90°	17"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	-9"	
Invert 2	1065.49'	240°	12.144"	6" HDPE	6.9"	Hole 10	10"	11.547"	-0.45"	-2"	
Invert 3	1065.49'	270°	35"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	9"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

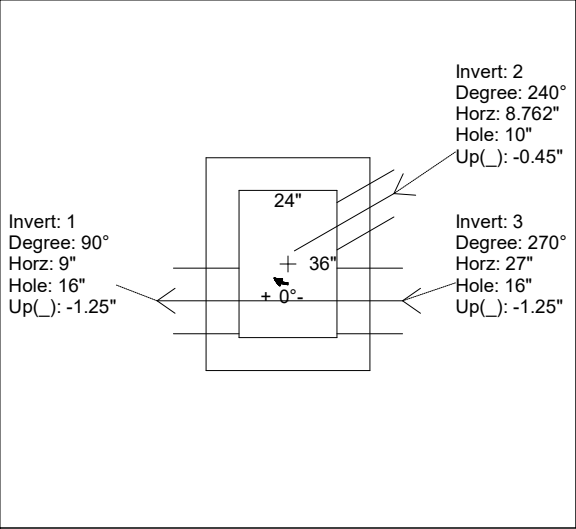

RIGHT-SIDE UP VIEW (int. dimensions)

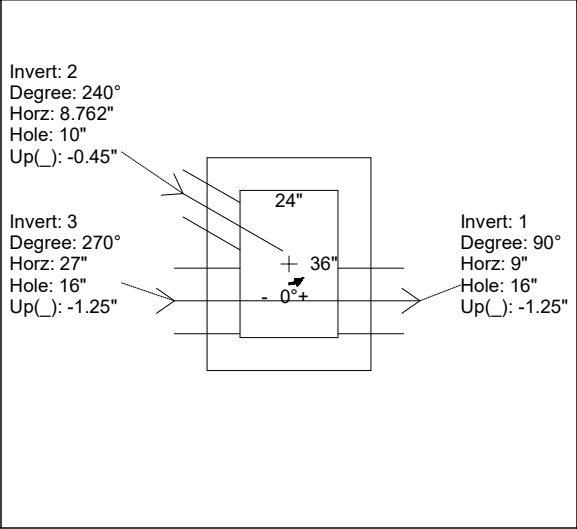


UPSIDE-DOWN VIEW (int. dimensions)

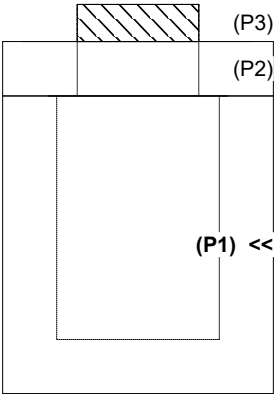


(P1) <<

INSIDE WALL DIMENSIONS

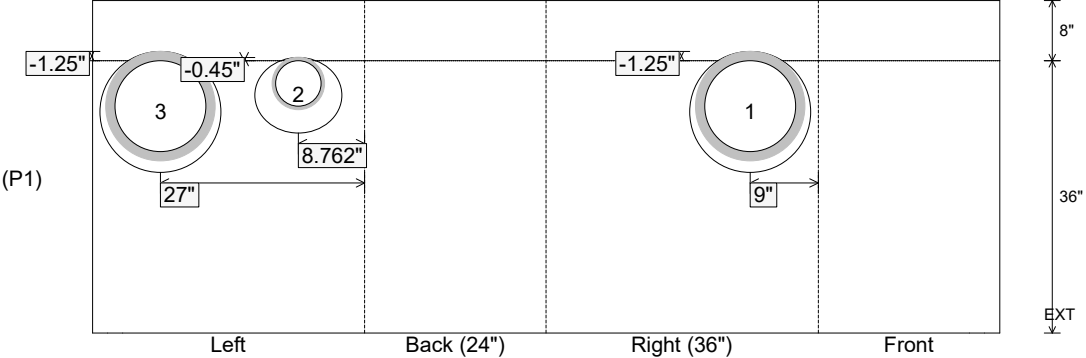

Left Back (24") Right (36") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4739 lb Volume (Net): 1.21cu.yd
----------------------------------	-------------------------------	--	--	--



Weight (Net): 3069 lb
Volume (Net): 0.78cu.yd

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)

Job Location: Independence, KY

Contractor: Eaton Asphalt

Plant: 100

6/4/2026 4:51:20 PM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 588

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10"

P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18"

P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 29"

1) CASTING - HOE KY-206 F/C (KY TY1)

1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast)

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 22

2) Hole - 8

3400 lb

5270 lb

4100 lb

206 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 12976 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TY A / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. NO STORM INVERT

5. NO STEPS

6. KY-206 FRAME & COVER "STORM" SUPPLIED BY iCAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP

7. INVERT 2 OFFSET 14" FROM CENTER OF WALL

Rim: 910.45'

Rim to Invert: 4.75'


Slack: 0"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	905.7'	0°	20"	15" ADS N-12	18"	Hole 22	22"	22"	-3.5"	0"
Invert 2	907.28'	90°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	17"	-14"
Invert 3	907.28'	180°	20"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	17"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

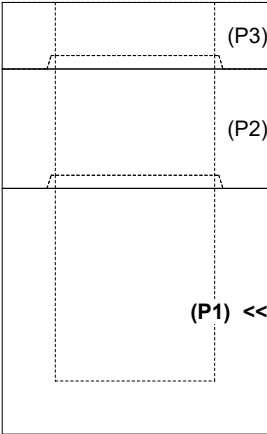

UPSIDE-DOWN VIEW (int. dimensions)

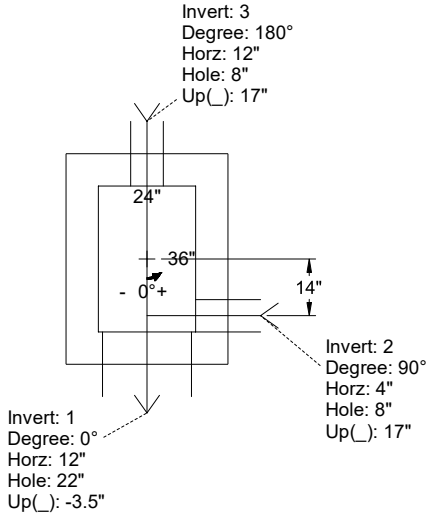

INSIDE WALL DIMENSIONS

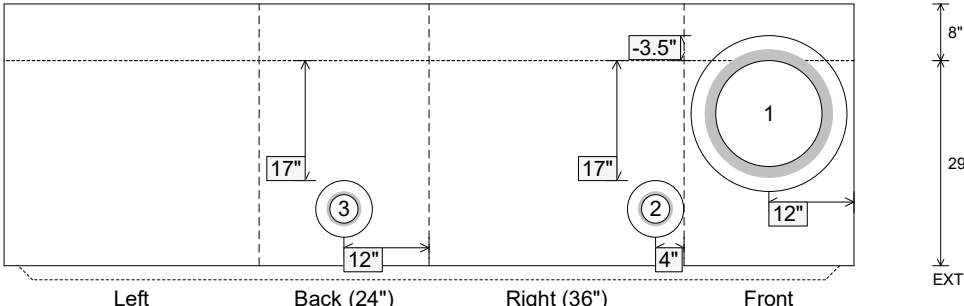

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 29"

Height (Ext): 37"

Weight (Net): 4100 lb

Volume (Net): 1.05cu.yd

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)

Job Location: Independence, KY

Contractor: Eaton Asphalt

Plant: 100

6/4/2026 4:51:19 PM

Tech: Jared - A

PC: J. Jarvis



Structure ID: 584

P1 BX2436-08BVF

BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10"

P2) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18"

P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 27"

1) CASTING - HOE KY-206 F/C (KY TY1)

1) This Structure Includes a Cast-in Item - KY-206 Frame (Supplied by iCast)

1) 24" x 36" - Conseal CS-102 1.00"

2) Hole - 24

1) Hole - 20

2) Hole - 8

3400 lb

5270 lb

3552 lb

206 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 12428 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC CBI TY A / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. NO STORM INVERT

5. NO STEPS

6. KY-206 FRAME & COVER "STORM" SUPPLIED BY ICAST - FRAME TO BE CAST INTO TOP PHASE TOP FLANGE SIDE UP

7. INVERTS 4 & 5 OFFSET 14" FROM CENTER OF WALL

Rim: 893.72'

Rim to Invert: 4.64'


Slack: 0.68"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	889.08'	0°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"
Invert 2	889.08'	180°	20"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"
Invert 3	889.08'	270°	26"	15" ADS N-12	18"	Hole 20	20"	20"	-2.5"	0"
Invert 4	890.5'	90°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	15"	-14"
Invert 5	890.5'	270°	12"	4" HDPE (perf pipe)	4.8"	Hole 8	8"	8"	15"	-14"
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

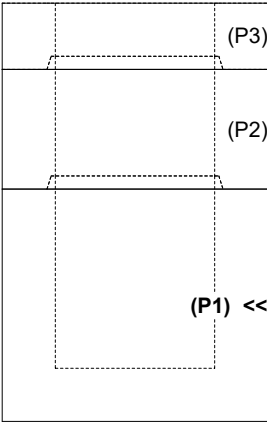

UPSIDE-DOWN VIEW (int. dimensions)

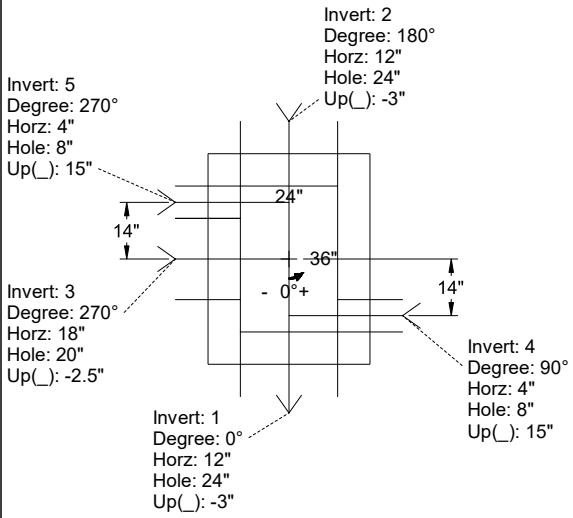

INSIDE WALL DIMENSIONS

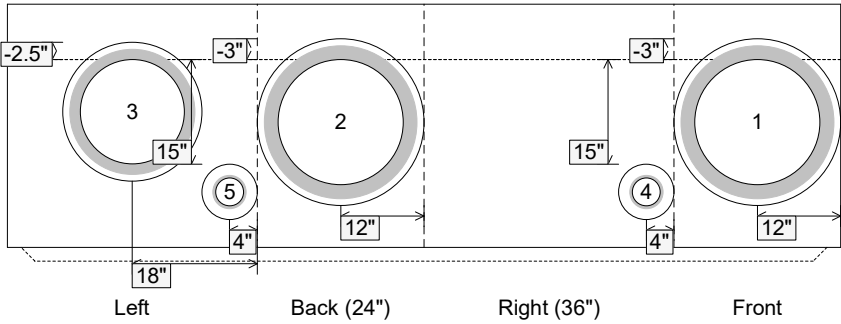

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"





Floor Height: 8"

Height (Int): 27"


Height (Ext): 35"

Weight (Net): 3552 lb


Volume (Net): 0.91cu.yd

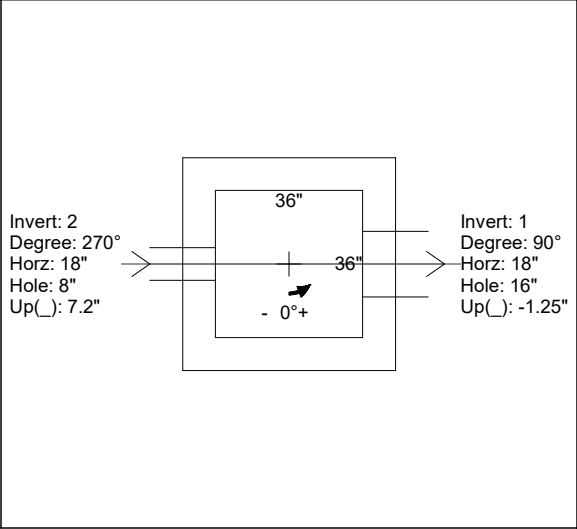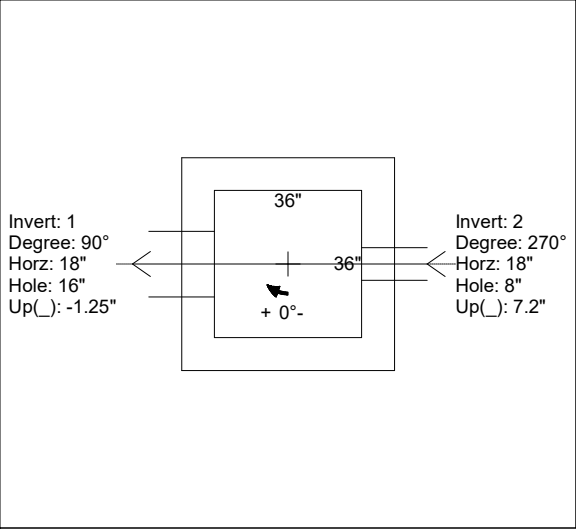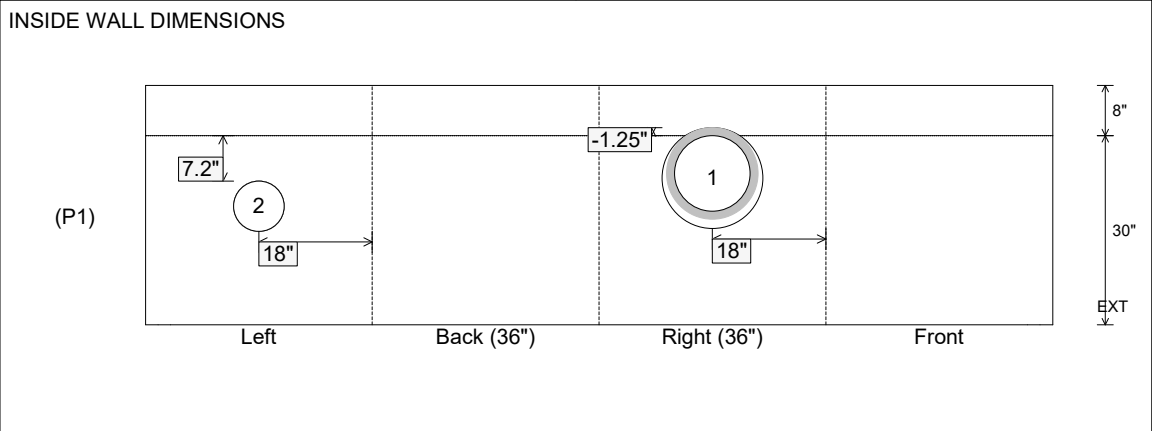Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC					Plant: 100 8/3/2026 11:45:32 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 12 ST-SCB											
P1 BX3636-08BA30 BOX BASE 8inW, 8inF											
P2) 36" x 36" - CASTING HEIGHT - 3" P1) 36" x 36" - BOX BASE 8inW, 8inF - 30" 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 16 1) Hole - 8					0 lb 5191 lb 0 lb 0 lb 0 lb Structure Total: 5191 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1063.2' Rim to Invert: 2.8' Slack: 0.6" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	1060.4'	90°	26"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"	
Invert 2	1061'	270°	26"	8" Hole	8"	Hole 8	8"	8"	7.2"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Flat Seam Dn: n/a Wall Thickness: 8" Floor Height: 8" Height (Int): 30" Height (Ext): 38" Weight (Net): 5191 lb Volume (Net): 1.33cu.yd											

Job Name: 26-2146 - Fairview Apartments Job Location: Russell Springs, KY 42642 Contractor: Dirt Design Construction LLC				Plant: 100 8/3/2026 11:45:38 AM		Tech: J. Horsley PC: M. Sullivan				
Structure ID: 22 ST-DCB										
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht						
P2) 36" x 36" - CASTING HEIGHT - 3" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 35" 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16				0 lb 5597 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5597 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 1067.95' Rim to Invert: 3.24' Slack: 0.88" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	1064.71'	15°	29.861"	15" HDPE	17.6"	Hole 20	20"	20.706"	-1.3"	-3"
Invert 2	1064.71'	270°	26"	12" HDPE	14.5"	Hole 16	16"	16"	-1.25"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										




RIGHT-SIDE UP VIEW (int. dimensions)



Invert: 2
Degree: 270°
Horz: 18"
Hole: 16"
Up(-): -1.25"

Invert: 1
Degree: 15°
Horz: 19.717"
Hole: 20"
Up(-): -1.3"


UPSIDE-DOWN VIEW (int. dimenions)



Invert: 2
Degree: 270°
Horz: 18"
Hole: 16"
Up(-): -1.25"

Invert: 1
Degree: 15°
Horz: 19.717"
Hole: 20"
Up(-): -1.3"

INSIDE WALL DIMENSIONS

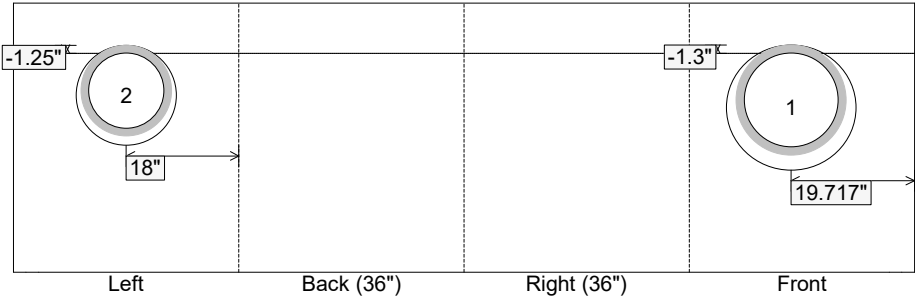

(P1)

Left

Back (36")

Right (36")


Front

EXT


Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 35" Height (Ext): 43"	Weight (Net): 5597 lb Volume (Net): 1.43cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 8/3/2026 12:43:26 PM		Tech: Jared - F PC: A. Chambers			
Structure ID: D1 DBI2										
P1 BX3648-08BA60 BOX BASE 8inW, 8inF F/n										
P2) 36" x 48" - P.I.P. - BY OTHERS - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60" 1) CASTING - HOE KY-398 SET (DBI 2) 1) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 40 1) Hole - 10					0 lb 9393 lb 398 lb 0 lb 0 lb 0 lb ----- Structure Total: 9791 lb		Structure Notes: 1. KYTC DBI TYPE 2 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-398 SET (DBI 2)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 367.57' Rim to Invert: 5.36' Slack: 1.32" Sump: 5" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	362.21'	90°	32"	30" RCP B WALL	37"	Hole 40	40"	40"	0"	0"
Invert 2	364.7'	180°	26"	6" HDPE	6.9"	Hole 10	10"	10"	32.875"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


#5 DOWELS @ 12" O.C.
STUBBED 20" OUT THE
TOP OF THE WALLS

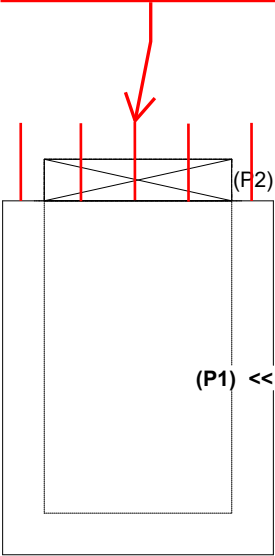


RIGHT-SIDE UP VIEW (int. dimensions)

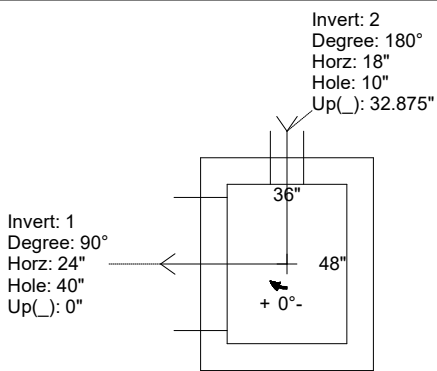

UPSIDE-DOWN VIEW (int. dimensions)

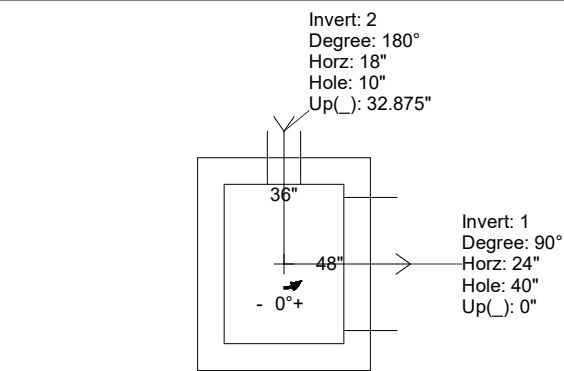

INSIDE WALL DIMENSIONS

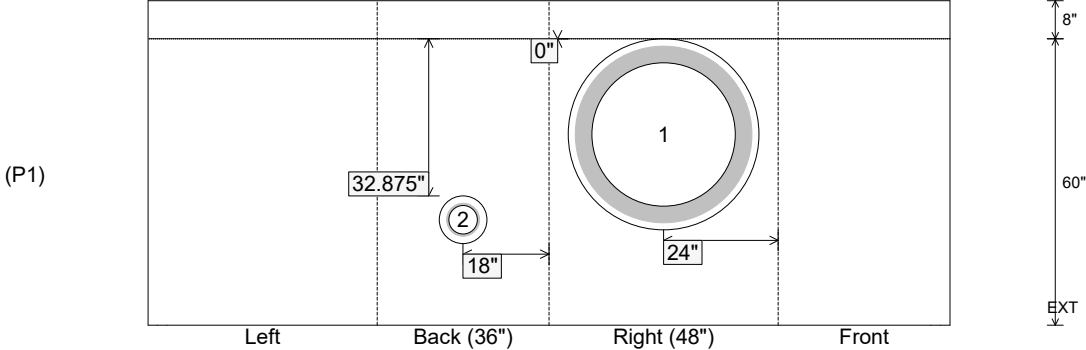

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 9393 lb Volume (Net): 2.4cu.yd
----------------------------------	-------------------------------	--	--	---

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100
7/10/2026 10:21:02 AM

Tech: Jared - F
PC: E. Bardley



Structure ID: QL70-3 POND3

P1 BX4848-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 48" x 48" - BX FLAT LID 8inW w/CC 24"x24" HOLE - 8"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 36"
1) CASTING - HOE-326-BH F/G
1) 48" x 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 0

Structure Notes: .
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE-326-BH F/G OR EJ 6626).
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Structure Total:



0 lb
2363 lb
8163 lb
289 lb
0 lb
0 lb
0 lb
10815 lb

Rim: 683' Rim to Invert: 4' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	679'	0°	32"	0" No Hole	0.01"	Hole 0	0"	0"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

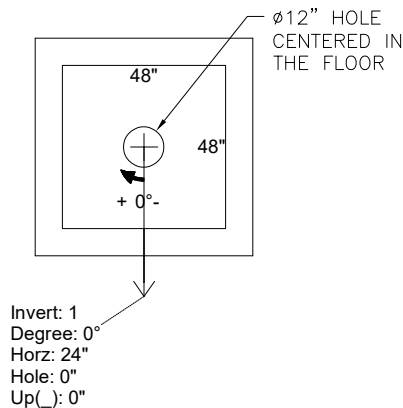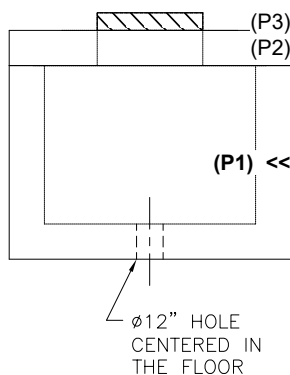

INSIDE WALL DIMENSIONS

(P1)



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 8163 lb
Volume (Net): 2.08cu.yd

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100

7/10/2026 10:21:01 AM

Tech: Jared - F

PC: E. Bardley



Structure ID: QL70-2 POND1

P1 BX4848-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 48" x 48" - BX FLAT LID 8inW w/CC 24"x24" HOLE - 8"
P1) 48" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 36"
1) CASTING - HOE-326-BH F/G
1) 48" x 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 0

Structure Total: 10815 lb



Structure Notes:
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE-326-BH F/G OR EJ 6626).
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

Rim: 652' Rim to Invert: 4' Slack: 0" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	648'	0°	32"	0" No Hole	0.01"	Hole 0	0"	0"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

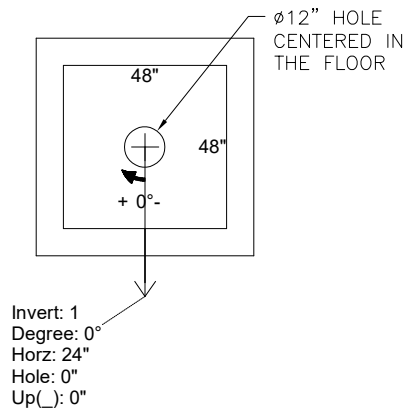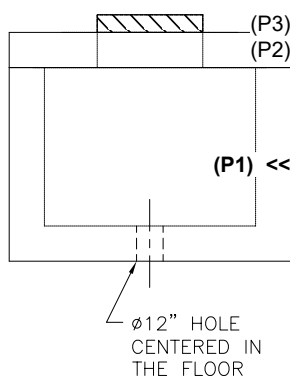

INSIDE WALL DIMENSIONS

(P1)



Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 36"
Height (Ext): 44"

Weight (Net): 8163 lb
Volume (Net): 2.08cu.yd

Job Number:

25-2952

Job Name:

KYTC Jefferson Co Call 106
(251315)

Structure:

63

Note:

HOE KY-210 Frame Supplied By
Others To Be Cast Into Flat Lid

Job Name: 26-1787 - Kroger Expansion
Job Location: Murray, KY
Contractor: Parker Excavating, LLC.

Plant: 100

7/22/2026 3:26:57 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: D1 ST-IN

P2 BX024048-08LD08S

BX FLAT LID 8inW SPEC. (JBS-3061) F/F


P3) 24" x 48" - CASTING HEIGHT - 0"
P2) 24" x 48" - BX FLAT LID 8inW SPEC. (JBS-3061) F/F - 8"
P1) 24" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 50"
1) SECONDARY POUR
1) CASTING - JBS 3061 F/G
1) 24" x 48" - Conseal CS-102 1.00"
1) Hole - 30
4) Hole - 6

0 lb
945 lb
7194 lb
0 lb
250 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 8389 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (JBS 3061 F/G CAST FLUSH).
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

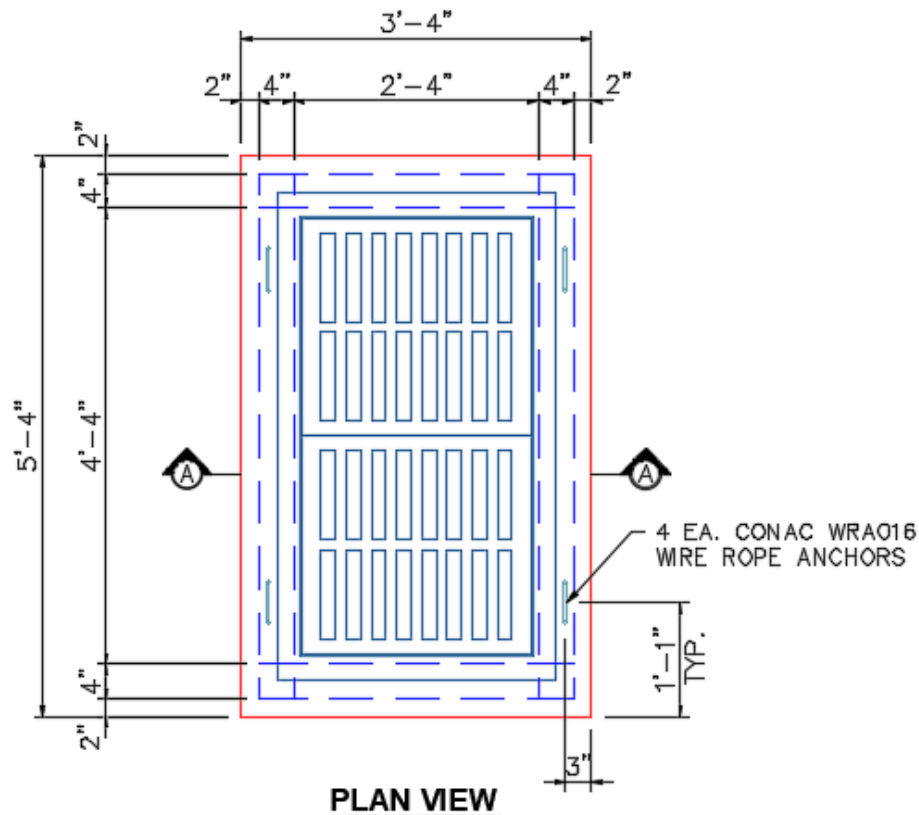

PLAN VIEW



SECTION A-A

#5 BAR CUT LIST

2 EA. @ 60" LG.
2 EA. @ 36" LG

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 945 lb
Volume (Net): 0.24cu.yd

Job Name: 26-2146 - Fairview Apartments
Job Location: Russell Springs, KY 42642
Contractor: Dirt Design Construction LLC

Plant: 100

8/3/2026 11:47:15 AM

Tech: J. Horsley

PC: M. Sullivan



Structure ID: 09 ST-DCB

P2 BX2436_08LD08

CB FLAT TOP 8"W (18"x36" HOLE)

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 24" x 36" - CB FLAT TOP 8"W (18"x36" HOLE) - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 22"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 16


Structure Total: 4332 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY OTHERS (HOE 580 F/G)

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

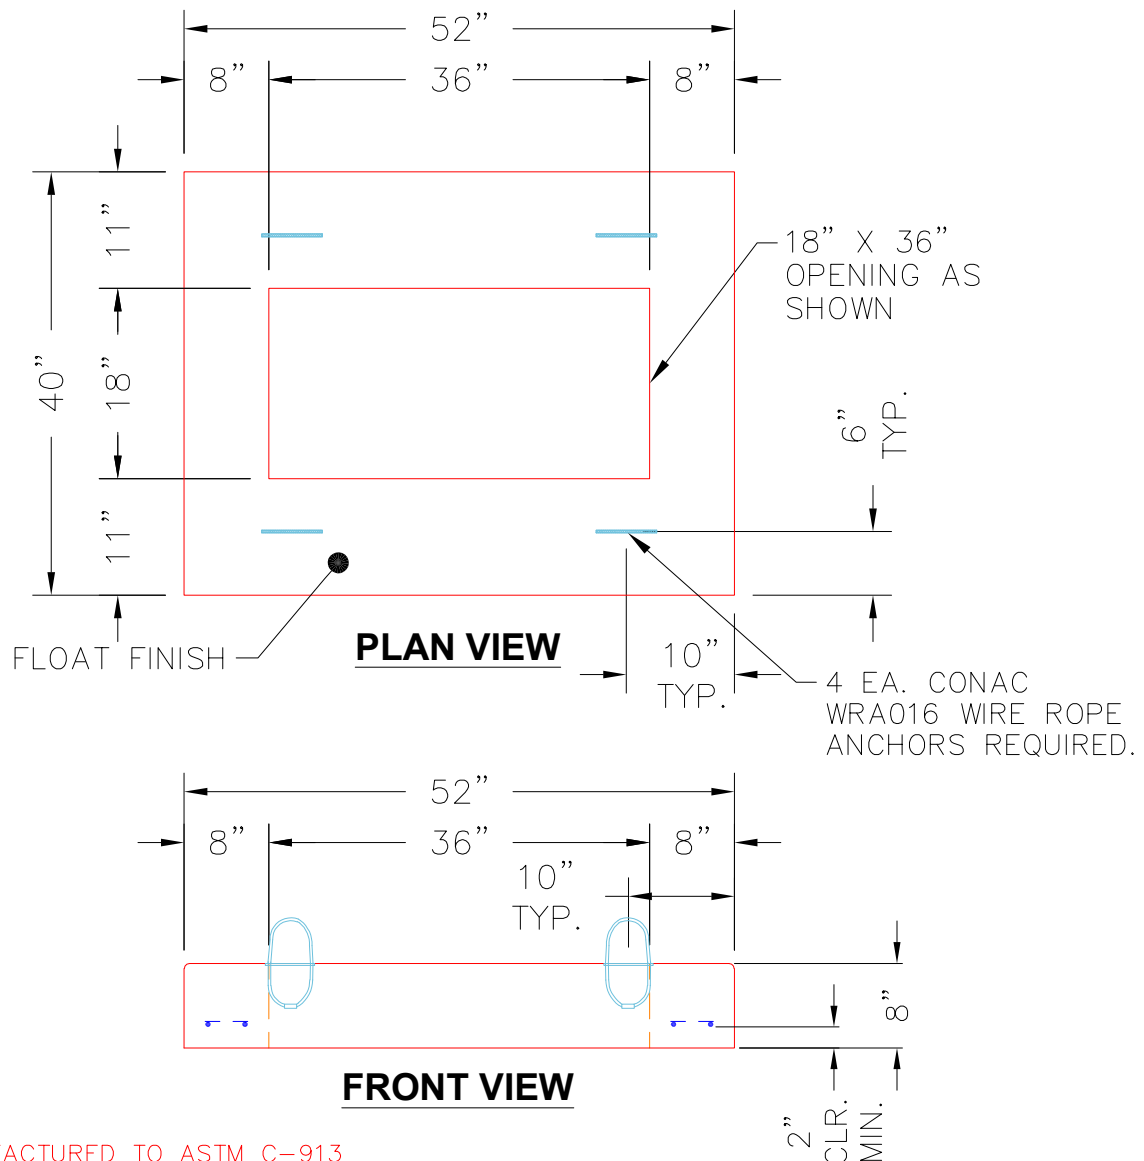

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: H20 LOADING #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 961 lb
Volume (Net): 0.25cu.yd

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2

Job Location: Sturgis, KY

Contractor: M. Bowling, Inc.

Plant: 100

7/31/2026 11:12:12 AM

Tech: Jared - F

PC: A. Chambers

Structure ID: C3 DBI7

P1 BX3654-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 36" x 36" - P.I.P. - BY OTHERS - 8"

P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 50"

P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70"

1) CASTING - HOE KY-328 SET (DBI 7)

2) 36" x 54" - Conseal CS-102 1.00"

2) Hole - 54

1) Hole - 10

0 lb

7055 lb

10099 lb

328 lb

0 lb

0 lb

0 lb

Structure Total: 17482 lb

Structure Notes:

1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)

4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W..

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 367.96'

Rim to Invert: 10.2'

Slack: 0.4"

Sump: 6"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	357.76'	90°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	0"	0"
Invert 2	357.96'	270°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

WEIGHTS

FIRST POUR - 2,443 LBS

SECOND POUR - 7,656 LBS

TOTAL - 10,099 LBS

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 70"

Height (Ext): 78"

Weight (Net): 10099 lb

Volume (Net): 2.58cu.yd

1ST POUR (FLOOR)

STUB #5 L BARS OUT

TOP FLOOR, SPA AT

12" C/C FOR

CONNECTING WALLS

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2

Job Location: Sturgis, KY

Contractor: M. Bowling, Inc.

Plant: 100

7/31/2026 11:12:12 AM

Tech: Jared - F

PC: A. Chambers

Structure ID: C3 DBI7

P1 BX3654-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

P3) 36" x 36" - P.I.P. - BY OTHERS - 8"

P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 50"

P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70"

1) CASTING - HOE KY-328 SET (DBI 7)

2) 36" x 54" - Conseal CS-102 1.00"

2) Hole - 54

1) Hole - 10

0 lb

7055 lb

10099 lb

328 lb

0 lb

0 lb

0 lb

Structure Total: 17482 lb

Structure Notes:

1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)

4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)).

REINFORCING PER ASTM A615 (GRADE 60).

- WALLS (As .31) #5 BARS AT 12" C.C.E.W..

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 367.96'

Rim to Invert: 10.2'

Slack: 0.4"

Sump: 6"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	357.76'	90°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	0"	0"
Invert 2	357.96'	270°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

WEIGHTS

FIRST POUR - 2,443 LBS

SECOND POUR - 7,656 LBS

TOTAL - 10,099 LBS

INSIDE WALL DIMENSIONS

Coating (Int):

Coating (Ext):

Seam Up: Tongue

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 70"

Height (Ext): 78"

Weight (Net): 10099 lb

Volume (Net): 2.58cu.yd

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2
Job Location: Sturgis, KY
Contractor: M. Bowling, Inc.

Plant: 100

7/31/2026 11:12:11 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: C2 DBI7

P1 BX3654-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 42"
P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70"
1) CASTING - HOE KY-328 SET (DBI 7)
2) 36" x 54" - Con Seal CS-102 1.00"
1) Hole - 54
1) Hole - 48
1) Hole - 10

0 lb
5916 lb
10038 lb
328 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 16282 lb

Structure Notes:


1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)).
- REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 368.27' Rim to Invert: 9.56' Slack: 0.72" Sump: 6" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	358.71'	90°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	0"	0"
Invert 2	358.91'	270°	35"	36" RCP B WALL	44"	Hole 48	48"	48"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

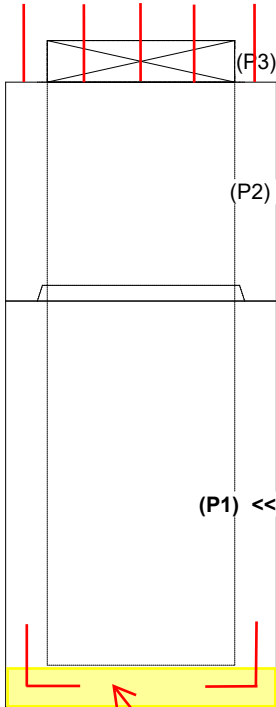

Invert: 1
Degree: 90°
Horz: 27"
Hole: 54"
Up(): 0"

Invert: 2
Degree: 270°
Horz: 27"
Hole: 48"
Up(): 2.375"

WEIGHTS

FIRST POUR - 2,443 LBS


SECOND POUR - 7,595 LBS

TOTAL - 10,038 LBS

Invert: 2
Degree: 270°
Horz: 27"
Hole: 48"
Up(): 2.375"

Invert: 1
Degree: 90°
Horz: 27"
Hole: 54"
Up(): 0"

INSIDE WALL DIMENSIONS

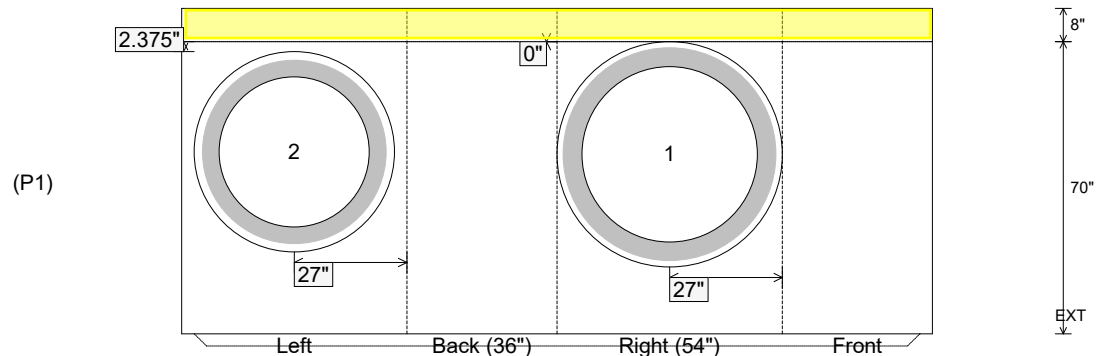

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 70"
Height (Ext): 78"

Weight (Net): 10038 lb
Volume (Net): 2.56cu.yd

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2
Job Location: Sturgis, KY
Contractor: M. Bowling, Inc.

Plant: 100

7/31/2026 11:12:11 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: C2 DBI7

P1 BX3654-08BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
P2) 36" x 54" - BOX RISER 8inW, Variable Ht F/G - 42"
P1) 36" x 54" - BOX BASE 8inW, 8inF, Variable Ht T/n - 70"
1) CASTING - HOE KY-328 SET (DBI 7)
2) 36" x 54" - Con Seal CS-102 1.00"
1) Hole - 54
1) Hole - 48
1) Hole - 10

0 lb
5916 lb
10038 lb
328 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 16282 lb

Structure Notes:


1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)).
- REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 368.27' Rim to Invert: 9.56' Slack: 0.72" Sump: 6" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	358.71'	90°	35"	42" RCP B WALL	51"	Hole 54	54"	54"	0"	0"
Invert 2	358.91'	270°	35"	36" RCP B WALL	44"	Hole 48	48"	48"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

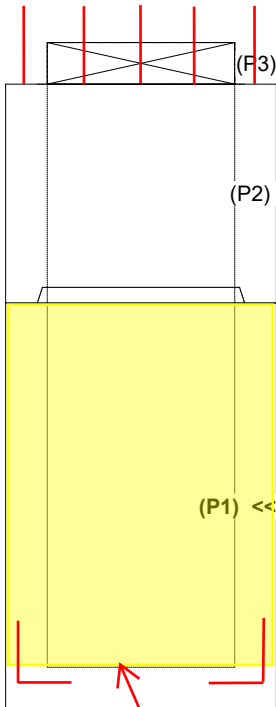

Invert: 1
Degree: 90°
Horz: 27"
Hole: 54"
Up(): 0"



Invert: 2
Degree: 270°
Horz: 27"
Hole: 48"
Up(): 2.375"


WEIGHTS

FIRST POUR - 2,443 LBS

SECOND POUR - 7,595 LBS


TOTAL - 10,038 LBS

Invert: 2
Degree: 270°
Horz: 27"
Hole: 48"
Up(): 2.375"



Invert: 1
Degree: 90°
Horz: 27"
Hole: 54"
Up(): 0"

INSIDE WALL DIMENSIONS

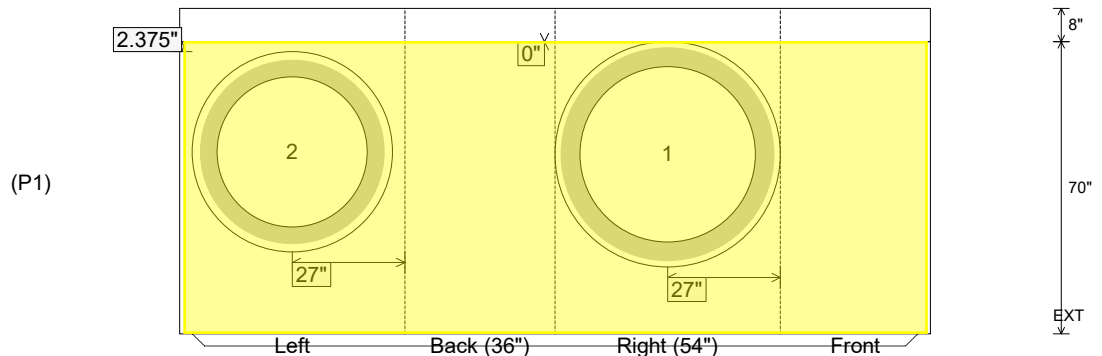

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 70"
Height (Ext): 78"

Weight (Net): 10038 lb
Volume (Net): 2.56cu.yd

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2
Job Location: Sturgis, KY
Contractor: M. Bowling, Inc.

Plant: 100

7/31/2026 11:12:13 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: C4 DBI7

P1 BX6072-08W08F-BAVF

BOX BASE 8inW, 8inF, Variable Ht T/n

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
P2) 60" x 72" - BOX RISER 8inW, Variable Ht F/G - 55"
P1) 60" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 82"
1) CASTING - HOE KY-328 SET (DBI 7)
2) 60" x 72" - Con Seal CS-102 1.00"
1) Hole - 62
1) Hole - 40
1) Hole - 54
1) Hole - 10

0 lb
10876 lb
15713 lb
328 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 26917 lb

Structure Notes:

1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C)
 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)).
- REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 368.36' Rim to Invert: 11.55' Slack: 0.6" Sump: 7" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	356.81'	60°	39.375"	48" RCP B WALL	58"	Hole 62	62"	71.591"	0"	15"
Invert 2	358.7'	315°	29.375"	30" RCP B WALL	37"	Hole 40	40"	56.569"	24.625"	25"
Invert 3	357.01'	270°	44"	42" RCP B WALL	51"	Hole 54	54"	54"	3.375"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

WEIGHTS


FIRST POUR - 4,489 LBS

SECOND POUR - 11,224 LBS

TOTAL - 15,713 LBS

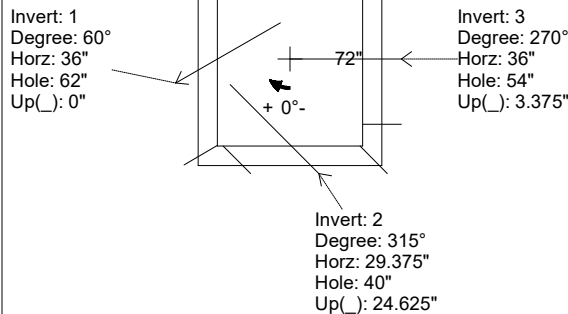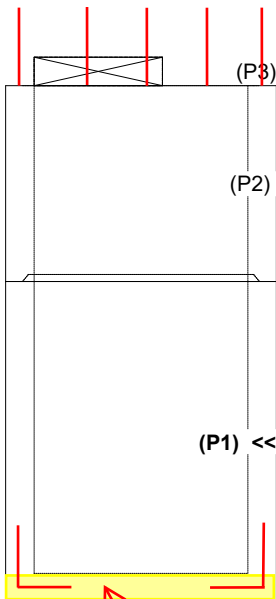

INSIDE WALL DIMENSIONS

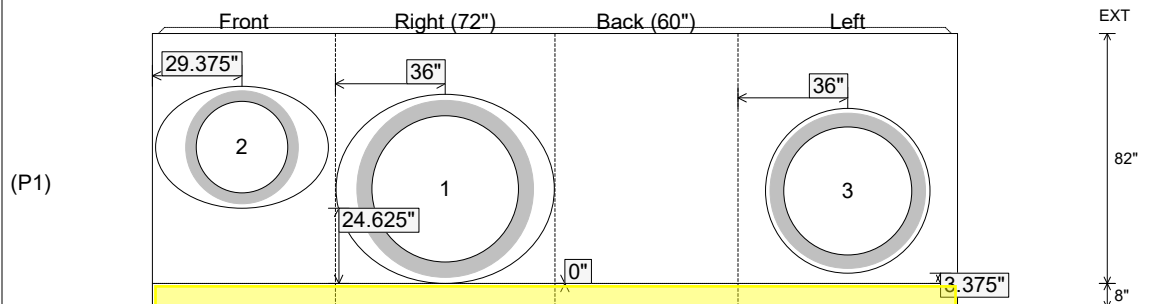

**1ST POUR (FLOOR)
STUB #5 L BARS OUT
TOP FLOOR, SPA AT
12" C/C FOR
CONNECTING WALLS**

Coating (Int):
Coating (Ext):


Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 82"
Height (Ext): 90"


Weight (Net): 15713 lb
Volume (Net): 4.01cu.yd

Job Name: 26-2038 - Sturgis Municipal Airport-Ph2 Job Location: Sturgis, KY Contractor: M. Bowling, Inc.					Plant: 100 7/31/2026 11:12:13 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: C4 DBI7										
P1 BX6072-08W08F-BAVF BOX BASE 8inW, 8inF, Variable Ht T/n										
P3) 36" x 36" - P.I.P. - BY OTHERS - 8" P2) 60" x 72" - BOX RISER 8inW, Variable Ht F/G - 55" P1) 60" x 72" - BOX BASE 8inW, 8inF, Variable Ht T/n - 82" 1) CASTING - HOE KY-328 SET (DBI 7) 2) 60" x 72" - Conseal CS-102 1.00" 1) Hole - 62 1) Hole - 40 1) Hole - 54 1) Hole - 10					0 lb 10876 lb 15713 lb 328 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 26917 lb		Structure Notes: 1. KYTC DBI TYPE 7 / PER ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY ICAST (HOE KY-328 SET (DBI 7)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 368.36' Rim to Invert: 11.55' Slack: 0.6" Sump: 7" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	356.81'	60°	39.375"	48" RCP B WALL	58"	Hole 62	62"	71.591"	0"	15"
Invert 2	358.7'	315°	29.375"	30" RCP B WALL	37"	Hole 40	40"	56.569"	24.625"	25"
Invert 3	357.01'	270°	44"	42" RCP B WALL	51"	Hole 54	54"	54"	3.375"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

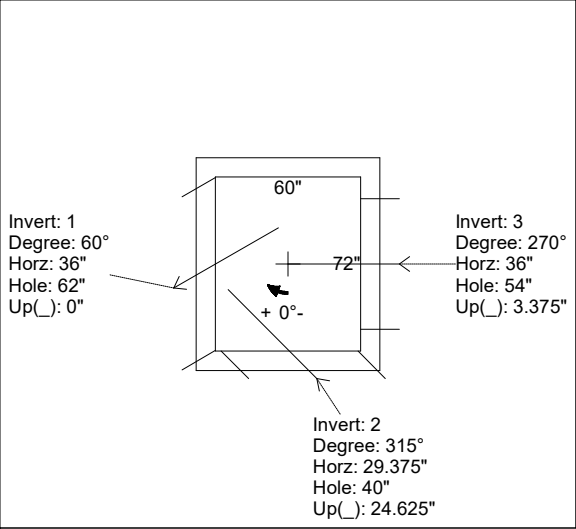


RIGHT-SIDE UP VIEW (int. dimensions)

WEIGHTS
FIRST POUR - 4,489 LBS
SECOND POUR - 11,224 LBS
TOTAL - 15,713 LBS

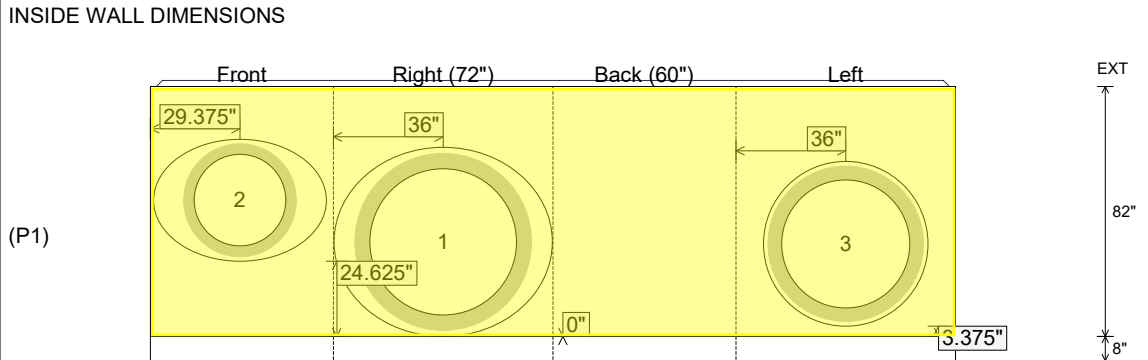

INSIDE WALL DIMENSIONS

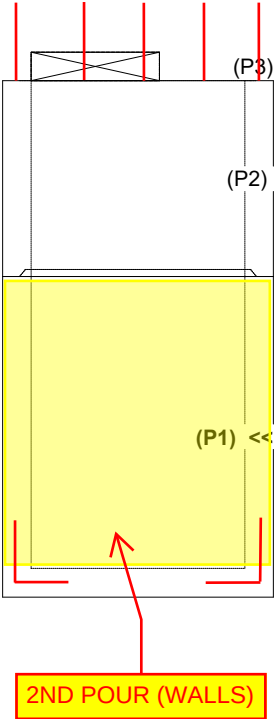

2ND POUR (WALLS)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 82" Height (Ext): 90"	Weight (Net): 15713 lb Volume (Net): 4.01cu.yd
----------------------------------	---------------------------------	--	--	---
