



Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply					Plant: 100 6/15/2026 11:39:51 AM		Tech: Jared - F PC: E. Bradley				
Structure ID: PMH4 SS-MH											
P1 MH048BA30CDARED			MH BASE w/ConBlock-CDA Red T/n								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) ADMIXTURE CONBLOCK CDA RED 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2251 lb 1677 lb 3378 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 8 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 428.6' Rim to Invert: 8.3' Slack: 0.6" Sump: 2" Step Position: 180					Structure Total: 9024 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	420.3'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

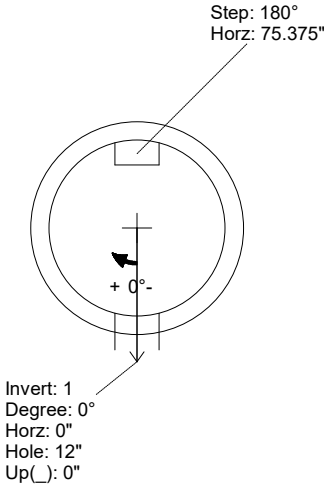

UPSIDE-DOWN VIEW (int. dimensions)

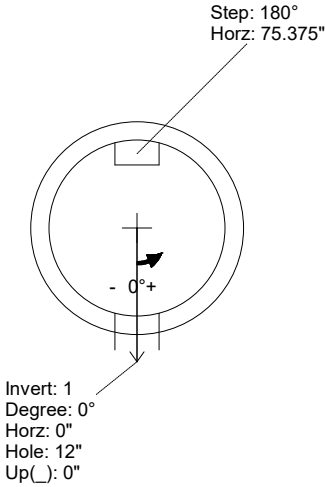


INSIDE WALL DIMENSIONS




Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3378 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--


Job Name: 26-2310 - 3rd & Madison Townhomes - Ph. 1 Job Location: Nashville, TN 37208 Contractor: Hayes Pipe Supply					Plant: 100 6/15/2026 11:39:51 AM		Tech: Jared - F PC: E. Bradley			
Structure ID: PMH4 SS-MH										
P1 MH048BA30CDARED			MH BASE w/ConBlock-CDA Red T/n							
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) ADMIXTURE CONBLOCK CDA RED 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 7) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2251 lb 1677 lb 3378 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 0 lb 8 lb 0 lb ----- Structure Total: 9024 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 428.6' Rim to Invert: 8.3' Slack: 0.6" Sump: 2" Step Position: 180										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	420.3'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

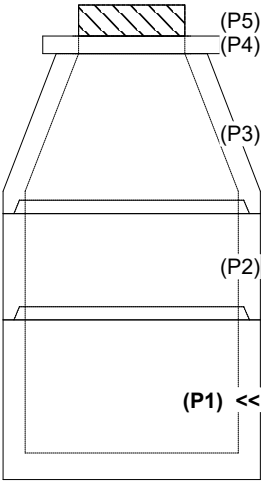


RIGHT-SIDE UP VIEW (int. dimensions)

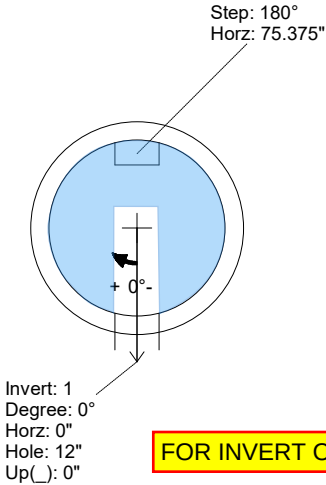

UPSIDE-DOWN VIEW (int. dimensions)

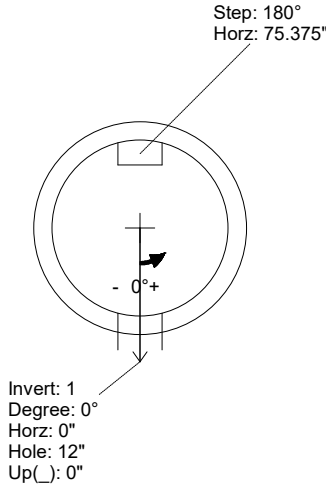

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3378 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--
