

Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements
 Job Location: Louisville, KY 40208
 Contractor: Louisville Paving and Construction

Plant: 100
 4/30/2026 1:22:32 PM

Tech: Jared - F
 PC: J. Jarvis



Structure ID: S211

P2 MH060RS18S

MH RISER T/G

- P4) 32" x 32" - CASTING HEIGHT - 3"
- P3) 60" - MH FLAT TOP w/32"x32" Hole F/G - 13"
- P2) 60" - MH RISER T/G - 18"
- P1) 60" - MH BASE Custom Ht T/n - 64"
- 1) CASTING - HOE 595 F/G
- 2) 60" - Conseal CS-102 1.00"
- 1) 32" x 32" - Conseal CS-102 1.00"
- 2) Hole - 30
- 1) Hole - 20
- 1) Hole - 8

0 lb
 2369 lb
 1854 lb
 8514 lb
 376 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb
 Structure Total: 13112 lb



Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. NO STEPS AND NO INVERT CHANNEL.
 4. CASTING BY ICAST (HOE 595 F/G)

REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


Rim: 454.52' Rim to Invert: 8.48' Slack: 3.76" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	452.21'	276°	173.375"	4" PVC SDR26	4.25"	Hole 8	8"	8.024"	5.125"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

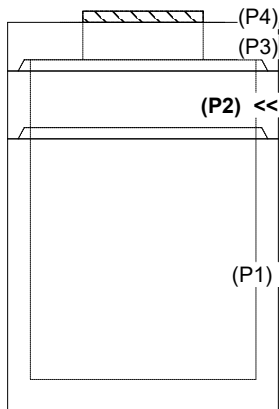

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 18" Height (Ext): 18"	Weight (Net): 1854 lb Volume (Net): 0.47cu.yd
----------------------------------	------------------------------------	--	--	--
