




Job Name: 26-1453 Clarksville, TN SPC13A Job Location: Clarksville, TN Contractor: Cleary Construction, Inc.					Plant: Beaver Dam 6/18/2026 7:40:27 AM		Tech: J. Coppage PC: C. Goff				
Structure ID: 13A-SS-MH-004											
P2 MH060RS48CDARED			MH RISER w/ConBlock-CDA Red								
P6) 24" - CASTING HEIGHT - 6" P5) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 13" P4) 60" - MH RISER w/ConBlock-CDA Red - 36" P3) 60" - MH RISER SPECIAL w/ConBlock-CDA Red - 72" P2) 60" - MH RISER w/ConBlock-CDA Red - 48" P1) 60" - MH BASE w/ConBlock-CDA Red - 30" 1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 4) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) A-Lok - 0285 1) A-Lok - 0410 2) A-Lok - 0200 15) MH Step ML-10-TDS-NCR - 10"						0 lb 2800 lb 3758 lb 7440 lb 5011 lb 5752 lb 0 lb 0 lb 2962 lb 0 lb 0 lb 2 lb 1 lb 2 lb 0 lb		Structure Notes: . 1. JBS-1155 SANITARY PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 543.08'		Rim to Invert: 17.02'		Slack: 1.24"		Sump: 2'		Structure Total: 27728 lb Step Position: 45'			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

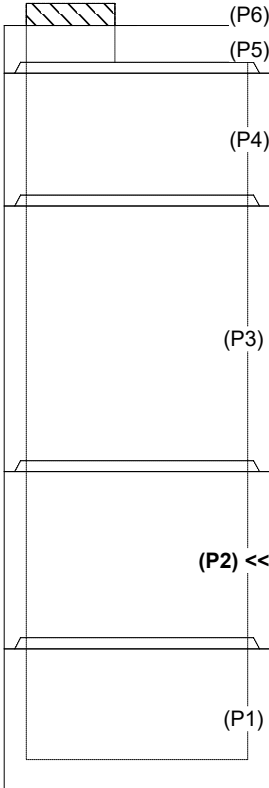

RIGHT-SIDE UP VIEW (int. dimensions)

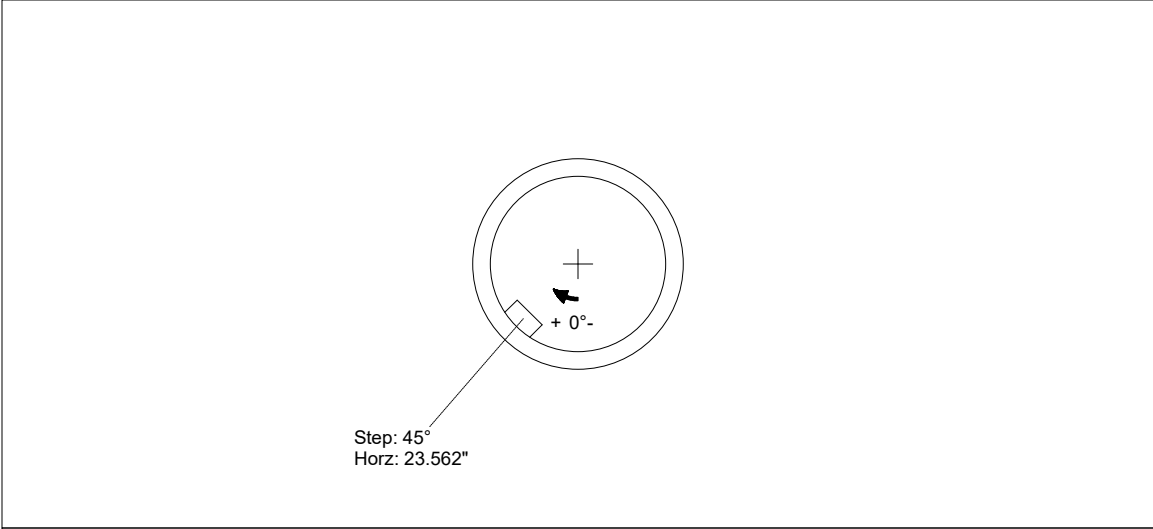

INSIDE WALL DIMENSIONS

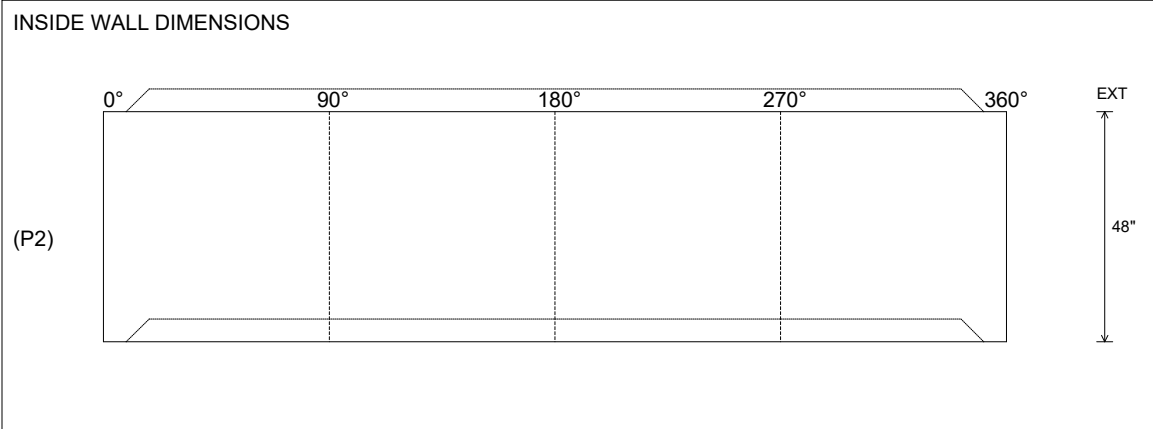

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 5011 lb Volume (Net): 1.28cu.yd
----------------------------------	------------------------------------	--	--	--
