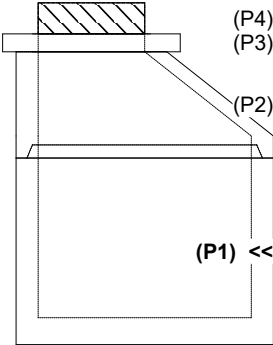
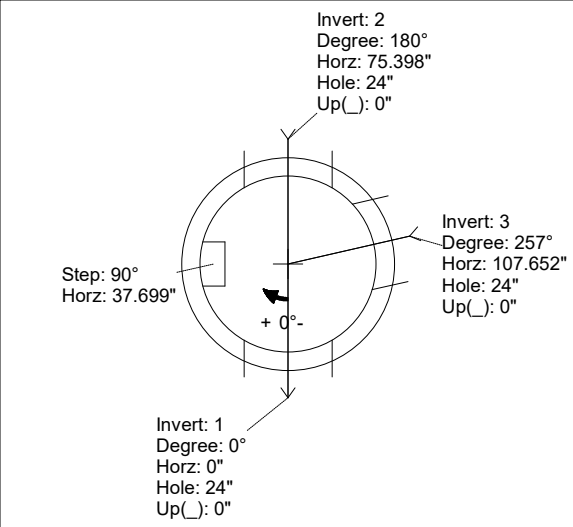
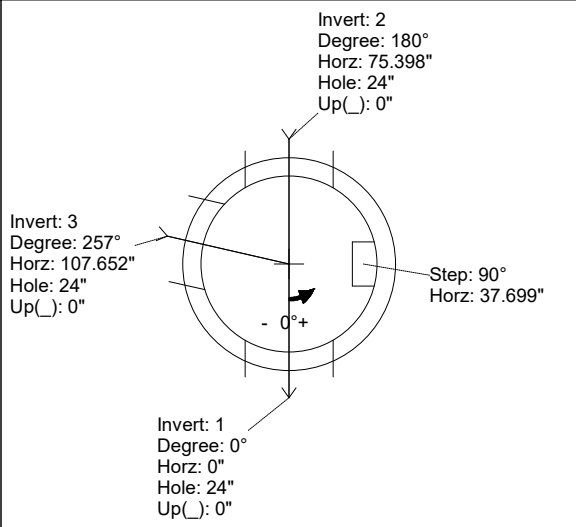
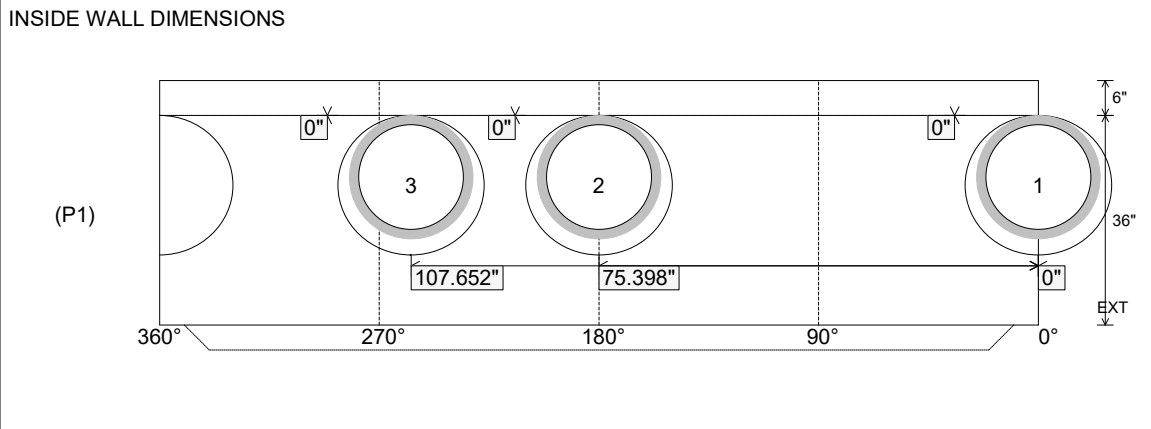


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:02:39 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: Y8.2 ST-MH											
P1 MH048BA36		MH BASE T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 36" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 3) Hole - 24"						0 lb 270 lb 1550 lb 3253 lb 271 lb 0 lb 0 lb 0 lb ----- Structure Total: 5344 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 372.38'		Rim to Invert: 5.89'		Slack: 1.28"		Sump: 1.6"		Step Position: 90°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	366.49'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"	
Invert 2	366.49'	180°	91.106"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"	
Invert 3	366.49'	257°	130.079"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions) INSIDE WALL DIMENSIONS											
   											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 36" Height (Ext): 42"		Weight (Net): 3253 lb Volume (Net): 0.83cu.yd		
