

Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements
Job Location: Louisville, KY 40208
Contractor: Louisville Paving and Construction

Plant: 100

4/30/2026 1:22:57 PM

Tech: Jared - F

PC: J. Jarvis



Structure ID: S108

P2 MH048LD12S

MH FLAT TOP w/32"x32" Hole F/G

- P3) 32" x 32" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/32"x32" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 68"
1) CASTING - HOE 595 F/G
1) 48" - Conseal CS-102 1.00"
1) 32" x 32" - Conseal CS-102 1.00"
2) Hole - 24
2) Hole - 8
1) Hole - 20



0 lb
1629 lb
5509 lb
376 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 7514 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 595 F/G)

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

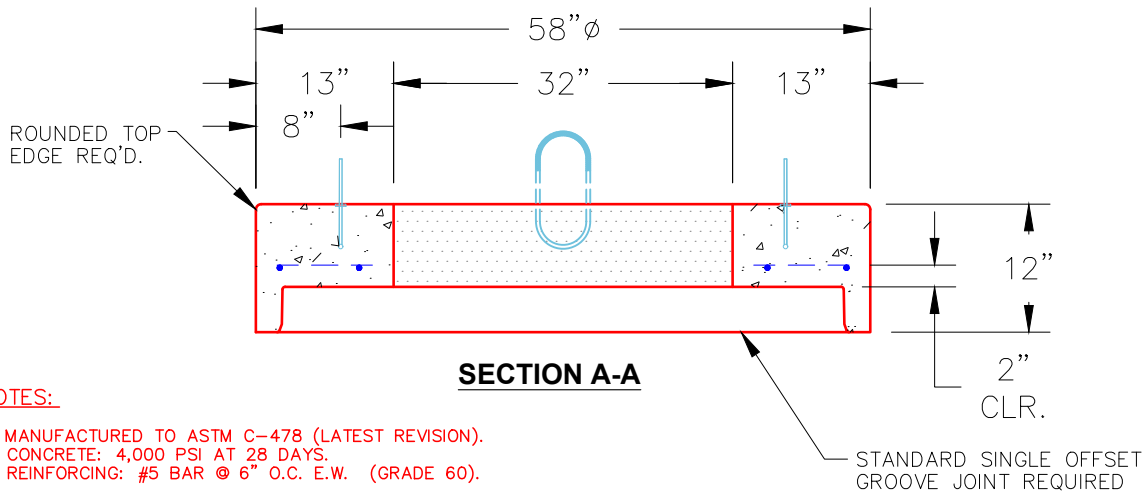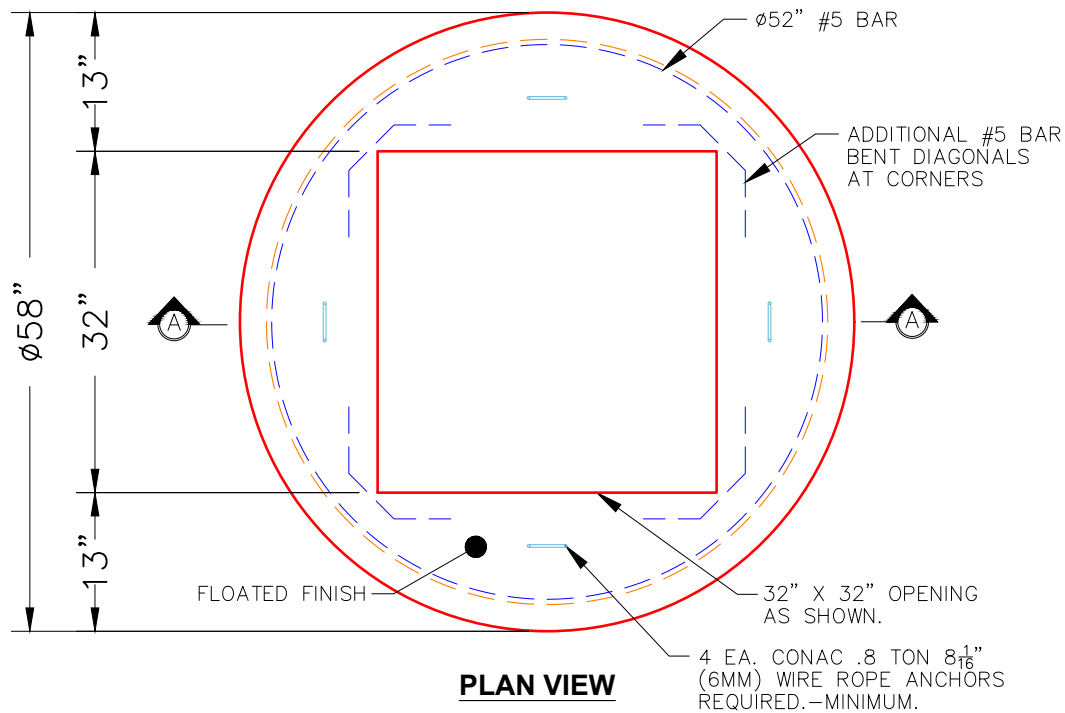

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

STANDARD SINGLE OFFSET GROOVE JOINT REQUIRED

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1629 lb
Volume (Net): 0.42cu.yd
