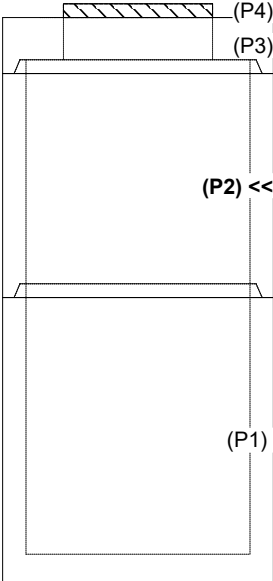

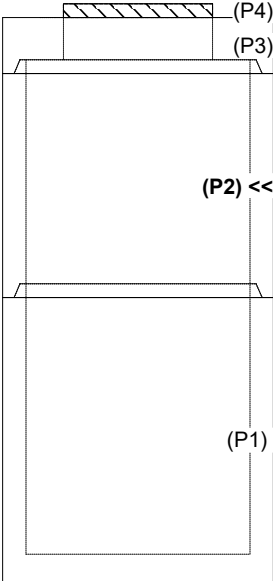
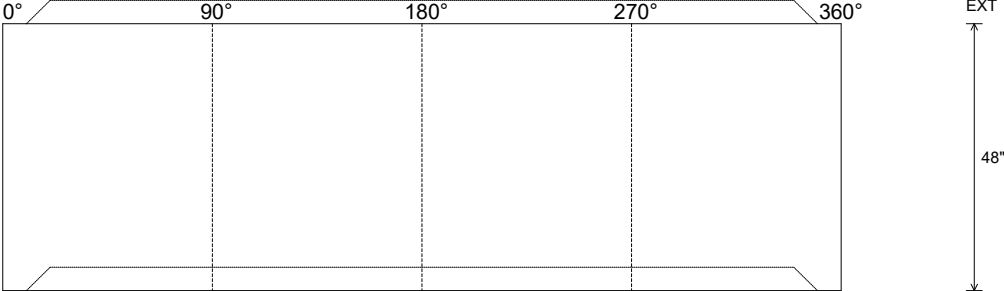


Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100 4/30/2026 1:22:31 PM		Tech: Jared - F PC: J. Jarvis				
Structure ID: S116											
P2		MH048RS48S		MH RISER T/G							
P4) 32" x 32" - CASTING HEIGHT - 3" P3) 48" - MH FLAT TOP w/32"x32" Hole F/G - 12" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE Custom Ht T/n - 55" 1) CASTING - HOE 595 F/G 2) 48" - Conseal CS-102 1.00" 1) 32" x 32" - Conseal CS-102 1.00" 2) Hole - 30					0 lb 1629 lb 3353 lb 4540 lb 376 lb 0 lb 0 lb 0 lb ----- Structure Total: 9899 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 455.25' Rim to Invert: 9.85' Slack: 0.2" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd	
