
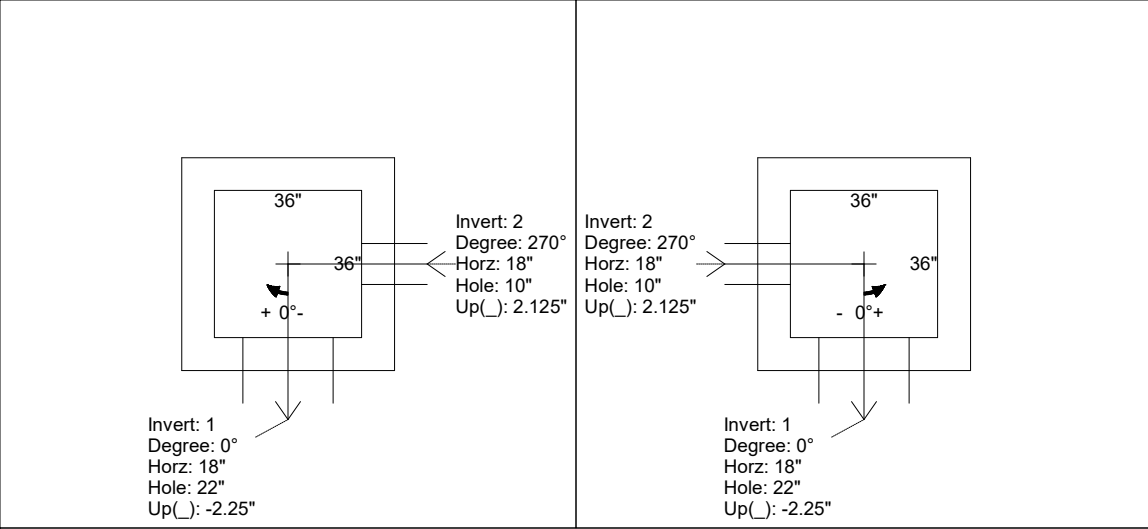
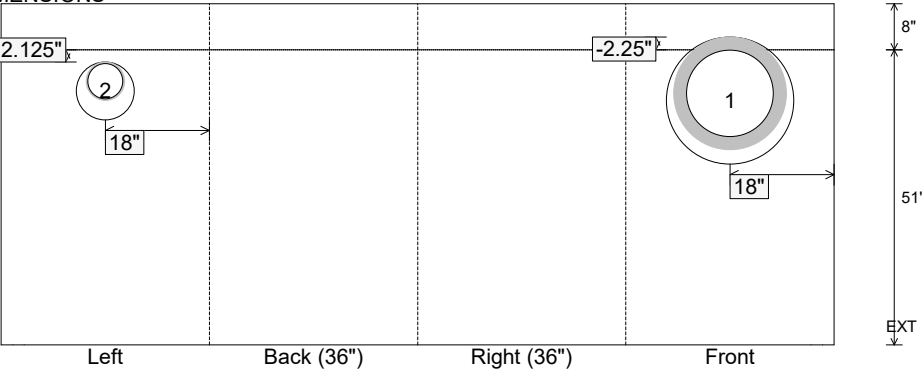


Job Name: 26-1185 - Wells Fargo Smyrna Job Location: Smyrna, TN 37167 Contractor: Hayes Pipe Supply					Plant: 100 7/21/2026 3:56:00 PM		Tech: Jared - F PC: E. Bradley					
Structure ID: A11-6 ST-OCS												
P1 BX3636-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n										
P2) 36" x 36" - CASTING HEIGHT - 0" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 51" 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 22" 1) Hole - 10"					0 lb 7533 lb 0 lb 0 lb 0 lb ----- Structure Total: 7533 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 588.5'					Rim to Invert: 4.25'		Slack: -0.002"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	584.25'	0°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"		
Invert 2	584.45'	270°	26"	6" PVC SCH40	6.625"	Hole 10	10"	10"	2.125"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)												
												
INSIDE WALL DIMENSIONS												
												
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 51" Height (Ext): 59"		Weight (Net): 7533 lb Volume (Net): 1.92cu.yd			
