

Job Name: 26-2480 - Jimmy Risinger Construction

Job Location: Louisville, KY 40219

Contractor: Bill Risinger Construction

Plant: Beaver Dam, KY

6/8/2026 11:34:50 AM

Tech: K. Cardwell

PC: J. Jarvis



Structure ID: Sump Pit

P1 BX3072-06BAVF

BOX BASE 6inW, 6inF, Variable Ht F/n

P1) 30" x 72" - BOX BASE 6inW, 6inF, Variable Ht F/n - 36"

1) SECONDARY POUR

1) 30" x 72" - Conseal CS-102 1.00"

1) No Openings

5909 lb

0 lb

0 lb

0 lb

Structure Total: 5909 lb

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS

2. CONCRETE: 4,500 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. NO STEPS

5. NO PIPE OPENINGS

6. NO CASTING

7. WET STICK 12" X 18" #5 L-BARS @ 12" C.C. (GRADE 60) OUT OF FLOOR FOR WALL POUR TIE-IN (SEE L-BAR DETAIL)

FIRST POUR (FLOOR): 1,776 LBS

SECOND POUR (WALLS): 4,133 LBS

Rim: 3'

Rim to Invert: 3'


Slack: 0"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1				No Openings						
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

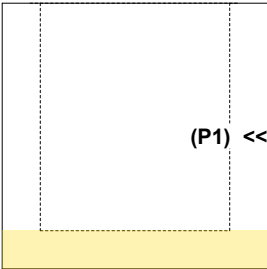

UPSIDE-DOWN VIEW (int. dimensions)

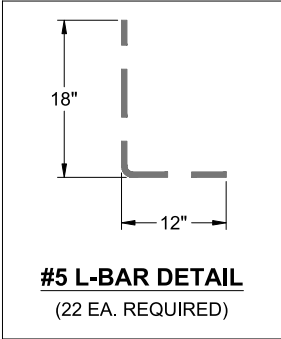

INSIDE WALL DIMENSIONS



Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 6"




Floor Height: 6"

Height (Int): 36"

Height (Ext): 42"

Weight (Net): 5909 lb

Volume (Net): 1.51cu.yd

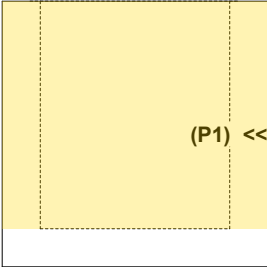Job Name: 26-2480 - Jimmy Risinger Construction Job Location: Louisville, KY 40219 Contractor: Bill Risinger Construction				Plant: Beaver Dam, KY 6/8/2026 11:34:50 AM		Tech: K. Cardwell PC: J. Jarvis					
Structure ID: Sump Pit											
P1 BX3072-06BAVF				BOX BASE 6inW, 6inF, Variable Ht F/n							
P1) 30" x 72" - BOX BASE 6inW, 6inF, Variable Ht F/n - 36" 1) SECONDARY POUR 1) 30" x 72" - Conseal CS-102 1.00" 1) No Openings				5909 lb 0 lb 0 lb 0 lb ----- Structure Total: 5909 lb		<u>Structure Notes:</u> 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STEPS 5. NO PIPE OPENINGS 6. NO CASTING 7. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN					
FIRST POUR (FLOOR): 1,776 LBS SECOND POUR (WALLS): 4,133 LBS											
Rim: 3' Rim to Invert: 3' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset	
Invert 1				No Openings							
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 36" Height (Ext): 42"		Weight (Net): 5909 lb Volume (Net): 1.51cu.yd	
