

Structure ID: 100 (6)

P4 MH048RS72CDARED




MH RISER w/ConBlock-CDA Red T/G

P6) 24" - CASTING HEIGHT - 7" P5) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P4) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P3) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P2) 60" - MH TRANS. SLAB ECC w/ConBlock-CDA Red T/G - 15" P1) 60" - MH BASE Custom Ht, w/ConBlock-CDA Red T/n - 67" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL EWSU w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 60" - Conseal CS-102 1.00" (Double) 3) 48" - Conseal CS-102 1.00" (Double) 1) Kor-N-Seal2 - S206-30 1) Kor-N-Seal2 - S206-22L	0 lb 1961 lb 5030 lb 5030 lb 2204 lb 9162 lb 0 lb 0 lb 2962 lb 258 lb 0 lb 0 lb 6 lb 6 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C "SANITARY"). 4. NO STEPS. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.
Structure Total:		26621 lb

Rim: 379.83' Rim to Invert: 21.69' Slack: 0.28" Sump: 3" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

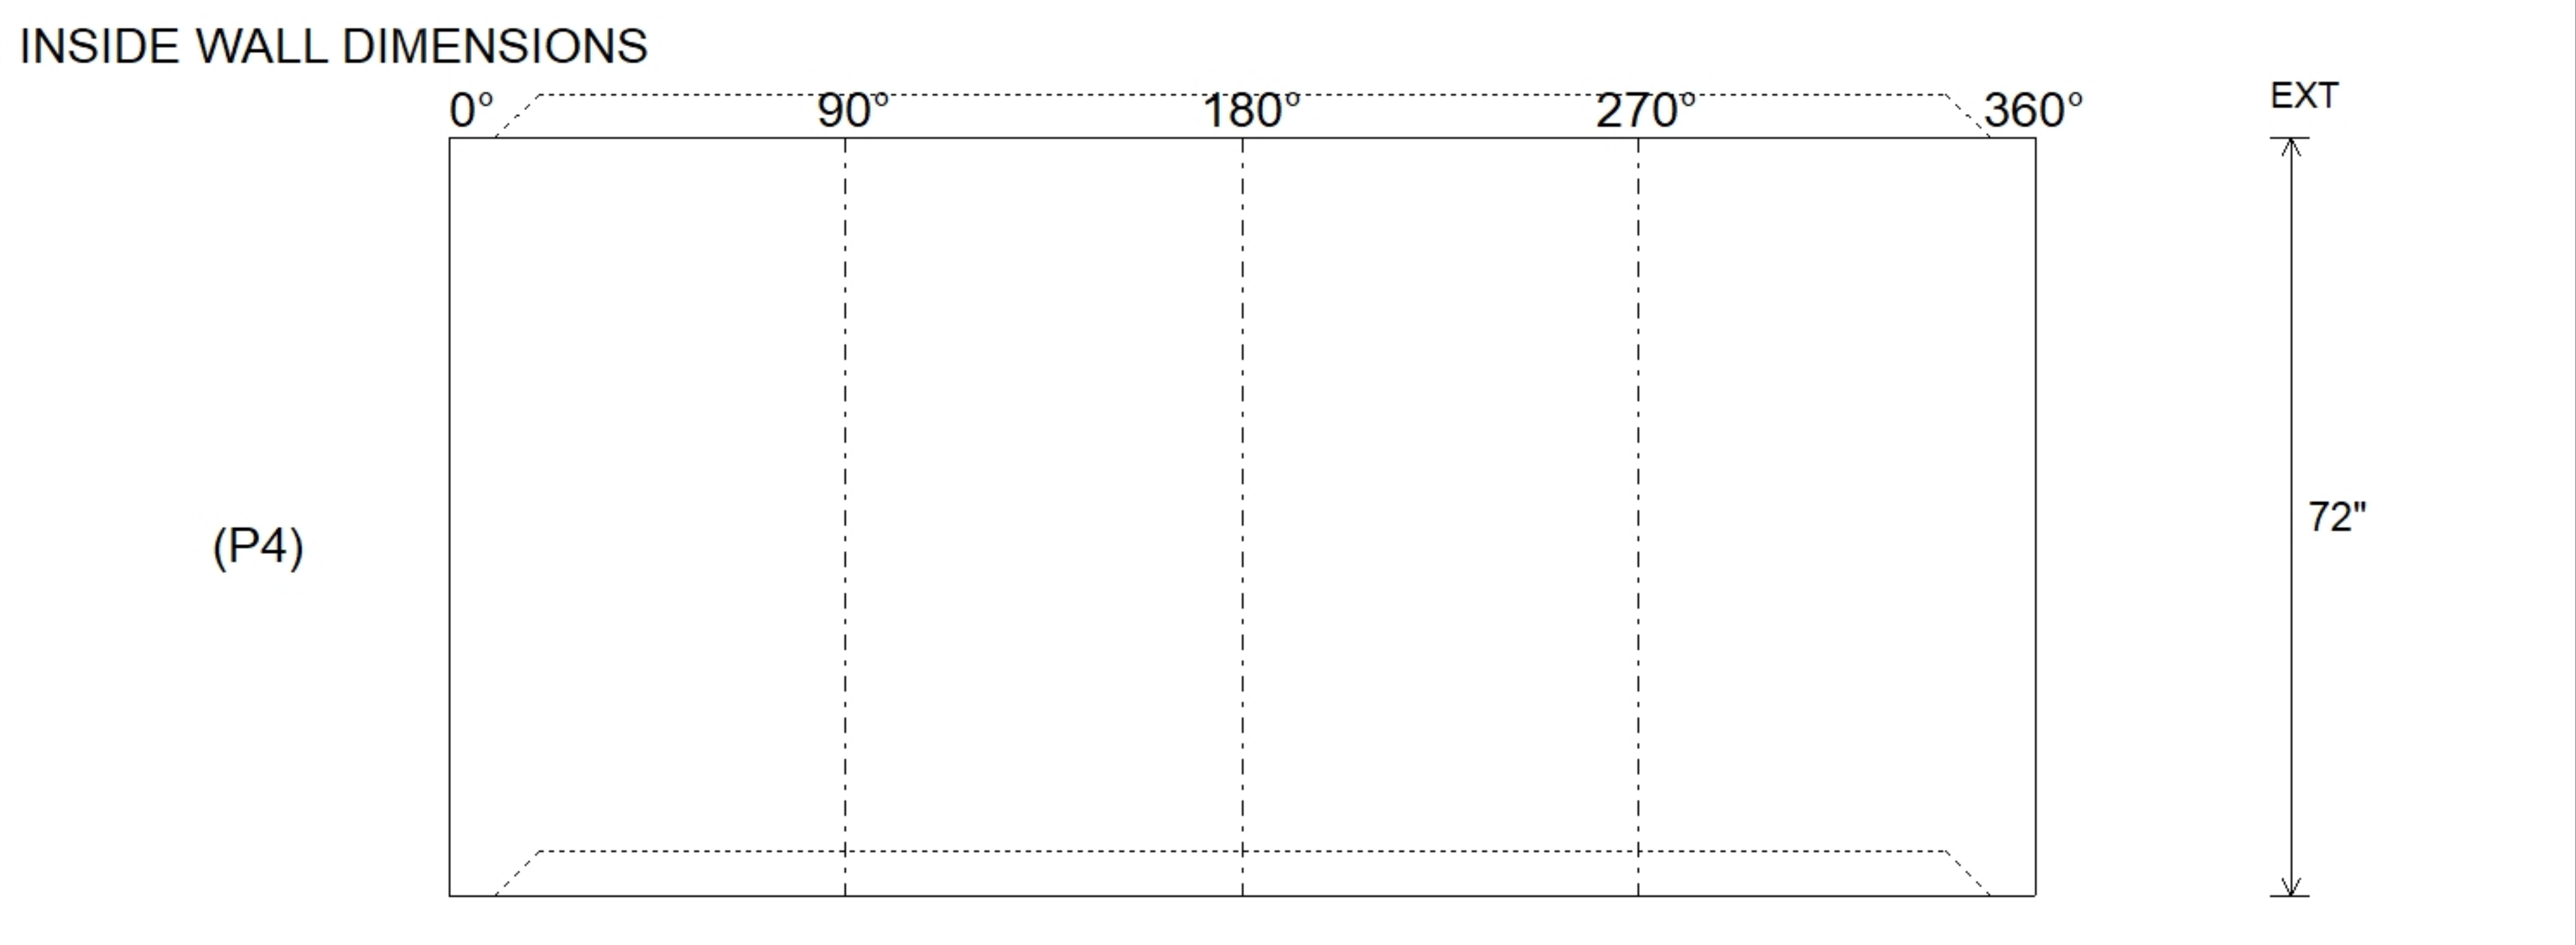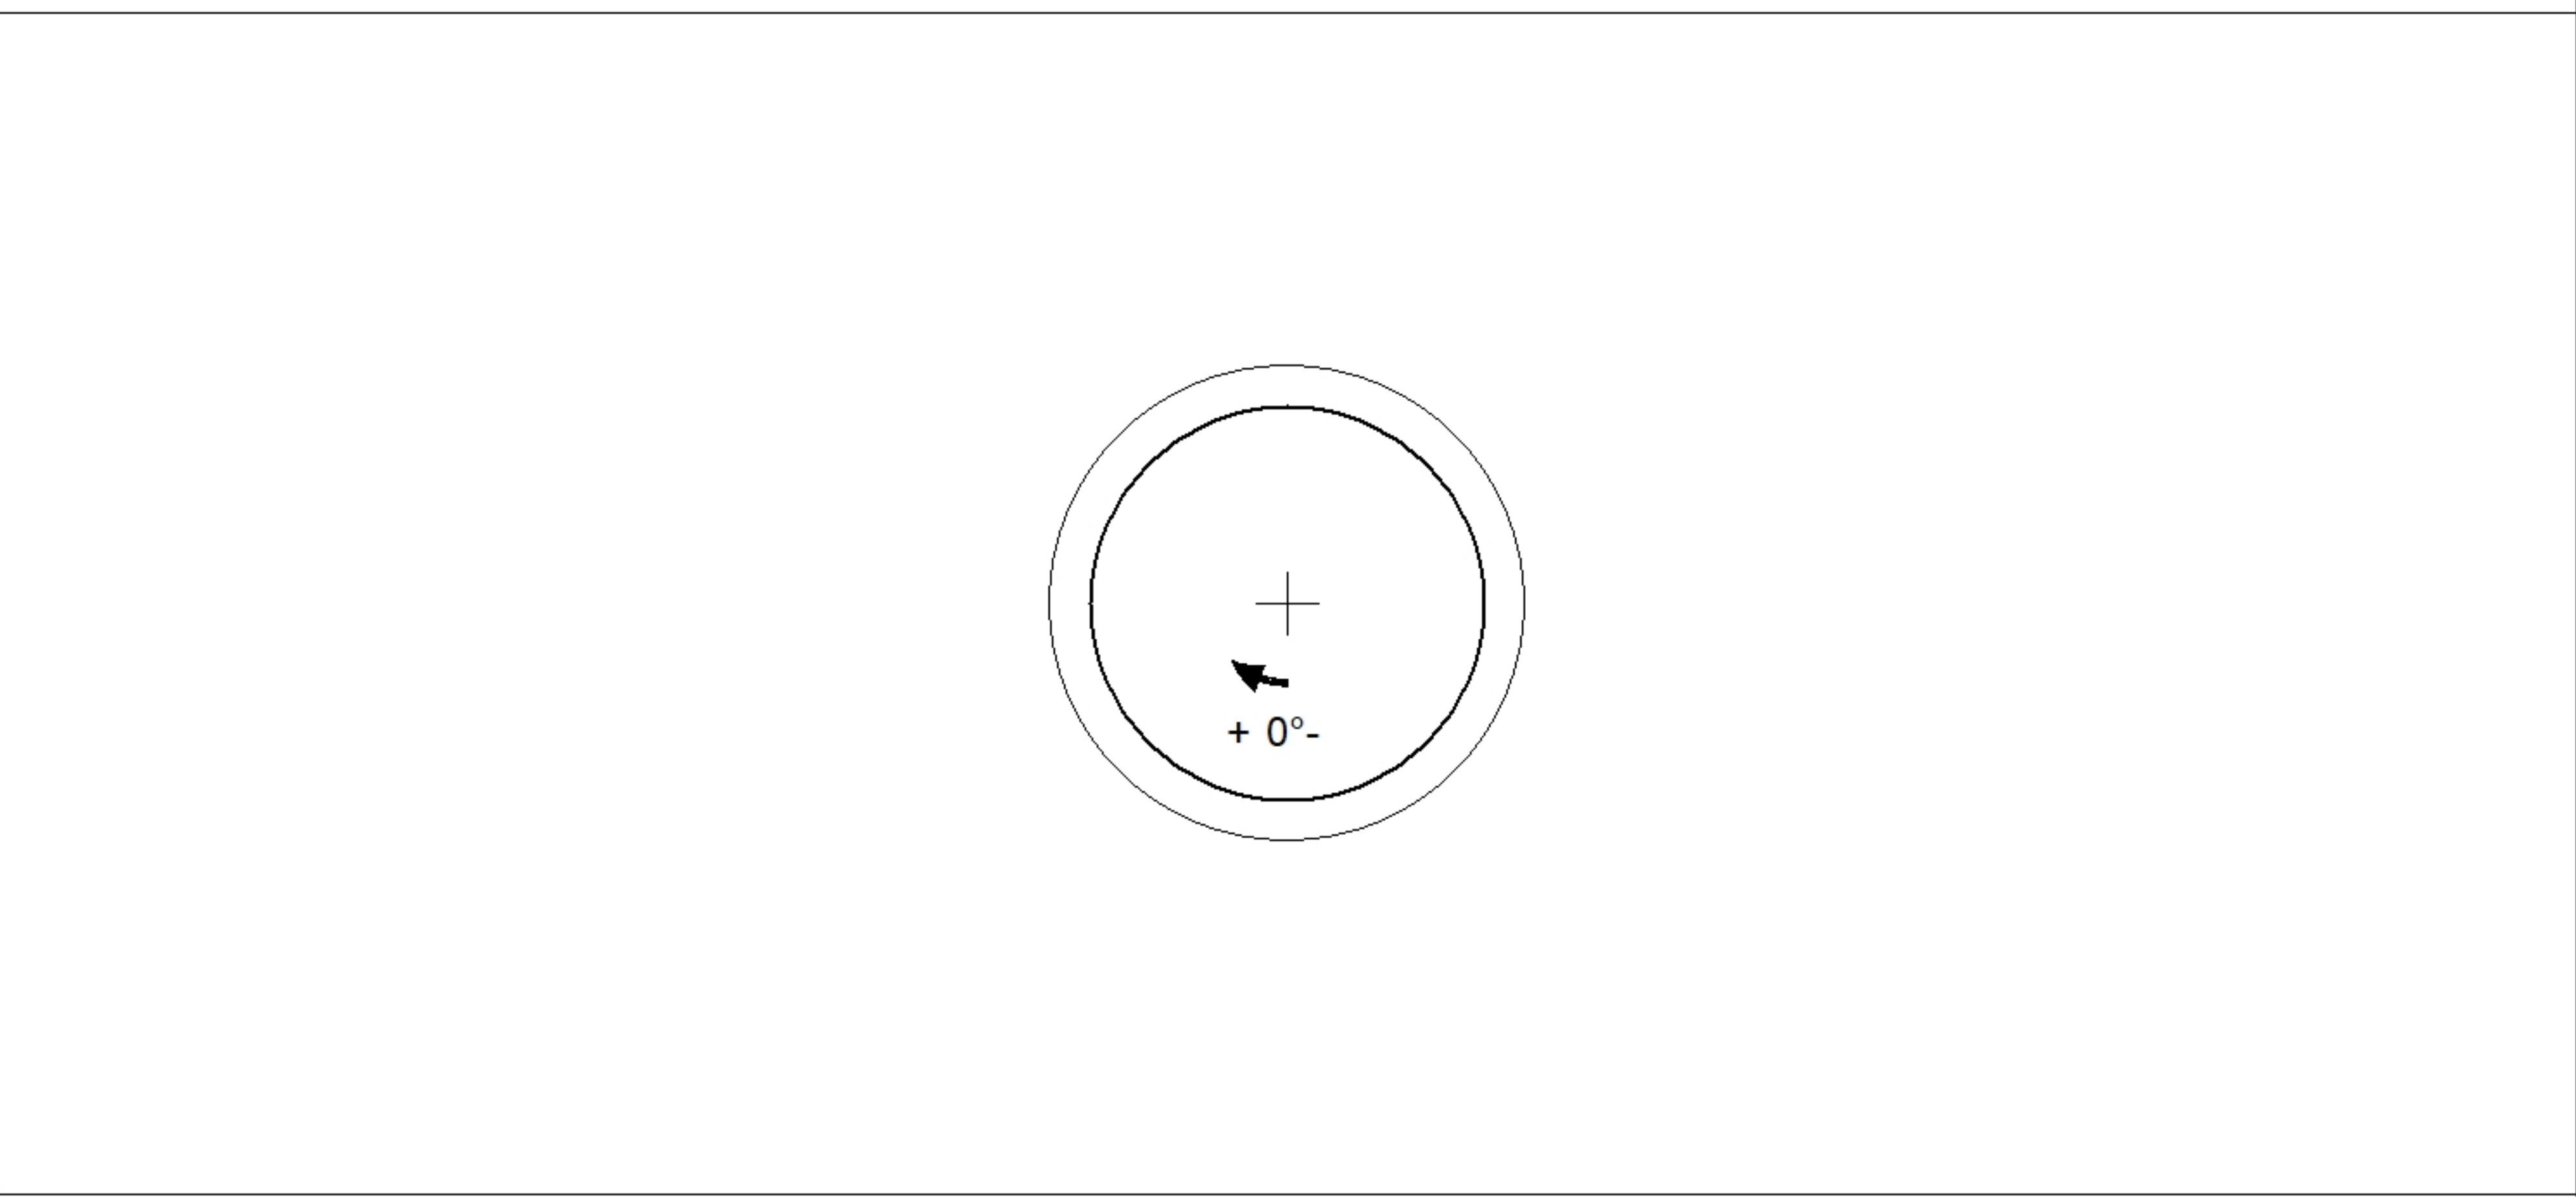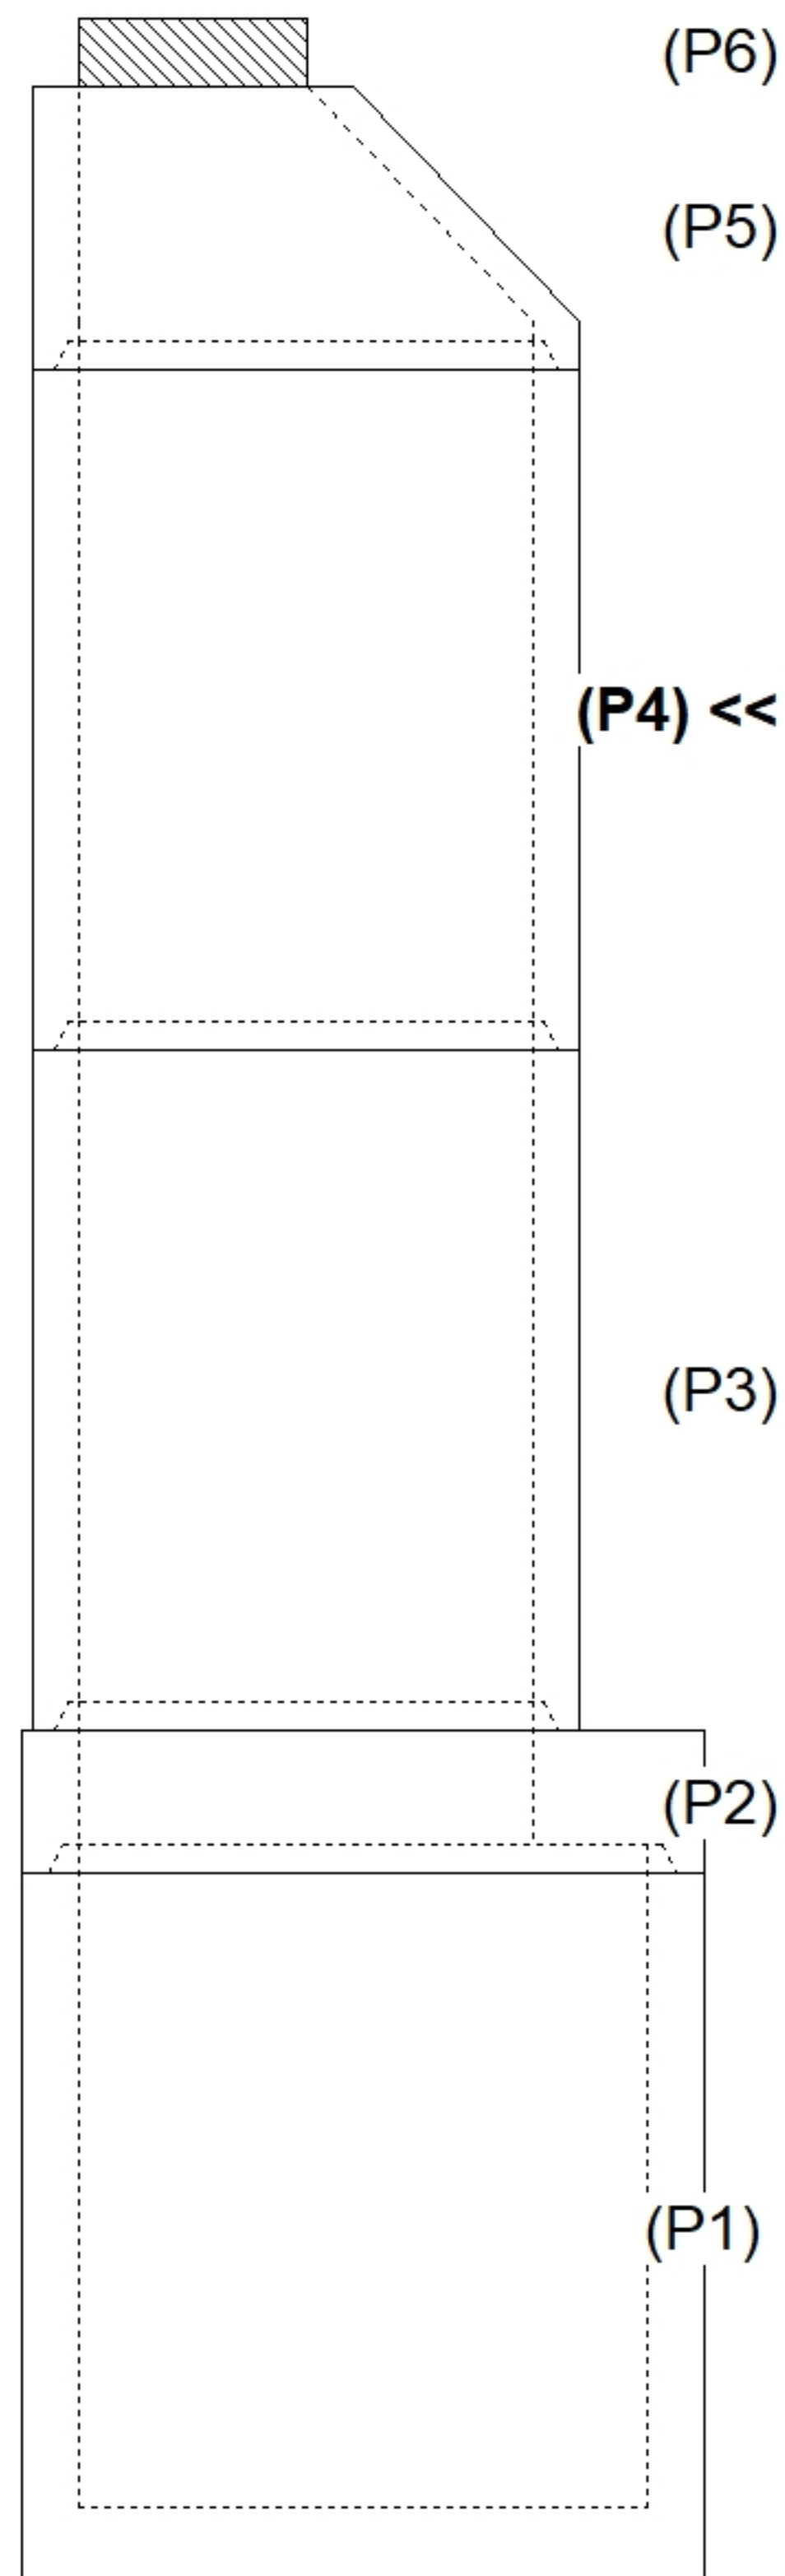

Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 72"
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 72"
		Weight (Net): 5030 lb Volume (Net): 1.28cu.yd	
