




Job Name: 25-4694 - 314 Old Nashville Hwy Job Location: La Vergne, TN Contractor: Hayes Pipe Supply					Plant: 100 7/10/2026 10:41:06 AM		Tech: Jared - A PC: E. Bradley				
Structure ID: 4 (5)											
P1		MH048BA30		MH BASE T/n							
P3) 24" - CASTING (cast in) - 4" P2) 48" - MH MONOTOP W/ MCS-288 CAST IN, Custom Ht F/G - 24" P1) 48" - MH BASE T/n - 30" 1) This Structure Includes a Cast-in Item - MCS-288 Frame (Supplied by Others) 1) 48" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 8 4) Weir n/n - 30"x6"						0 lb 2038 lb 3208 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5246 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STEPS 5. HOE MCS-288 FRAME & COVER "STORM" SUPPLIED BY OTHERS - FRAME TO BE CAST INTO TOP OF MONOTOP FLANGE SIDE UP			
Rim: 613.5'		Rim to Invert: 4.5'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	609'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.625"	0"	
Invert 2	609'	165°	83.5"	6" HDPE (perf pipe)	6.9"	Hole 8	8"	8.038"	-0.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

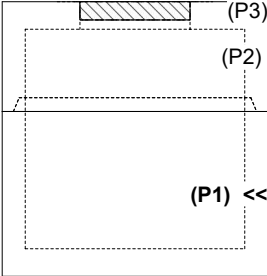


RIGHT-SIDE UP VIEW (int. dimensions)

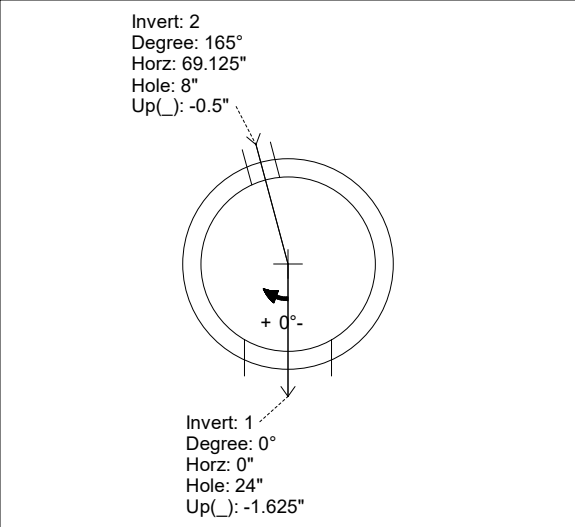

UPSIDE-DOWN VIEW (int. dimensions)

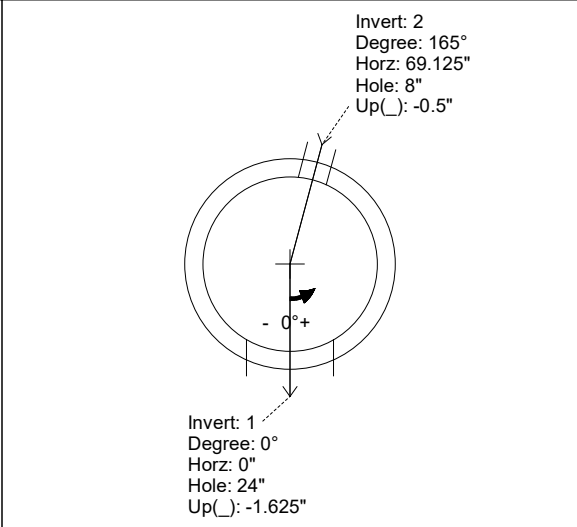

INSIDE WALL DIMENSIONS

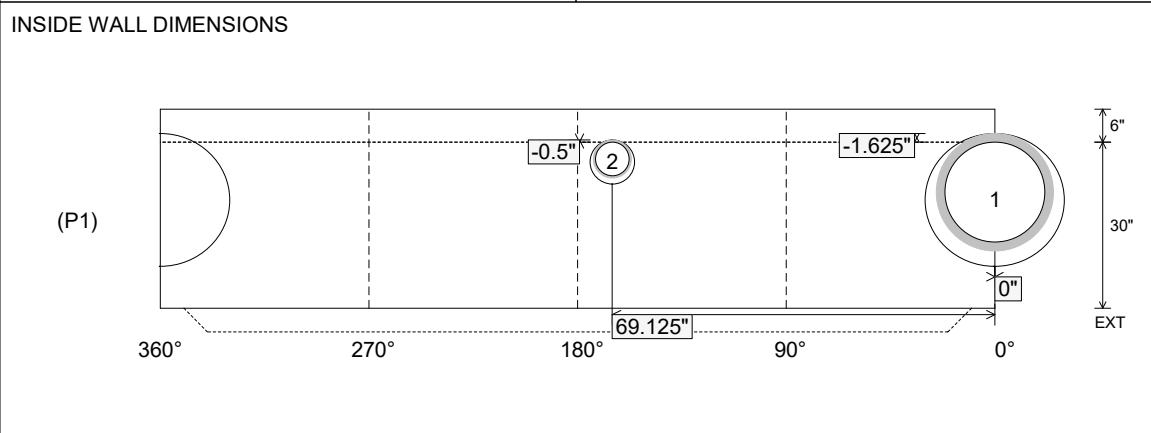

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3208 lb Volume (Net): 0.82cu.yd
----------------------------------	---------------------------------	--	--	--
