

Job Name: 25-2471 - Texas Roadhouse
Job Location: Danville, KY
Contractor: McCain Bros Excavating LLC

Plant: 100

6/11/2026 11:35:52 AM

Tech: Jared - F
PC: M. Sullivan



Structure ID: 6

P2 MH048LD06SP

MH FLAT TOP w/18"x36" Hole F/F

P3) 18" x 36" - CASTING HEIGHT - 5.5"
P2) 48" - MH FLAT TOP w/18"x36" Hole F/F - 6"
P1) 48" - MH BASE Custom Ht F/n - 19"
1) 48" - Conseal CS-102 1.00"
1) 18" x 36" - Conseal CS-102 1.00"
1) DOGHOUSE INVRTD - 24"x20"
1) Hole - 16

Structure Total:



0 lb
1004 lb
2379 lb
0 lb
0 lb
0 lb
0 lb

3383 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS (HOE 580-A F/G).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

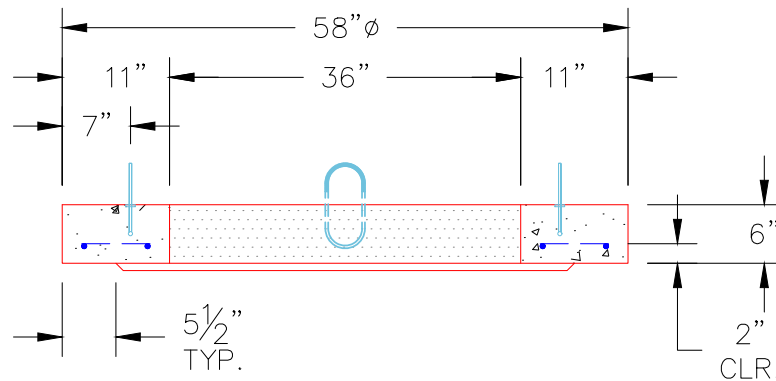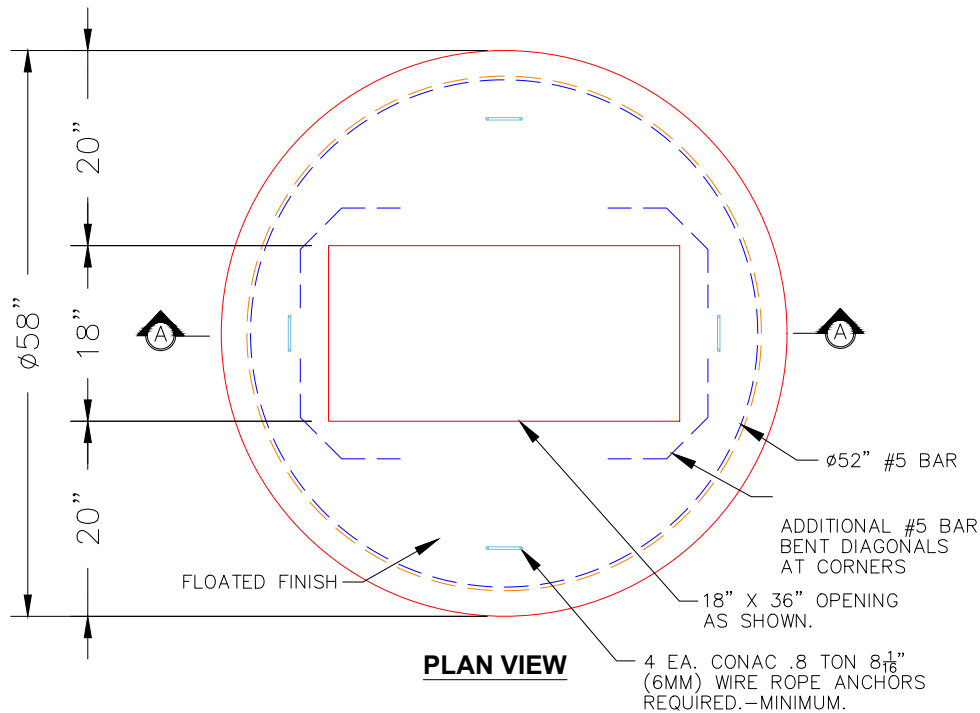

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 6"

Weight (Net): 1004 lb
Volume (Net): 0.26cu.yd
