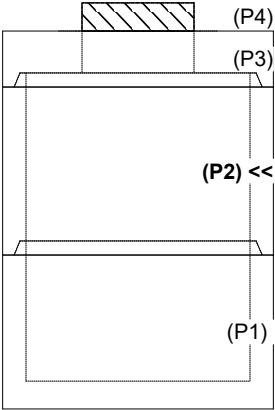




Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A				
Job Location: Elizabethtown, KY 40165					7/30/2026 10:20:31 AM		PC: Celina Goff				
Contractor: Kauffeld Brothers Construction											
Structure ID: CB 5-63 (95)											
P2 MH048RS36S					MH RISER SPECIAL						
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 36" P1) 48" - MH BASE Custom Ht - 27" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 1935 lb 2515 lb 3107 lb 362 lb 0 lb 0 lb 0 lb ----- 7920 lb		Structure Notes: . 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 862.87' Rim to Invert: 6.68' Slack: 0.41' Sump: 1.25' Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd		
