




Job Name: 23-2309 - Richland Estates Subdivision Job Location: Portland, TN Contractor: Core & Main LP (BG)					Plant: 100 6/30/2026 8:52:24 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 03 SS-MH											
P1 MH048BA24X		MH BASE w/XYPEX									
P4) 24" - CASTING HEIGHT - 6" P3) 24" - XYPEX GRADE RING - 3" P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 1981 lb 2911 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 6551 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = XYPEX C-500 NF RED 4. CASTING BY OTHERS (JBS 1155 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 805.87' Rim to Invert: 5.14' Slack: 0.68" Sump: 2" Step Position: 108.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	800.73'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	800.93'	217°	109.834"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.4"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

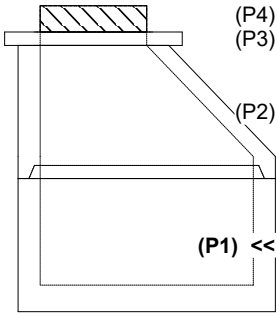


RIGHT-SIDE UP VIEW (int. dimensions)

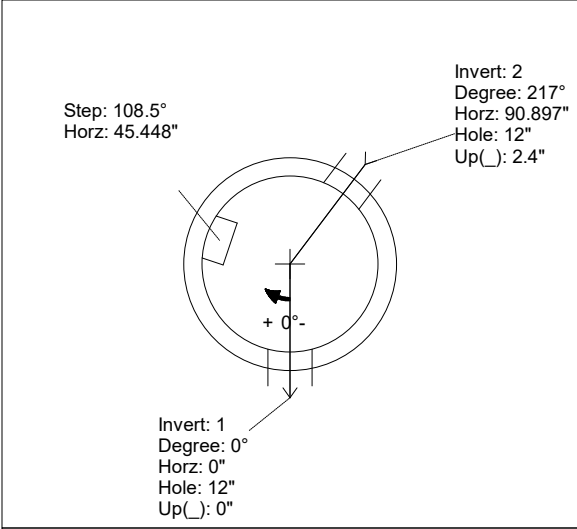

UPSIDE-DOWN VIEW (int. dimensions)

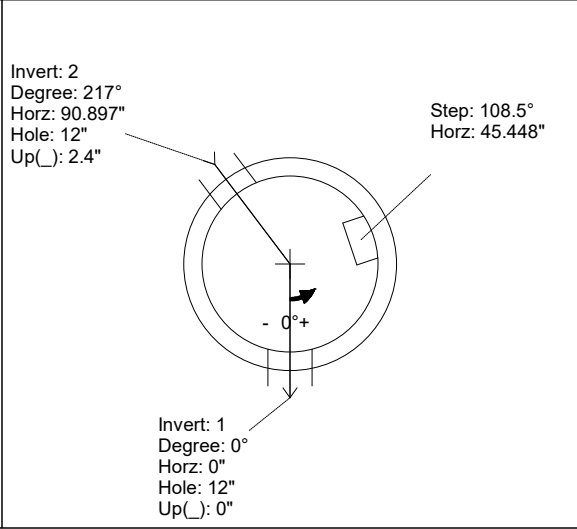

INSIDE WALL DIMENSIONS

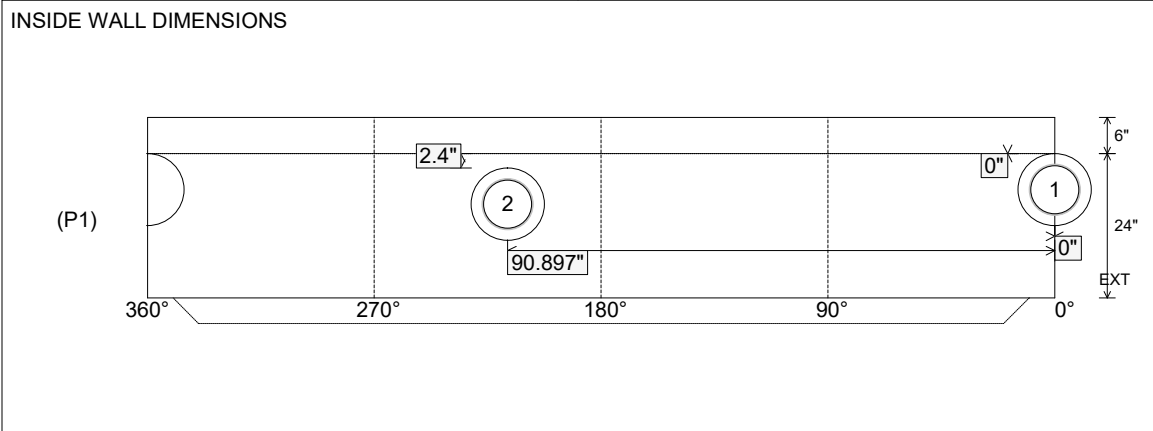

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 23-2309 - Richland Estates Subdivision Job Location: Portland, TN Contractor: Core & Main LP (BG)					Plant: 100 6/30/2026 8:52:24 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: 03 SS-MH											
P1 MH048BA24X		MH BASE w/XYPEX									
P4) 24" - CASTING HEIGHT - 6" P3) 24" - XYPEX GRADE RING - 3" P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 1981 lb 2911 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- 6551 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = XYPEX C-500 NF RED 4. CASTING BY OTHERS (JBS 1155 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 805.87' Rim to Invert: 5.14' Slack: 0.68" Sump: 2" Step Position: 108.5°					INVERT CHANNEL DRAWING FULL HEIGHT INVERT						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	800.73'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2	800.93'	217°	109.834"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	2.4"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2911 lb Volume (Net): 0.74cu.yd
----------------------------------	---------------------------------	--	--	--
