

Job Name: 26-1333 - Mitchell Hill Road Project

Job Location: Louisville, KY 40118

Contractor: Hall Contracting of Kentucky Inc

Plant: 100

6/16/2026 1:23:17 PM

Tech: J. Horsley

PC: J. Jarvis



Structure ID: WALL P1-P2

P3 CUSTOM WALL

WALL PANEL 6" THICK F/F

P3) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG

P2) 77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG

P1) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG

1) Hole - 2

1398 lb

932 lb

1398 lb

0 lb

Structure Total: 3727 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28" DAYS.

3. SMOOTH FORM FINISH ON THE FRONT SURFACE.

4. 3/4" CHAMFER ON ALL LONG EDGES.

REINFORCING PER ASTM A615 (GRADE 60).

-VERTICAL BARS = #4 BARS AT 12" C/C

-HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)

Rim: 702'


Rim to Invert: 2'

Slack: 0"

Sump: 72"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	700'	0°	38.5"	2" WEEP HOLE	2"	Hole 2	2"	2"	12"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

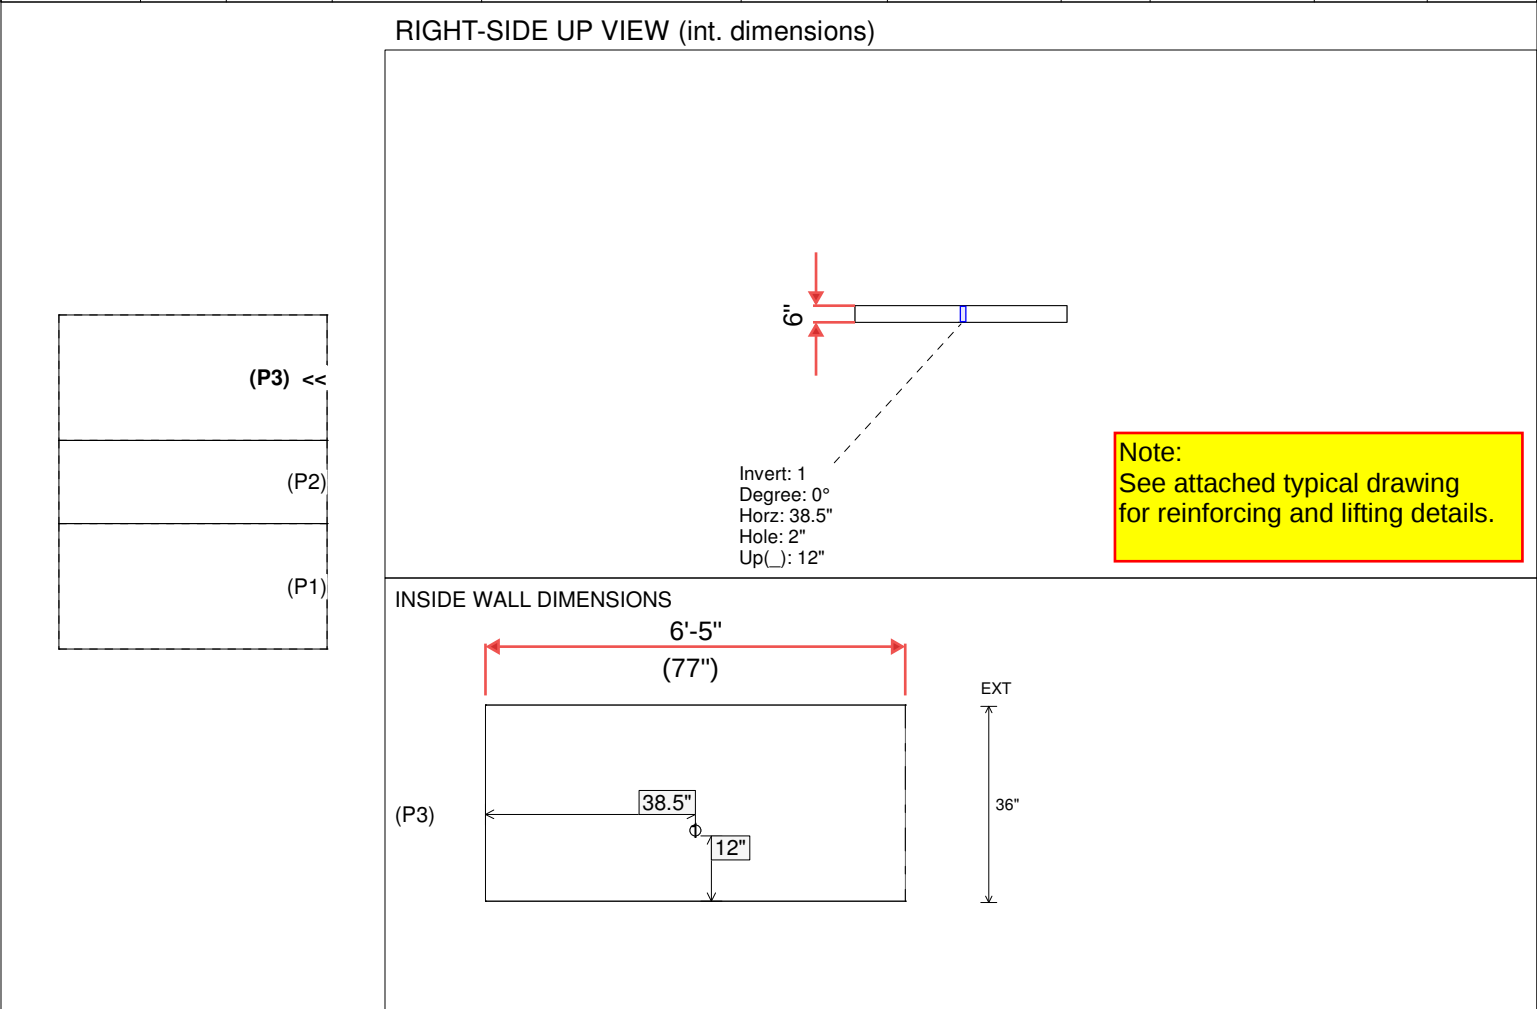

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: Flat

Wall Thickness: 0"




Floor Height: 0"

Height (Int): 36"

Height (Ext): 36"

Weight (Net): 1398 lb

Volume (Net): 0.36cu.yd

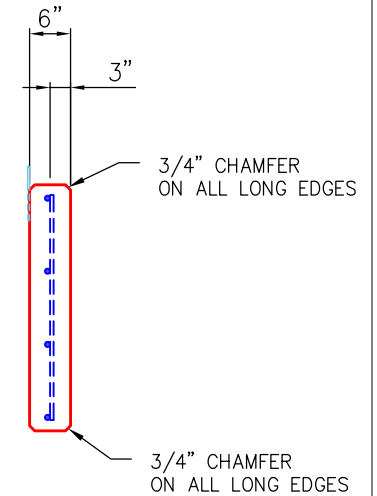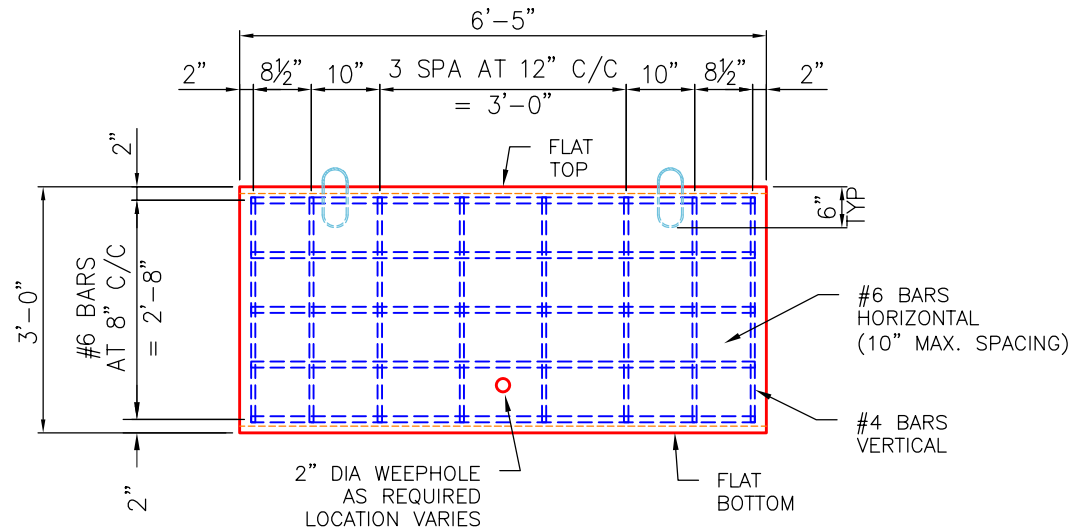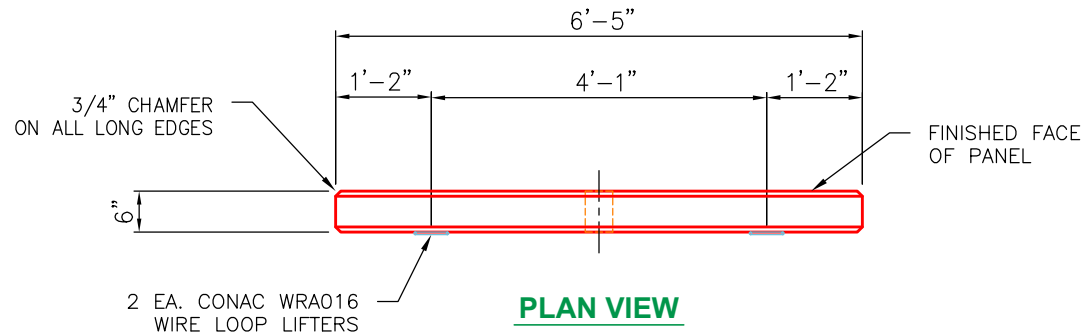

GENERAL NOTES:

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 1,413 LBS
6. 68 REQUIRED.

SIDE VIEW

END VIEW

REVISION INFORMATION				SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.	
REV. 	DATE:	NO REVISIONS TO DATE		CUSTOMER: HALL CONTRACTING OF KY INC.	
				PROJECT: MITCHELL HILL ROAD PROJECT	
				STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 36" HT)	
				SALES ORDER NO: 26-1333	
				CHECK: B. SMITH	DRAWN BY: J. HORSLEY
				DATE: 04/20/26	SCALE: NTS PG. 1 of 1
