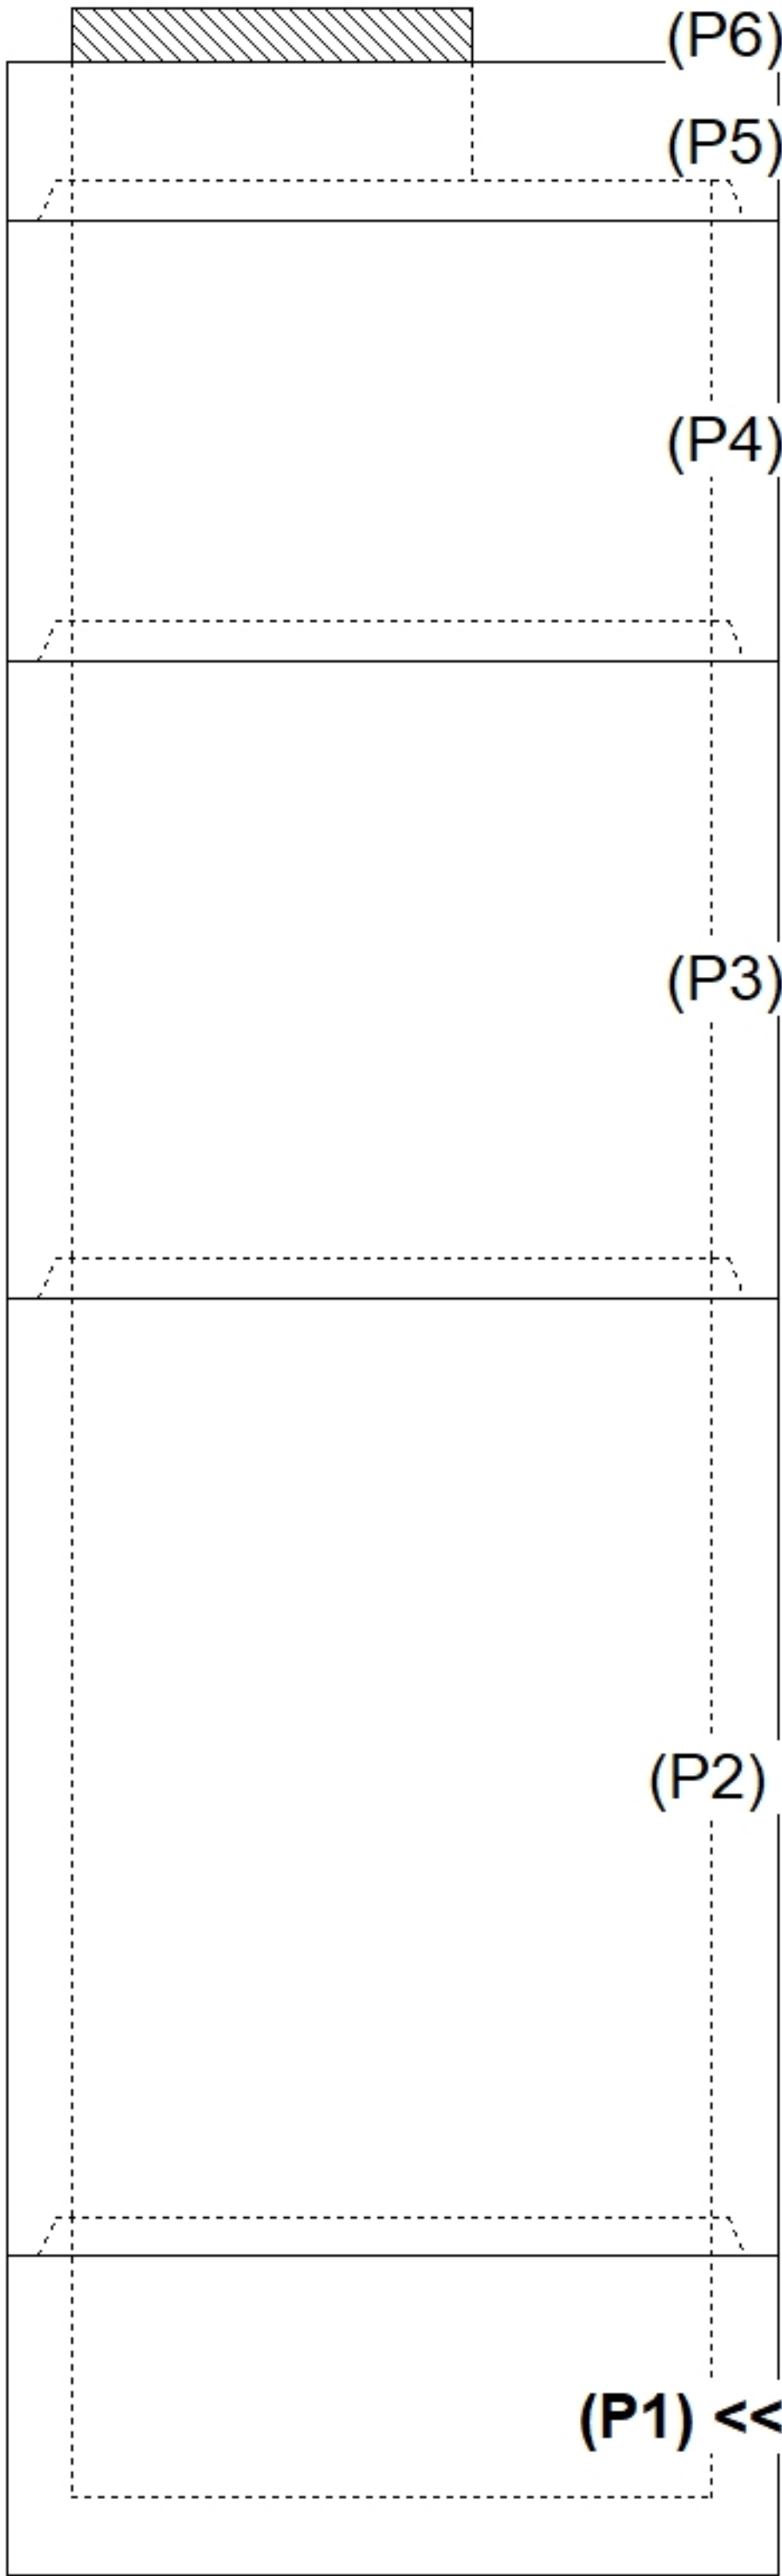
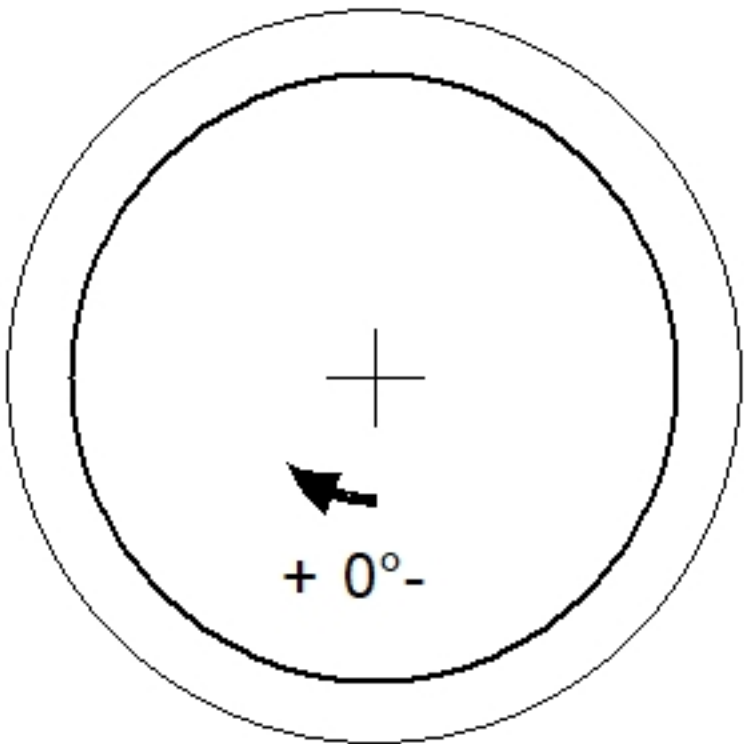
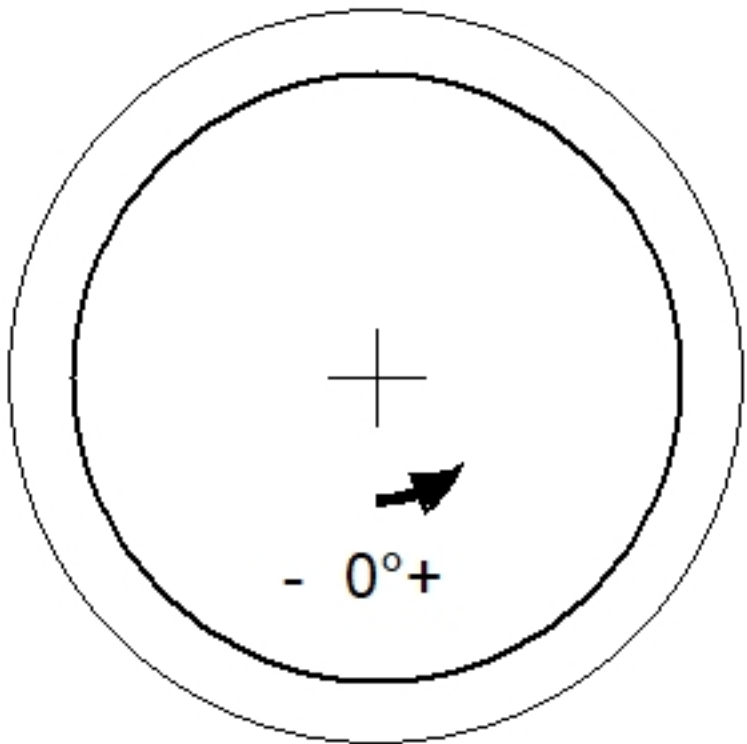
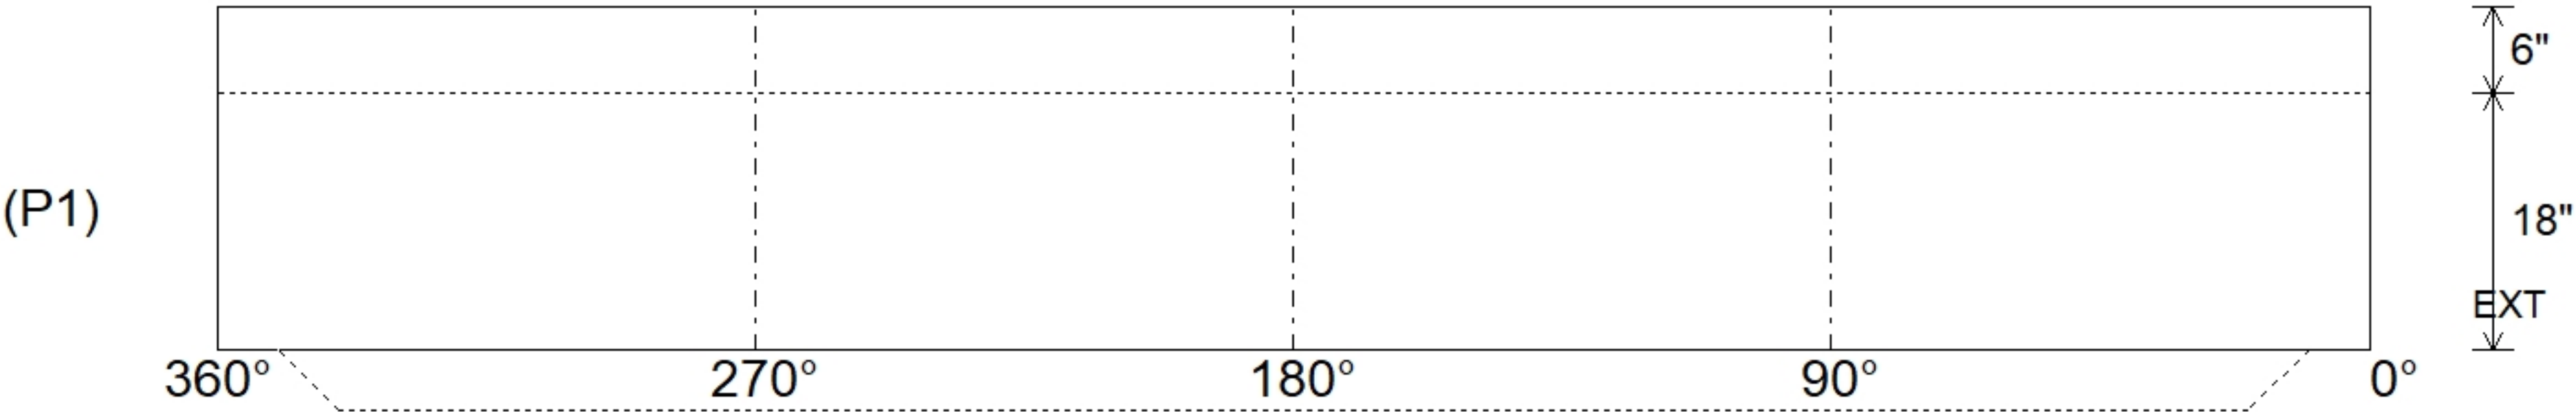


Job Name: 26-2801 900640 QuikTrip No. 0680 Job Location: CPU Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/25/2026 11:00:28 AM		Tech: S. Felletter PC: C. Goff						
Structure ID: 15-CS-4													
P1		MH048BA18			MH BASE T/n								
P6) 30" - CASTING HEIGHT - 4" P5) 48" - MH FLAT LID w/30in ECC Hole F/G - 12" P4) 48" - MH RISER Custom Ht T/G - 33" P3) 48" - MH RISER T/G - 48" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 4) 48" - Conseal CS-102 1.00" 2) PSX - 12-08 NYLO						0 lb 1413 lb 2305 lb 3353 lb 4934 lb 2588 lb 0 lb 0 lb 0 lb 16 lb ----- 14610 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 610.55' Rim to Invert: 12' Slack: 8" Sump: 51" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
						RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 							
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 2588 lb Volume (Net): 0.66cu.yd			
