



Job Name: 26-2801 900640 QuikTrip No. 0680 Job Location: CPU Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/25/2026 11:01:07 AM		Tech: S. Felletter PC: C. Goff						
Structure ID: 15-CS-4													
P2		MH048RS72S		MH RISER SPECIAL T/G									
P6) 30" - CASTING HEIGHT - 4" P5) 48" - MH FLAT LID w/30in ECC Hole F/G - 12" P4) 48" - MH RISER Custom Ht T/G - 33" P3) 48" - MH RISER T/G - 48" P2) 48" - MH RISER SPECIAL T/G - 72" P1) 48" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 4) 48" - Conseal CS-102 1.00" 2) PSX - 12-08 NYLO						0 lb 1413 lb 2305 lb 3353 lb 4934 lb 2588 lb 0 lb 0 lb 0 lb 16 lb ----- 14610 lb		Structure Notes: 4" CASTING BY OTHERS LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE ICAST TO INSTALL THE INTERNALS CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 610.55' Rim to Invert: 12' Slack: 8" Sump: 51" Step Position:													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	598.55'	270°	136.659"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	26.75"	0"			
Invert 2	598.55'	339°	171.583"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	26.75"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

RIGHT-SIDE UP VIEW (int. dimensions)

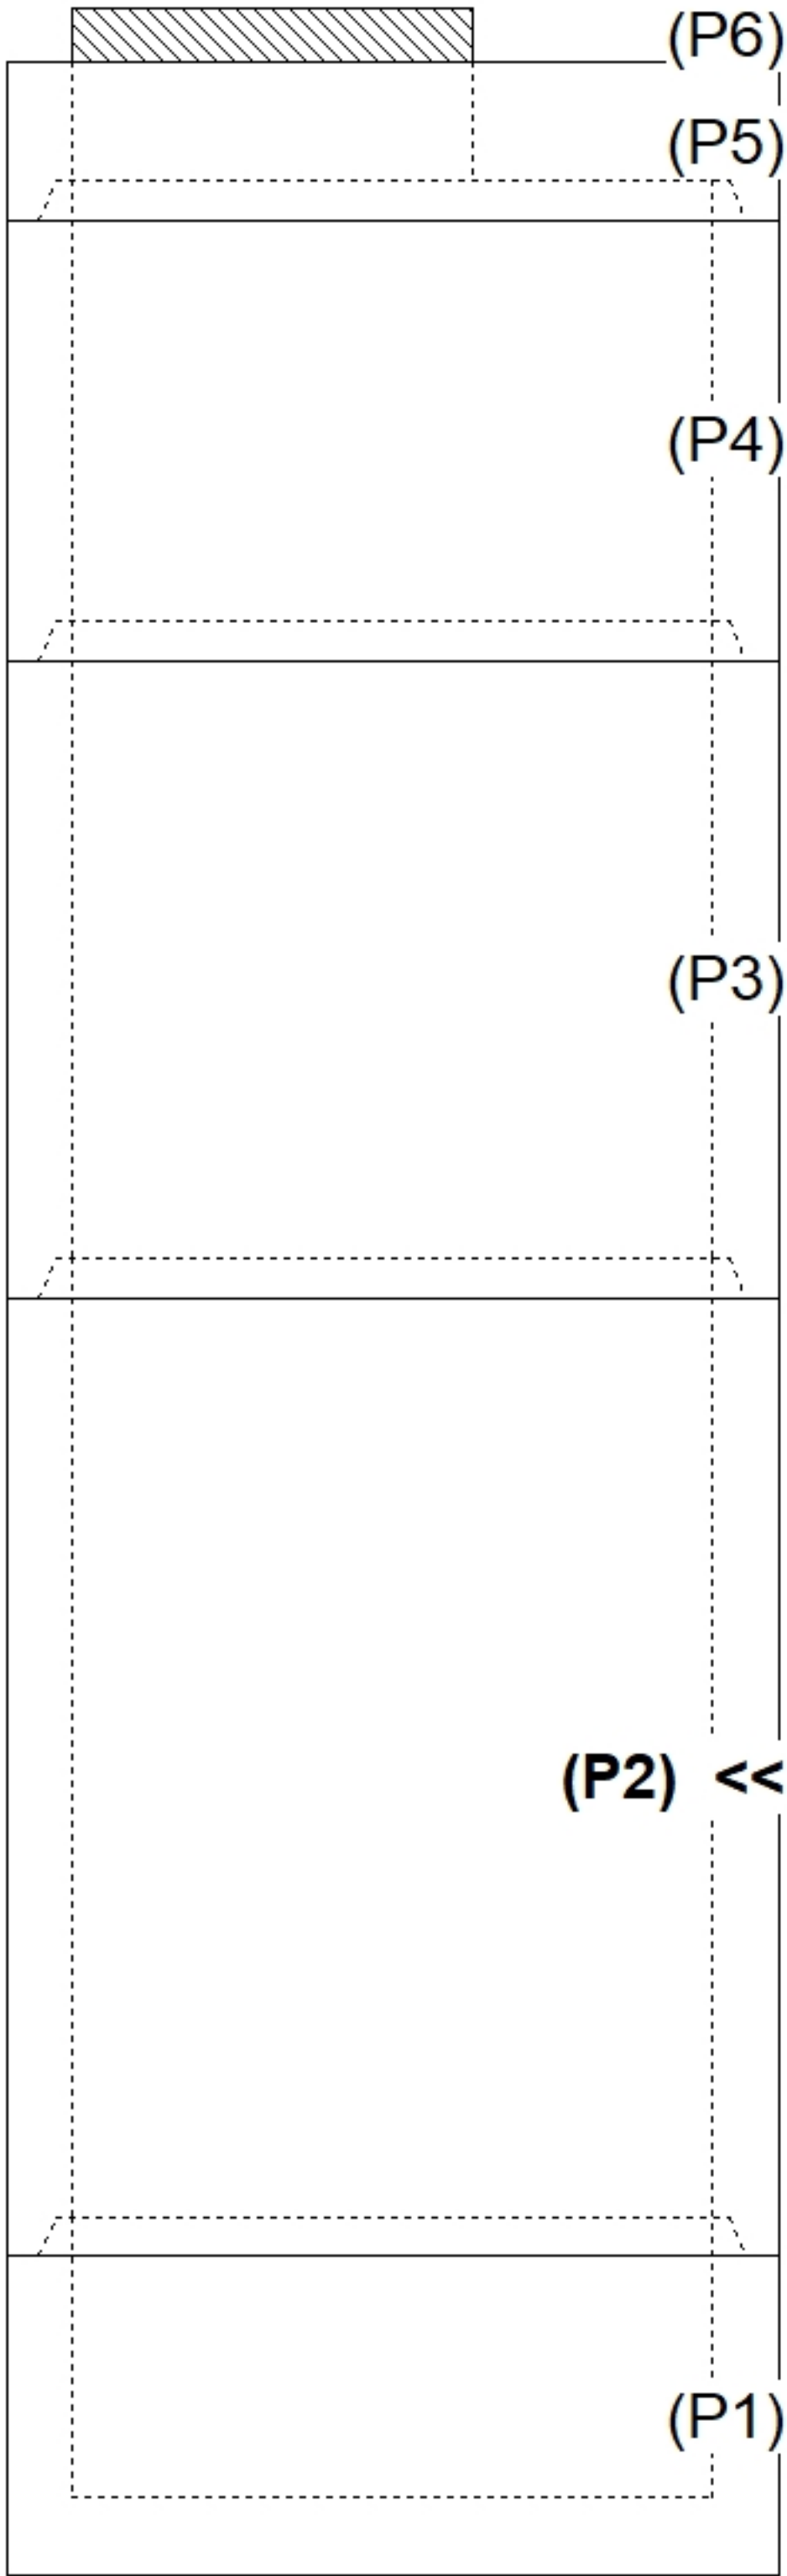


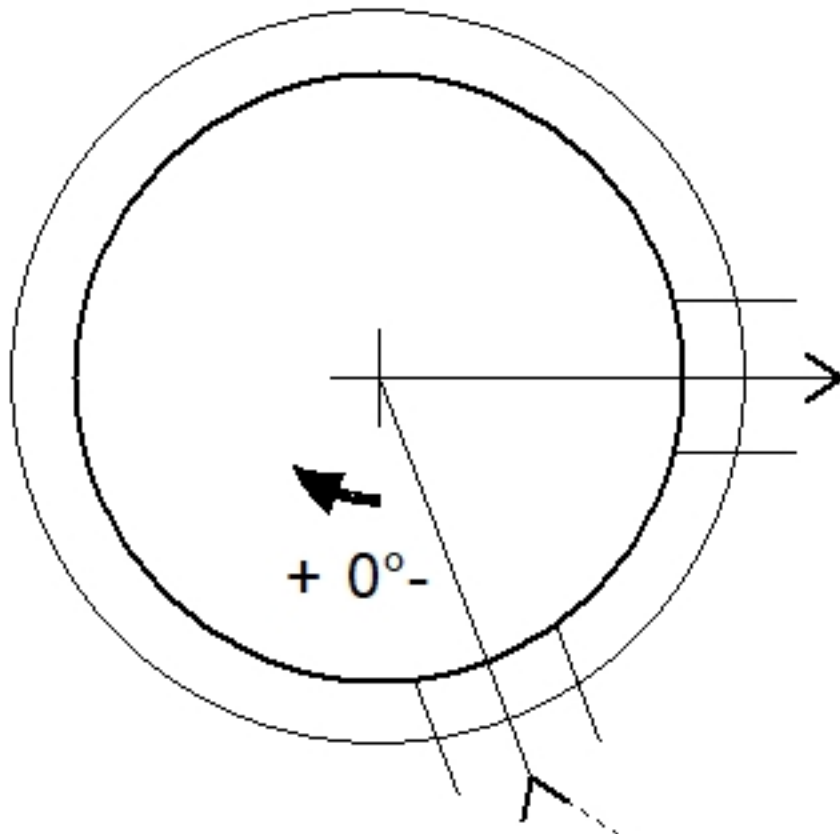

Invert: 1
Degree: 270°
Horz: 113.097"
Hole: 12"
Up(): 26.75"

Invert: 2
Degree: 339°
Horz: 142"
Hole: 12"
Up(): 26.75"

INSIDE WALL DIMENSIONS

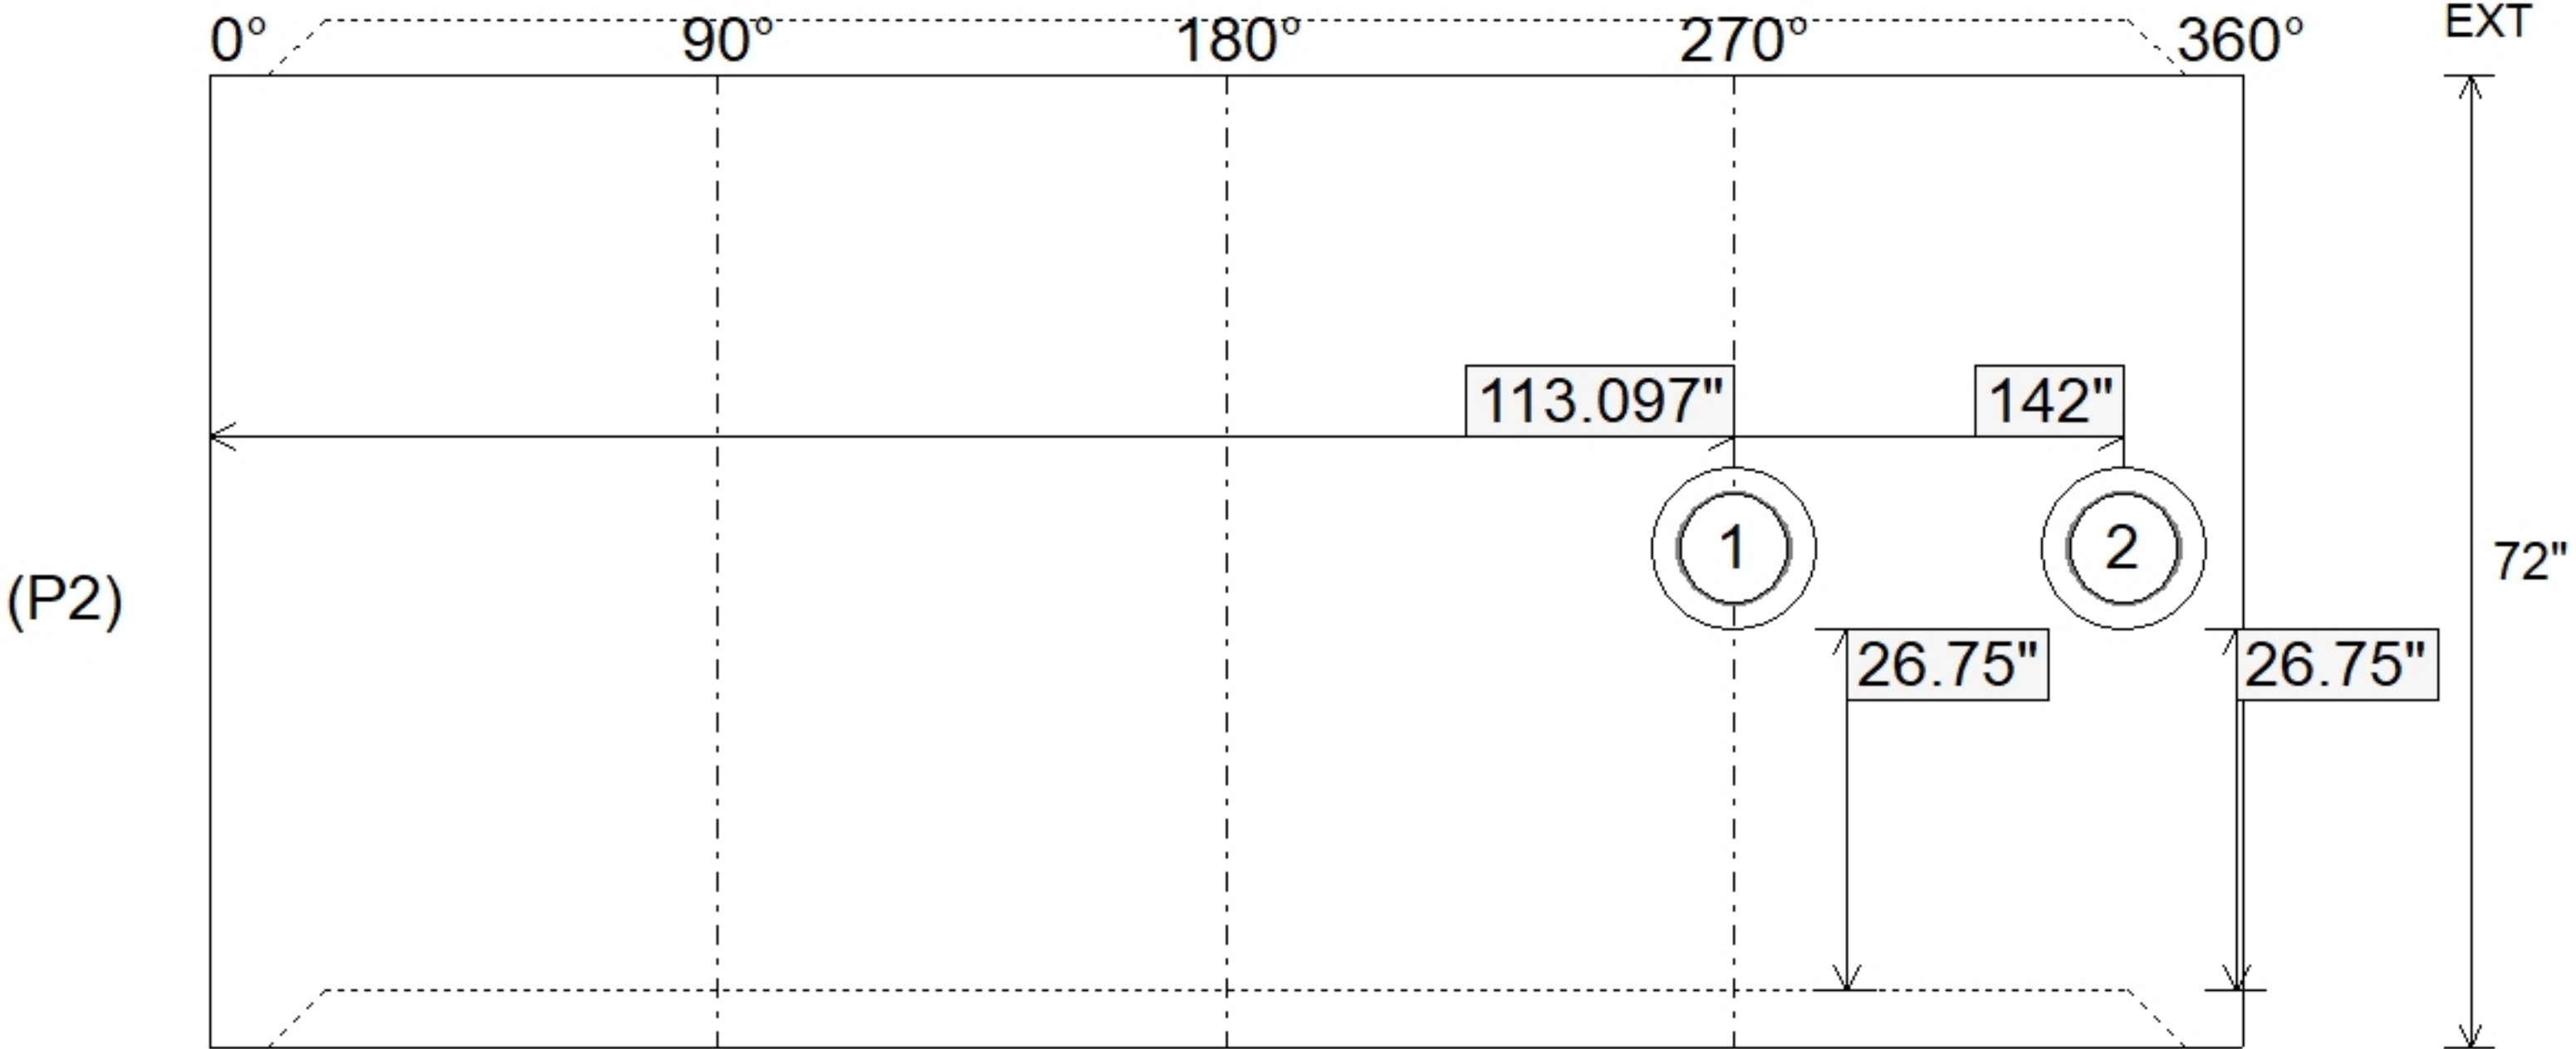

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 4934 lb Volume (Net): 1.26cu.yd
----------------------------------	------------------------------------	--	--	--
