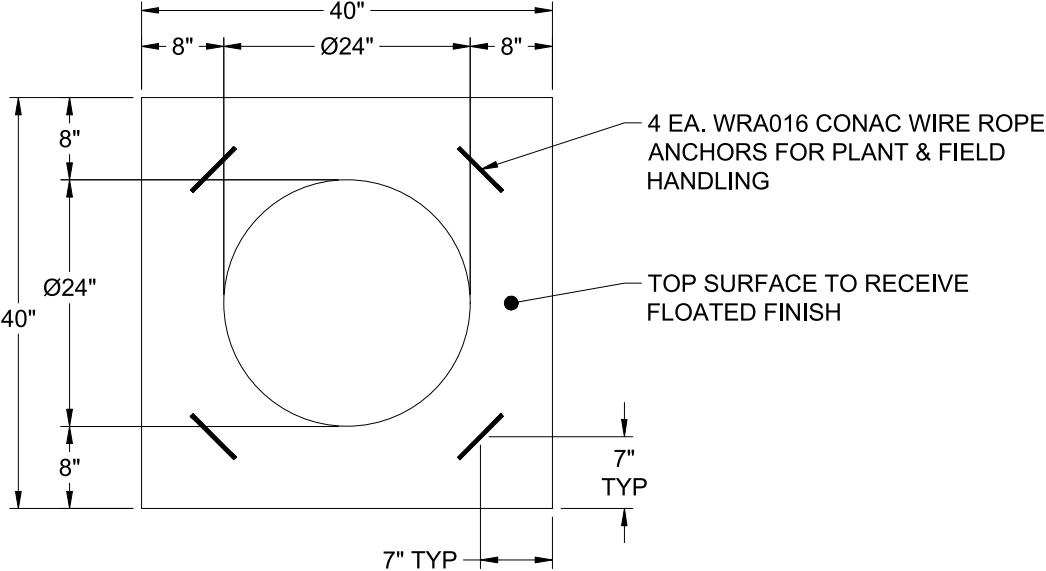
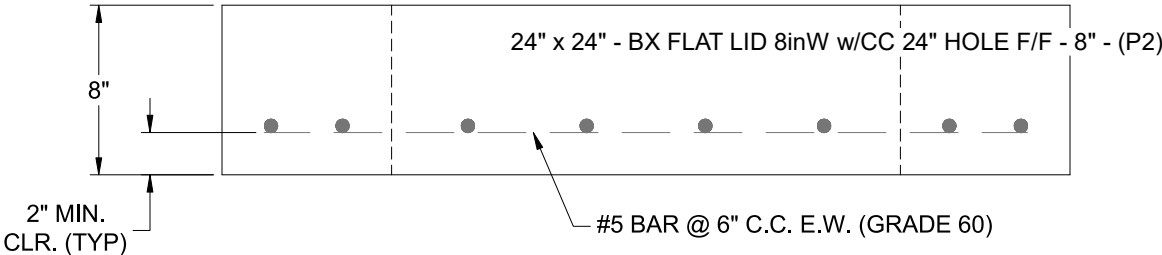


Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction		Plant: 100 6/12/2026 3:12:25 PM	Tech: J. Horsley - A PC: J. Jarvis	
Structure ID: 58				
P2 BXLD2424FL-24		BX FLAT LID 8inW w/CC 24" HOLE F/F		
P3) 24" - CASTING HEIGHT - 8" P2) 24" x 24" - BX FLAT LID 8inW w/CC 24" HOLE F/F - 8" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 20" 1) 24" x 24" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 18		0 lb 770 lb 2622 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 3392 lb	<u>Structure Notes:</u> ** KYTC STATE PROJECT ** 1. PER KYTC JB TYPE B / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE KY-510 FRAME & COVER "STORM" SUPPLIED BY OTHERS 5. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING 6. TOP SURFACE TO RECEIVE FLOATED FINISH	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 770 lb Volume (Net): 0.2cu.yd
