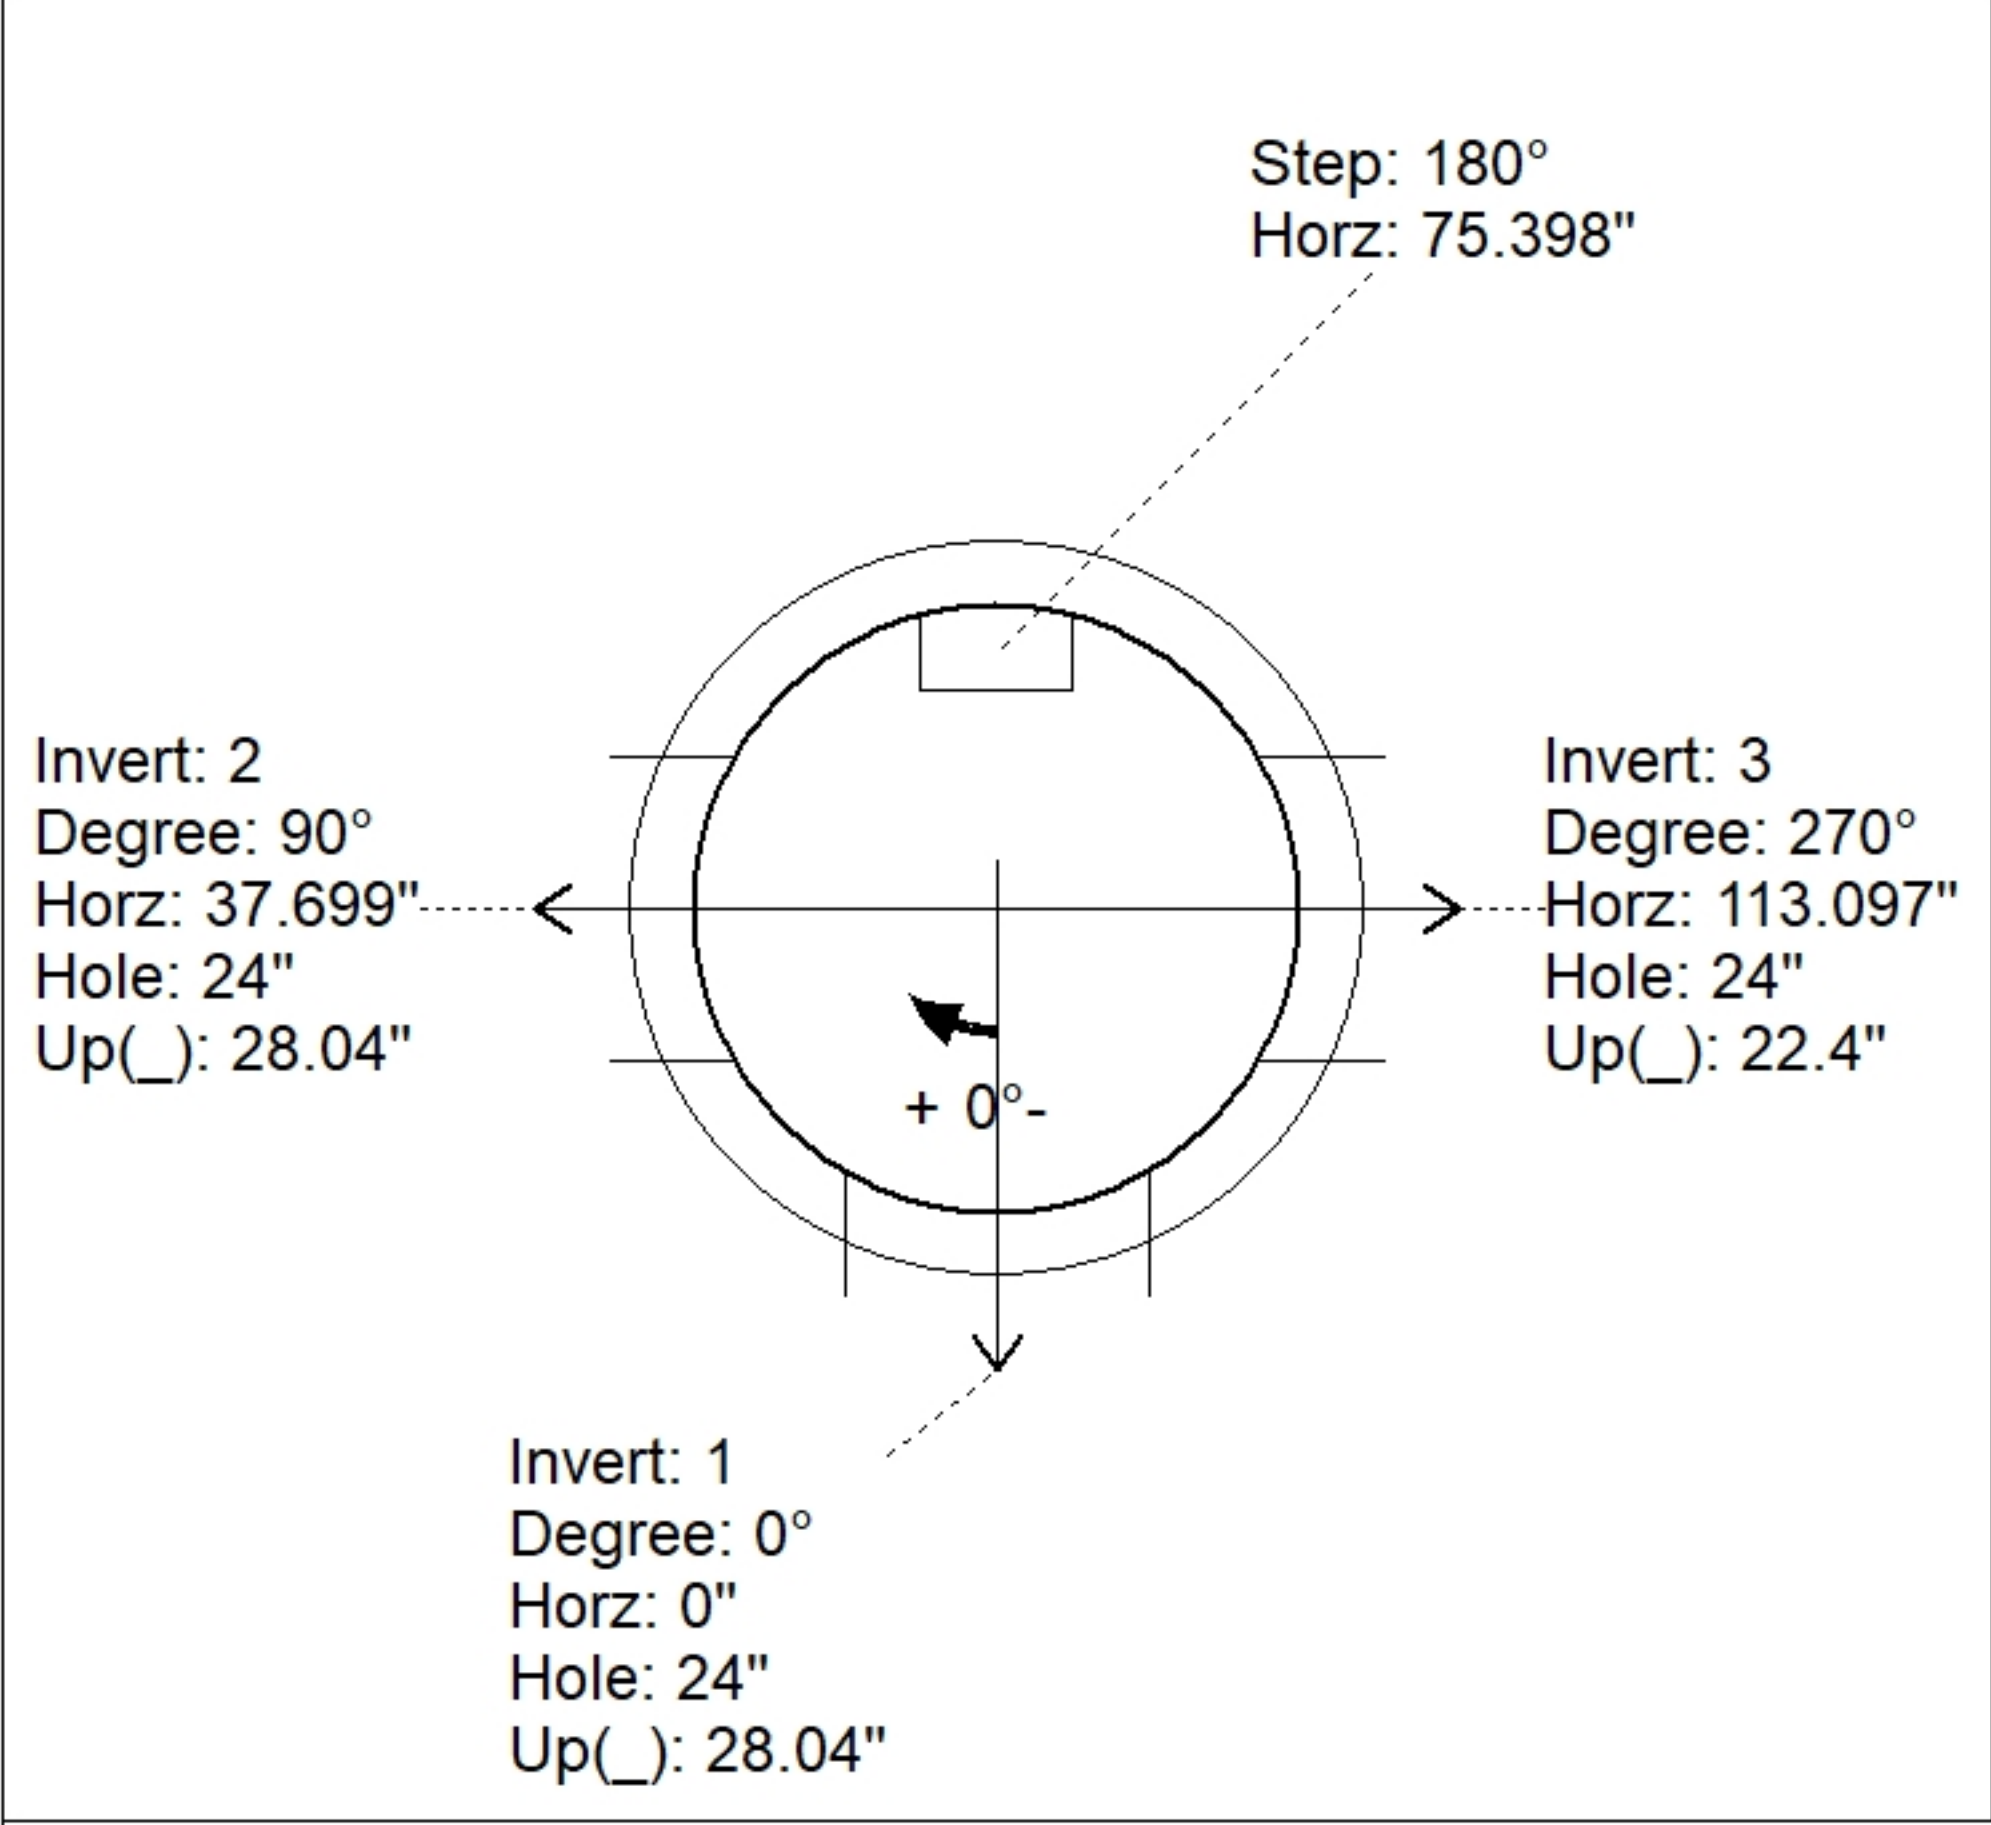
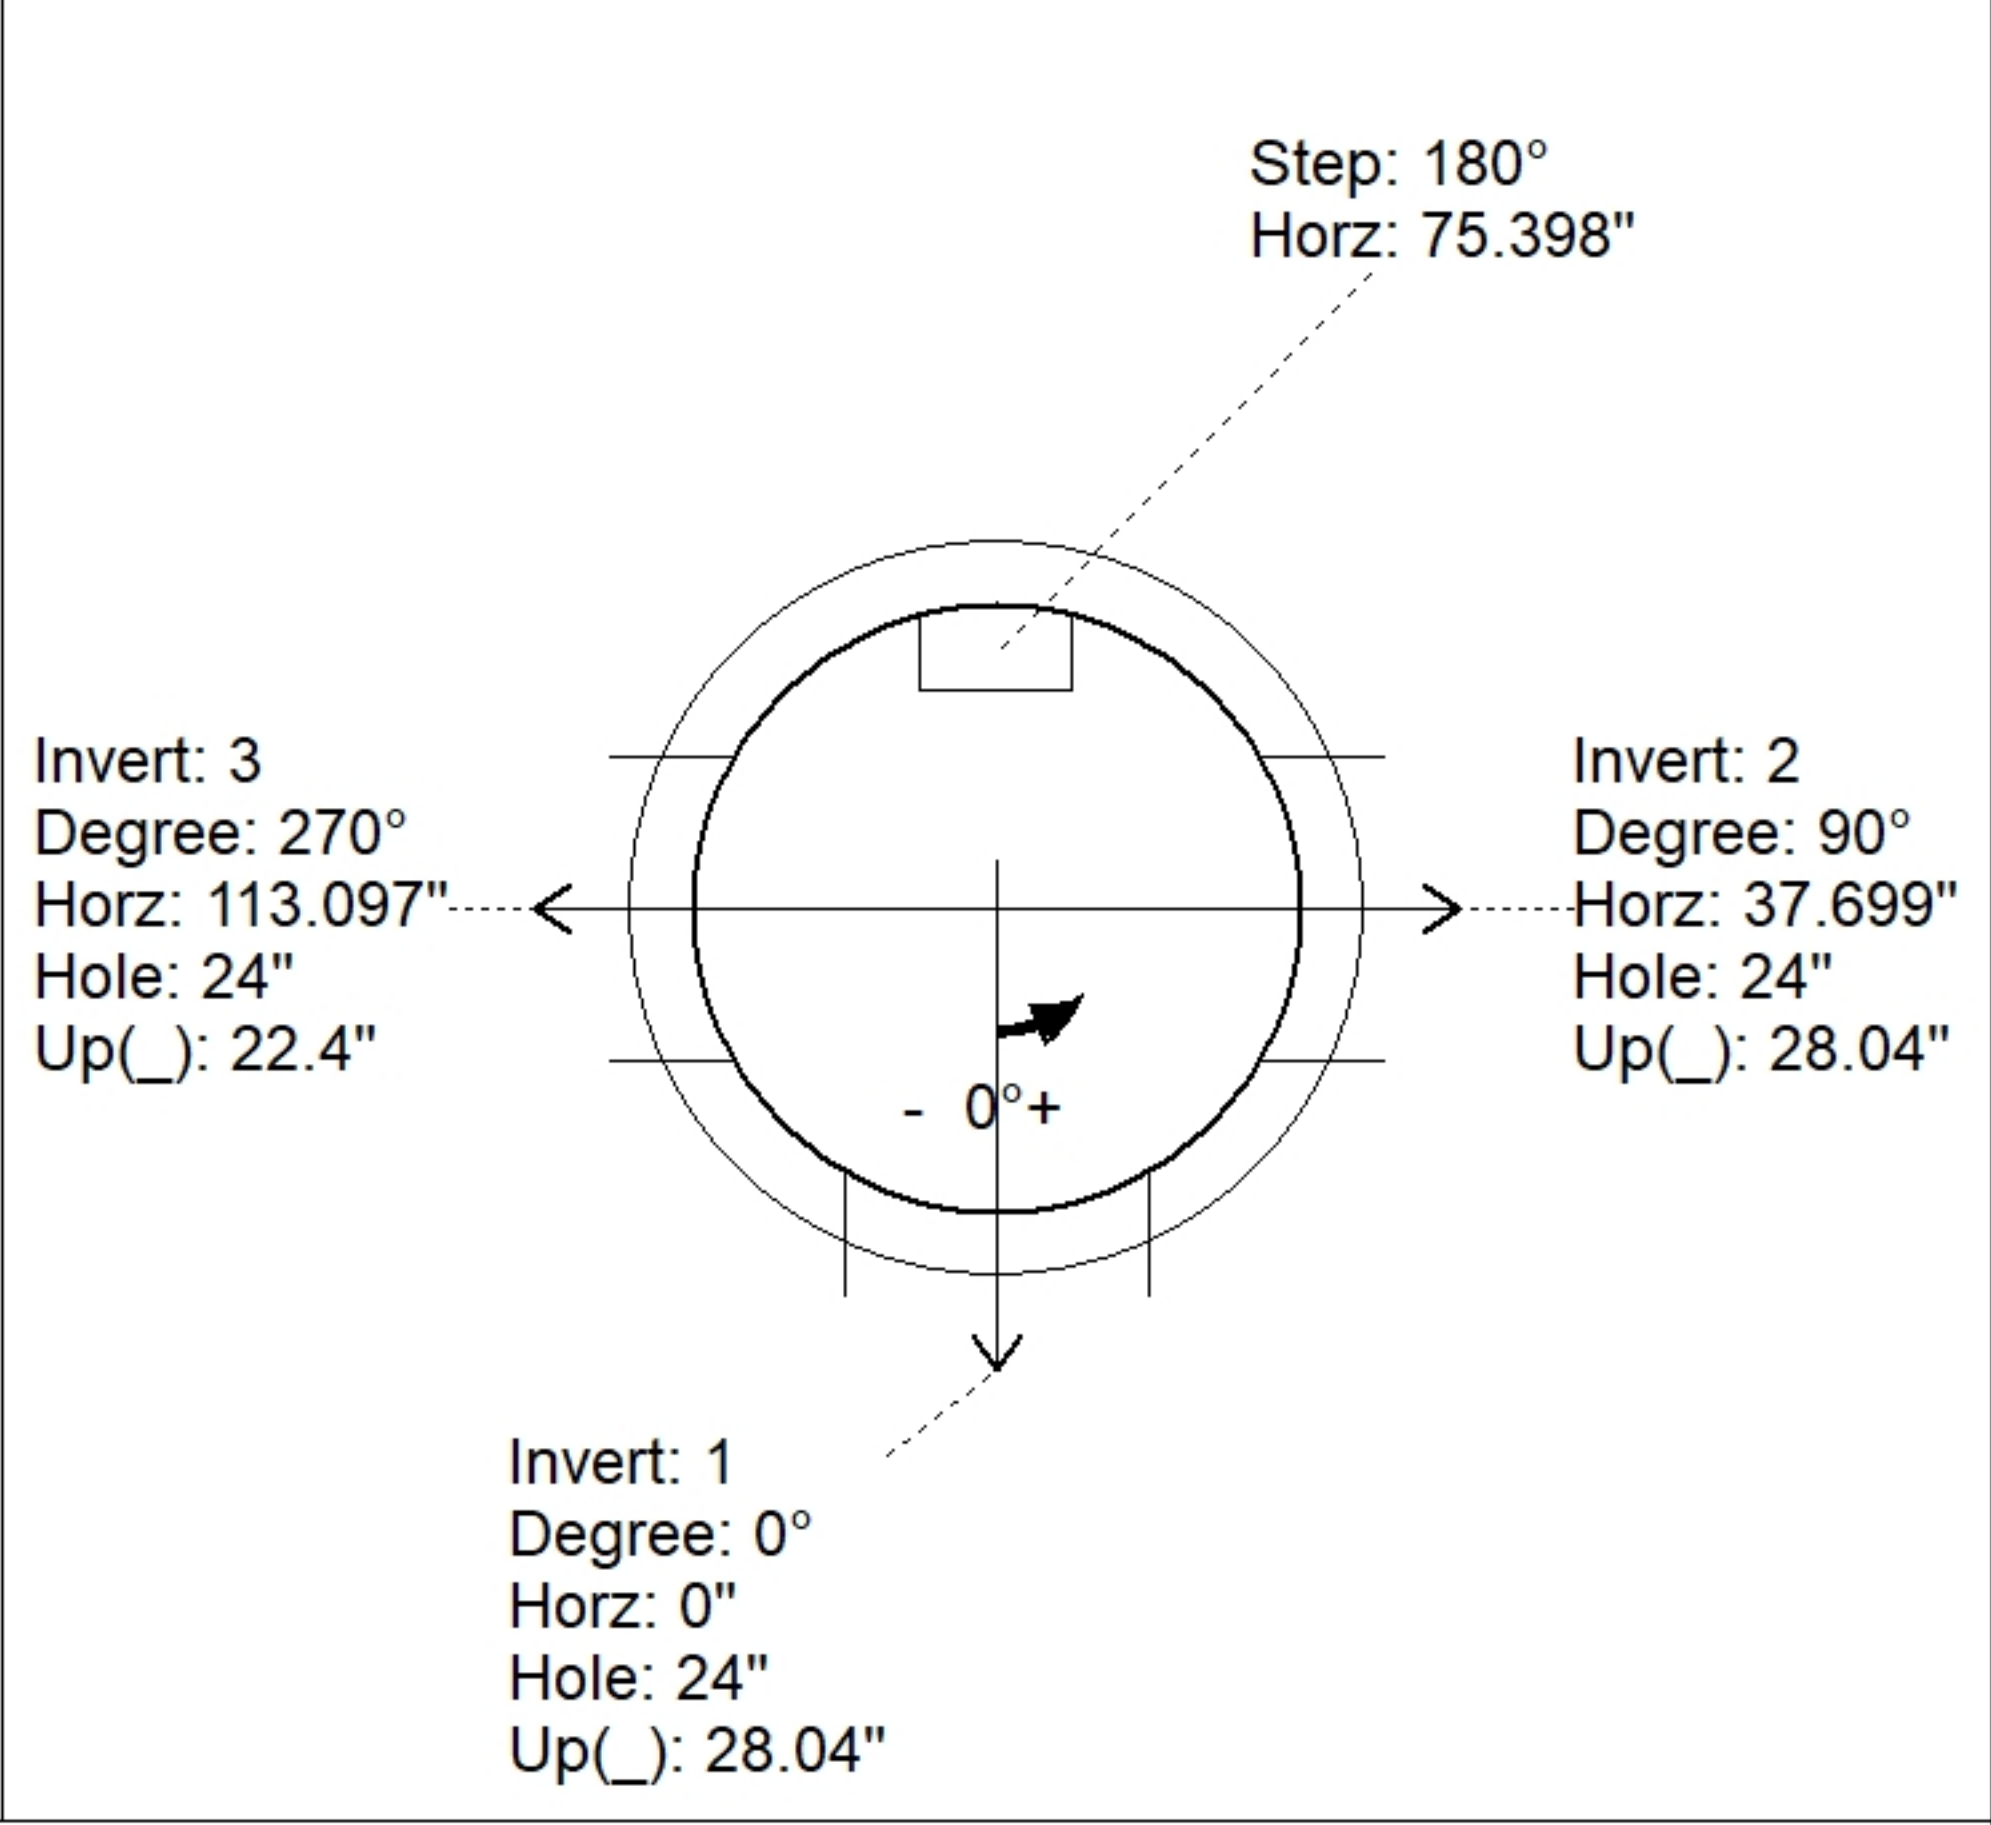
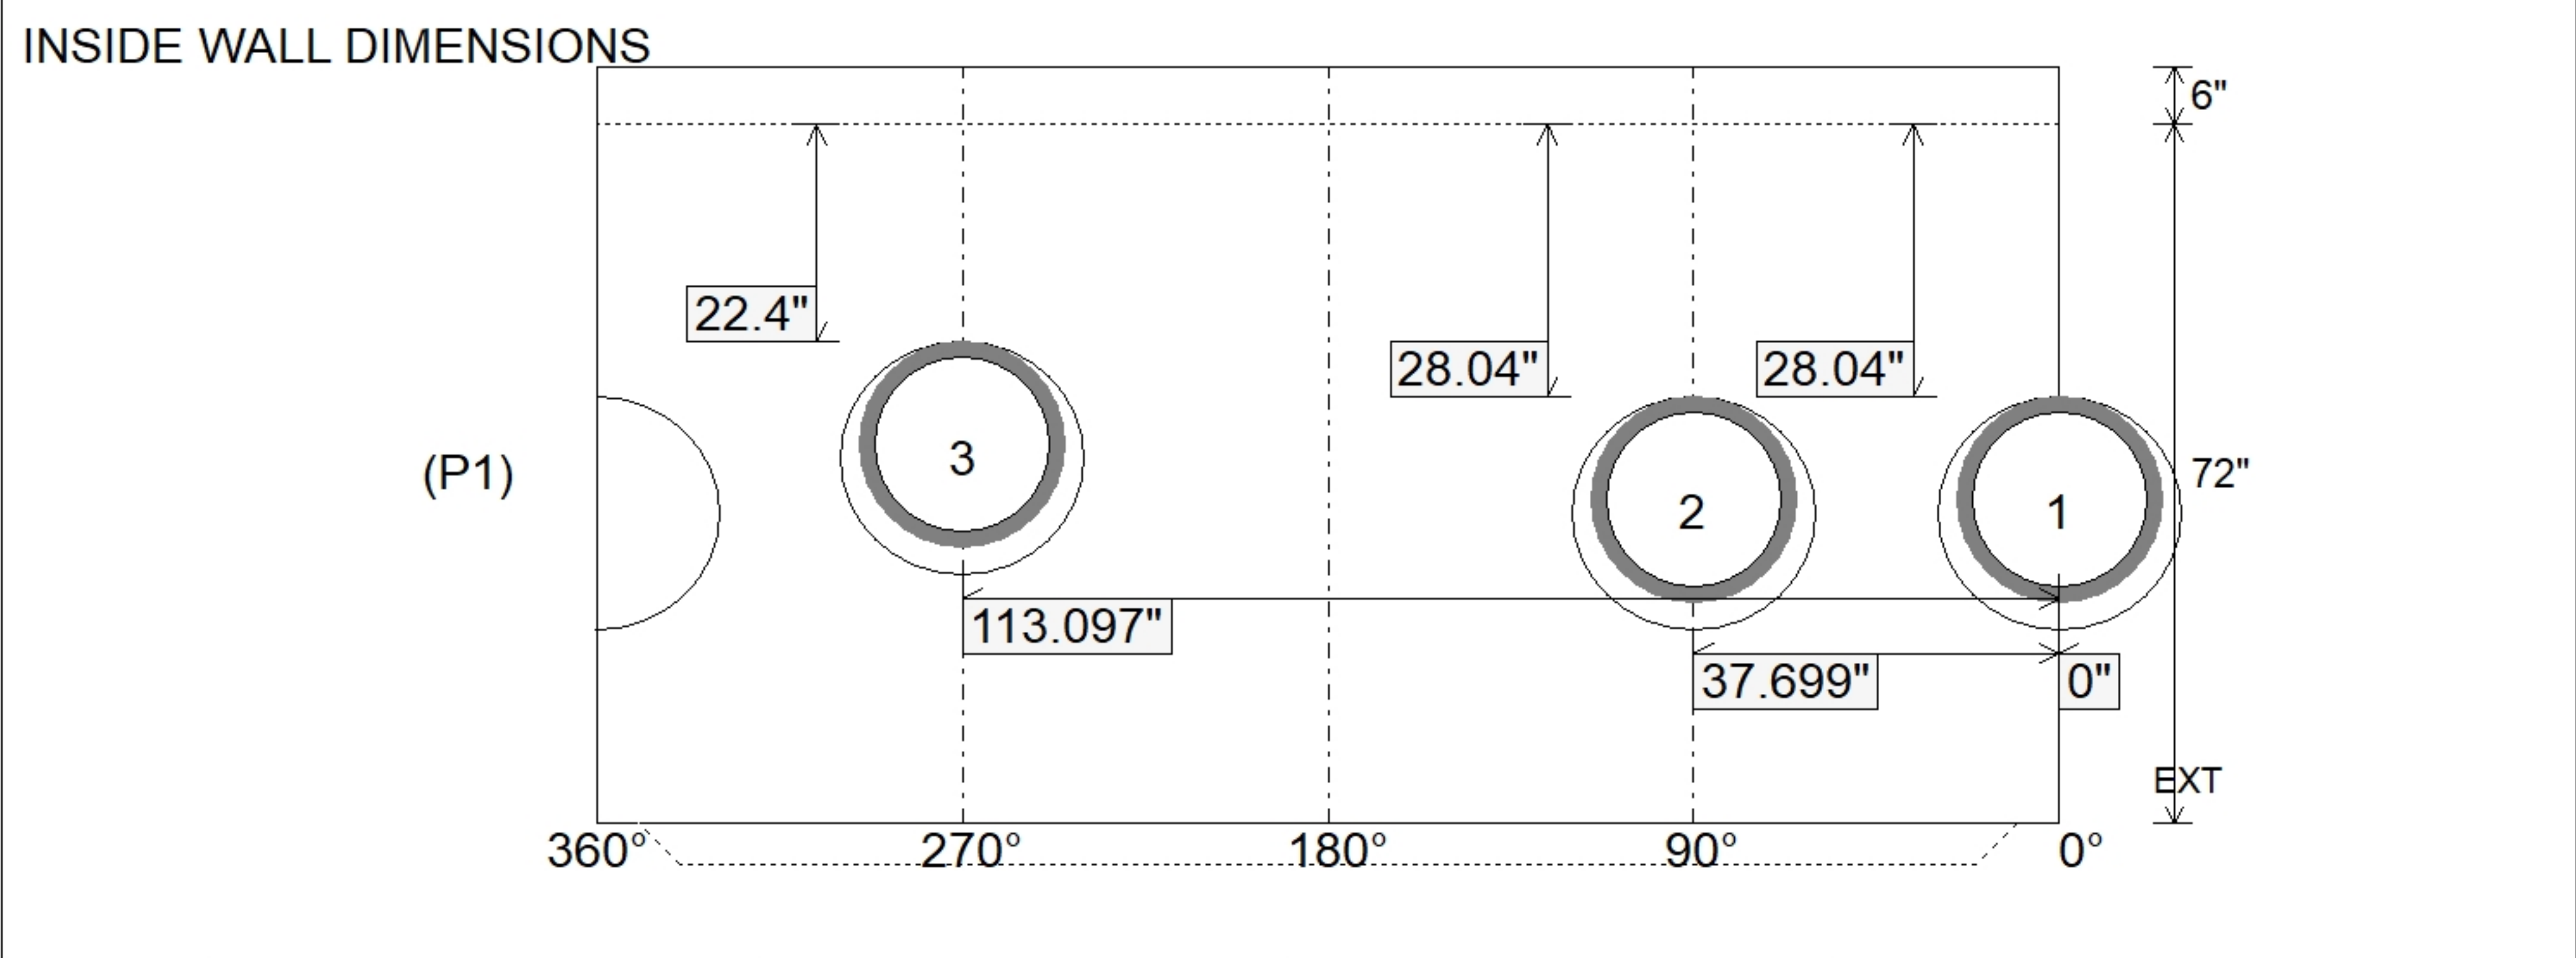


Job Name: 26-2484 Bass Pro Shops Outpost Paducah Job Location: Paducah, KY Contractor: Central Paving Co. of Paducah, Inc.					Plant: Beaver Dam 6/16/2026 8:00:45 AM		Tech: S. Felletter PC: A. Chambers				
Structure ID: Z2 ST-MH											
P1 MH048BA72			MH BASE T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 3" P2) 48" - ECC CONE w/ 24" HOLE F/G - 36" P1) 48" - MH BASE T/n - 72" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 3) Hole - 24 7) MH Step ML-10-TDS-NCR - 10"						0 lb 202 lb 3000 lb 5768 lb 271 lb 0 lb 0 lb 0 lb 0 lb ----- 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 368.9' Rim to Invert: 7.9' Slack: 0.8" Sump: 24" Step Position: 180°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	361.47'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	28.04"	0"	
Invert 2	361.47'	90°	45.553"	18" HDPE	21.2"	Hole 24	24"	25.133"	28.04"	0"	
Invert 3	361'	270°	136.659"	18" HDPE	21.2"	Hole 24	24"	25.133"	22.4"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 											
INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Tongue Seam Dn: n/a Wall Thickness: 5" Floor Height: 6" Height (Int): 72" Height (Ext): 78" Weight (Net): 5768 lb Volume (Net): 1.47cu.yd											
