

Job Name: 26-2509 - Airpark Expansion Industrial Subdivision Job Location: Owensboro, KY 42301 Contractor: Koberstein Contracting, Inc.					Plant: 100		Tech: Jared - F			
					7/20/2026 4:20:48 PM		PC: A. Chambers			
Structure ID: MH A-2 SS-MH										
P1 MH048BA24CDARED					MH BASE w/ConBlock-CDA Red T/n					
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-315 F/C RWRA 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 1) PSX - 16M NYLO 8) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 1961 lb 2515 lb 2703 lb 0 lb 0 lb 1440 lb 0 lb 258 lb 0 lb 0 lb 12 lb 8 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 395.5' Rim to Invert: 8.37' Slack: 1.44" Sump: 2" Structure Total: 2703 lb Step Position: 270'										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	387.13'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"
Invert 2	387.33'	90°	45.5"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	2.375"	0"
Invert 3	387.23'	180°	91.125"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.75"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2703 lb Volume (Net): 0.69cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-2509 - Airpark Expansion Industrial Subdivision Job Location: Owensboro, KY 42301 Contractor: Koberstein Contracting, Inc.					Plant: 100 7/20/2026 4:20:48 PM		Tech: Jared - F PC: A. Chambers				
Structure ID: MH A-2 SS-MH											
P1 MH048BA24CDARED			MH BASE w/ConBlock-CDA Red T/n								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 30" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 36" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) ADMIXTURE CONBLOCK CDA RED 1) CASTING - HOE MC-315 F/C RWRA 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-18L 1) PSX - 16M NYLO 8) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 1961 lb 2515 lb 2703 lb 0 lb 0 lb 1440 lb 0 lb 258 lb 0 lb 0 lb 12 lb 8 lb 0 lb ----- 9167 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY ICAST (HOE MC-315 F/C RWRA). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 395.5' Rim to Invert: 8.37' Slack: 1.44" Sump: 2" Structure Total: 9167 lb Step Position: 270'											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	387.13'	0°	0"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	0.5"	0"	
Invert 2	387.33'	90°	45.5"	12" PVC SDR35	12.5"	PSX 16M NYLO	16"	16.312"	2.375"	0"	
Invert 3	387.23'	180°	91.125"	15" PVC SDR35	15.3"	Kor-N-Seal2 S206-18L	18"	18.451"	1.75"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

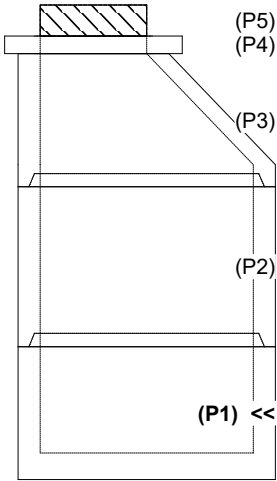

(P5)
(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

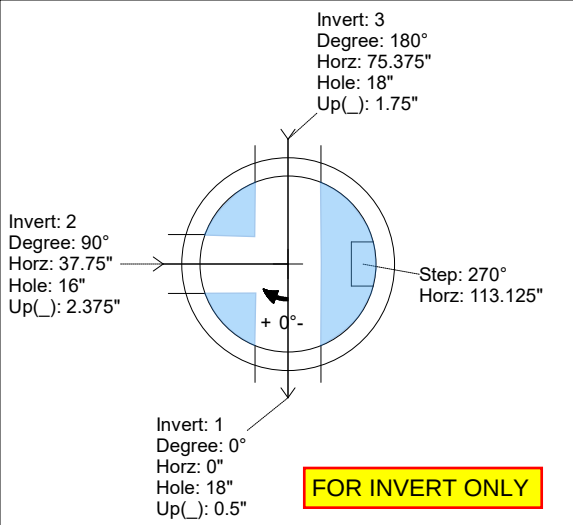

Invert: 3
Degree: 180°
Horz: 75.375"
Hole: 18"
Up(): 1.75"


Invert: 2
Degree: 90°
Horz: 37.75"
Hole: 16"
Up(): 2.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 18"
Up(): 0.5"

Step: 270°
Horz: 113.125"

FOR INVERT ONLY

UPSIDE-DOWN VIEW (int. dimensions)

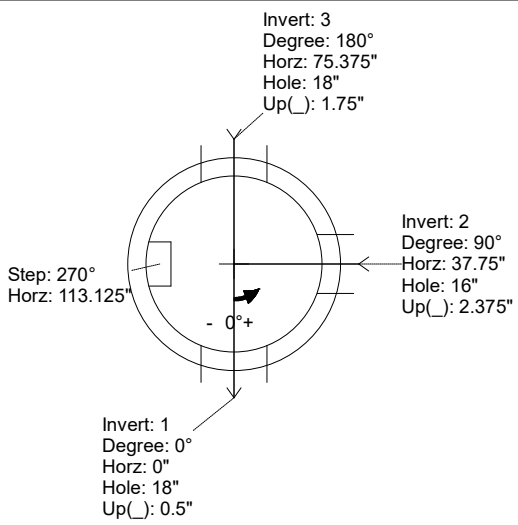


Invert: 3
Degree: 180°
Horz: 75.375"
Hole: 18"
Up(): 1.75"

Invert: 2
Degree: 90°
Horz: 37.75"
Hole: 16"
Up(): 2.375"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 18"
Up(): 0.5"

Step: 270°
Horz: 113.125"

INSIDE WALL DIMENSIONS



(P1)

Horizontal dimensions: 1.75", 2.375", 0.5"

Vertical dimensions: 6", 24"

Angles: 360°, 270°, 180°, 90°, 0°

Horizontal offsets: 75.375", 37.75", 0"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2703 lb Volume (Net): 0.69cu.yd
----------------------------------	---------------------------------	--	--	--
