




Job Name: 25-3452 - Churchill Downs Skye Terrace Improvements Job Location: Louisville, KY 40208 Contractor: Louisville Paving and Construction					Plant: 100 4/30/2026 1:21:40 PM		Tech: Jared - F PC: J. Jarvis				
Structure ID: S107											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 32" x 32" - CASTING HEIGHT - 3" P2) 48" - MH FLAT TOP w/32"x32" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 70" 1) CASTING - HOE 595 F/G 1) 48" - Conseal CS-102 1.00" 1) 32" x 32" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 22 1) Hole - 16					0 lb 1629 lb 5835 lb 376 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7840 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 595 F/G) REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 457.85' Rim to Invert: 7.09' Slack: 0.08" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	450.76'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	-1.25"	0"	
Invert 2	450.76'	97°	49.125"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	-2.25"	0"	
Invert 3	454.38'	277°	140.25"	12" HDPE	14.5"	Hole 16	16"	16.312"	42.25"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

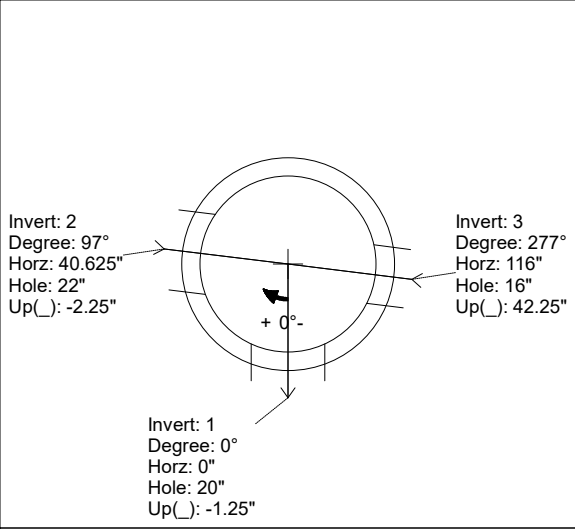


RIGHT-SIDE UP VIEW (int. dimensions)

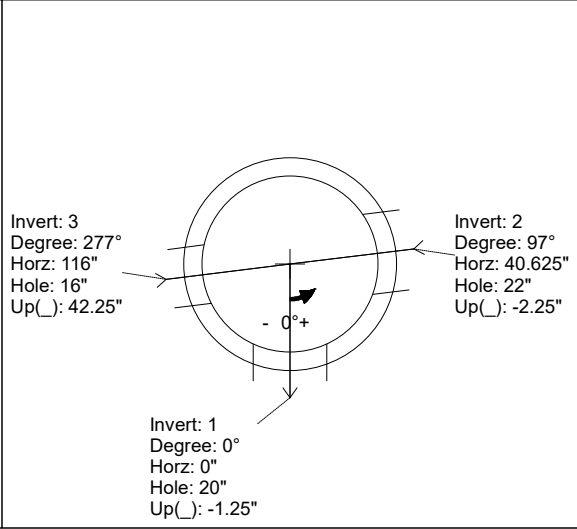

UPSIDE-DOWN VIEW (int. dimensions)

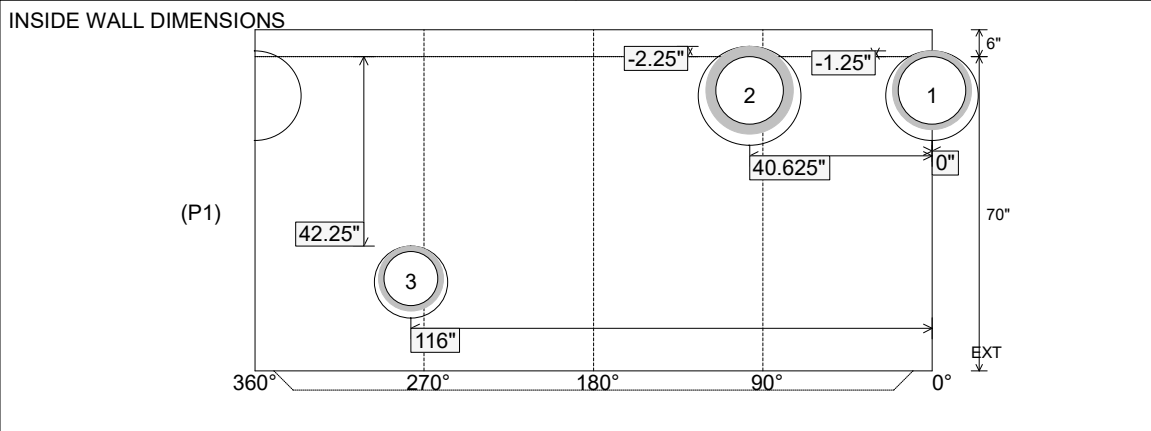

INSIDE WALL DIMENSIONS

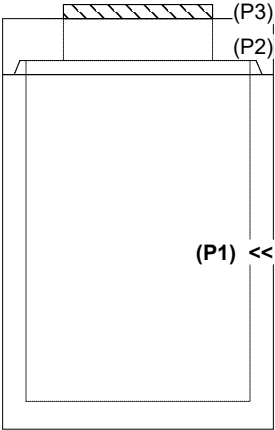

(P1) << (P2) (P3)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 70" Height (Ext): 76"	Weight (Net): 5835 lb Volume (Net): 1.49cu.yd
----------------------------------	---------------------------------	--	--	--
